























MIZRAHI

DESIGN / BUILD

APPENDIX A



Construction Progress Forecast

The One

	Sep/2019	Oct/2019	Nov/2019	Dec/2019	Jan/2020	Feb/2020	Mar/2020	Apr/2020	May/2020	Jun/2020	Jul/2020	Aug/2020	Sep/2020	Oct/2020	Nov/2020	Dec/2020	Jan/2021	Feb/2021	Mar/2021	Apr/2021	May/2021	Jun/2021	Jul/2021	Aug/2021	Sep/2021	Oct/2021	Nov/2021	Dec/2021
Baseline % Complete	39.50%	40.63%	42.19%	43.75%	45.31%	46.88%	48.44%	50.00%	51.56%	53.13%	54.69%	56.25%	57.81%	59.38%	60.94%	62.50%	64.06%	65.63%	67.19%	68.75%	70.31%	71.88%	73.44%	75.00%	76.56%	78.13%	79.69%	81.25%
AGP Restart % Projected													51.61%	52.40%	53.40%	54.30%	55.20%	56.60%	58.00%	59.40%	60.80%	62.20%	63.60%	65.00%	66.40%	67.80%	69.20%	70.60%
Actual % Complete (using Jan 2023 Schedule)	37.58%	38.62%	39.66%	40.70%	41.74%	42.78%	43.82%	44.86%	45.90%	46.94%	47.98%	49.02%	50.06%	51.10%	52.14%	53.19%	54.23%	55.27%	56.31%	57.35%	58.39%	59.43%	60.47%	61.51%	62.55%	63.59%	64.63%	65.67%
Actual Construction	17.98%	19.27%	20.95%	21.79%	22.57%	22.92%	23.36%	23.81%	24.02%	24.62%	25.23%	25.82%	26.57%	27.26%	28.03%	28.75%	29.52%	30.39%	31.34%	32.04%	33.04%	34.29%	35.30%	36.05%	36.91%	37.58%	38.57%	39.50%
Actual Procure/SDs	19.60%	19.35%	18.71%	18.91%	19.17%	19.86%	20.46%	21.05%	21.88%	22.32%	22.75%	23.20%	23.49%	23.84%	24.11%	24.44%	24.71%	24.88%	24.97%	25.31%	25.35%	25.14%	25.17%	25.46%	25.64%	26.01%	26.06%	26.17%

	Jan/2022	Feb/2022	Mar/2022	Apr/2022	May/2022	Jun/2022	Jul/2022	Aug/2022	Sep/2022	Oct/2022	Nov/2022	Dec/2022	Jan/2023	Feb/2023	Mar/2023	Apr/2023	May/2023	Jun/2023	Jul/2023	Aug/2023	Sep/2023	Oct/2023	Nov/2023	Dec/2023	Jan/2024	Feb/2024	Mar/2024	Apr/2024
Baseline % Complete	82.21%	84.38%	85.94%	87.50%	89.06%	90.63%	92.19%	93.75%	95.31%	96.88%	98.44%	100.00%																
AGP Restart % Projected	72.00%	73.00%	74.80%	76.20%	77.60%	79.00%	80.40%	81.80%	83.20%	84.60%	86.00%	87.40%	89.92%	92.44%	94.96%	97.48%	100.00%											
March 2025 Completion Schedule % Complete	57.83%	58.97%	59.99%	61.13%	62.23%	63.37%	64.47%	65.60%	66.74%	67.84%	68.98%	70.08%	71.21%	72.35%	73.38%	74.51%	75.61%	76.75%	77.85%	78.99%	80.12%	81.22%	82.36%	83.46%	84.60%	85.74%	86.80%	87.94%
Actual % Complete (using March 2025 Completion Schedule)	64.06%	65.01%	65.95%	66.90%	67.84%	68.79%	69.74%	70.68%	71.63%	72.57%	73.52%	74.46%	75.41%	76.36%	77.30%	78.25%	79.19%	80.14%	81.08%	82.03%	82.98%							
Actual Construction	40.86%	41.62%	42.25%	42.95%	43.83%	44.84%	46.38%	47.35%	48.40%	50.09%	51.30%	52.40%	54.10%	56.64%	58.48%	60.11%	63.09%	64.71%	67.47%	70.34%	72.01%							
Actual Procure/SDs	23.20%	23.39%	23.70%	23.95%	24.01%	23.95%	23.36%	23.33%	23.23%	22.48%	22.22%	22.06%	21.31%	19.72%	18.82%	18.14%	16.10%	15.43%	13.61%	11.69%	10.97%							

	May/2024	Jun/2024	Jul/2024	Aug/2024	Sep/2024	Oct/2024	Nov/2024	Dec/2024	Jan/2025	Feb/2025	Mar/2025																	
Baseline % Complete																												
AGP Restart % Projected																												
March 2025 Completion Schedule	89.04%	90.17%	91.27%	92.41%	93.55%	94.65%	95.78%	96.88%	98.02%	99.16%	100.00%																	
Actual % Complete (using March 2025 Completion Schedule)																												
Actual Construction																												
Actual Procure/SDs																												

NOTES:

Baseline % Complete	This row is the original projection for the baseline schedule
AGP Restart % Projected	This row is the revised projection based on the recovery schedule R60
Actual % Complete	This row is the actual % complete (based on the overall project schedule - includes procurement, shop drawings, etc.)
Actual Construction	This is the % of physical construction completed on site, based on billings to date
Actual Procure/SDs	This is the difference between the Actual % Complete and the Actual Construction % Complete to show what portion is procurement, shop drawings, etc.
March 2025 Completion Schedule % Complete	This row is the revised projection based on the update project schedule issued in March 2023
	Indicates actual numbers taken from previous reports and this months progress



MIZRAHI

DESIGN / BUILD

APPENDIX B

THE ONE
RETAIL AND RESIDENTIAL

ORGANIZATION CHART



DEVELOPER PROFILE



Sam Mizrahi

America, the private company, based in Toronto, Canada, is recognized for its unwavering commitment to quality no matter the size or scale of the project – from midrise to highrise condominium projects.

Mizrahi Developments aims to be the best, not just to offer a superlative urban living experience to the customer, but also to meet its own high standards for perfection and professional excellence. It is a matter of personal integrity with which Mizrahi Developments continues to develop its award-winning brand characterized by old-world craftsmanship, high attention to detail, innovation and a hands-on pursuit of excellence in all aspects of its business.

From the start, Mizrahi Developments has been structured to offer a difference. The only builder in Canada and one of only a few in the United States with international certifications such as the ISO 9001, a process management system based in Switzerland, the company is committed to excellence that is not simply promised, but guaranteed through continuous monitoring and auditing by a third party. The ISO 9001 certification requires rigorous scrutiny of business practices and schedules, putting an emphasis on customer satisfaction; on-time, on-budget delivery; and productive relationships with trades and suppliers. In addition to membership in building associations, Mizrahi Developments works to some of the world's highest environmental and sustainability certifications as part of its commitment to remain abreast of the latest improvements in construction and smart building technologies.

With its roots in luxury single-dwelling homes in Toronto's most valuable neighborhoods, Mizrahi Developments has earned a reputation for bringing vision, passion and excellence to the built environment, no matter what its

Mizrahi Developments is a proven leader in identifying mixed-use, commercial and residential opportunities and executing an inspired vision for them to the highest international standards with world-class architects and designers. With over 20 years of experience in real estate development and high-end building in North

use – commercial, retail or residential. The company is driven to surpass expectations by redefining what luxury can mean. The ability to custom-build to a finely-articulated vision, often with complex, artisanal and technological features, has allowed the company to become the trusted builder of high-end retail brand environments as well as landmark developments that have an important significance to the communities involved.

Mizrahi Developments' latest project will be the tallest building in Canada. This mix use, highrise at Toronto's iconic midtown intersection of Yonge and Bloor. Called THE ONE, the 85-storey condominium and retail tower is designed by Foster + Partners, one of the most innovative architectural firms in the world. With a jewel-box retail podium with flagship stores for leading global brands, a green civic space that invites pedestrian engagement and condominiums featuring innovative, glassed-in gardens, THE ONE is heralded as a bold and exciting vision for Toronto, as the city takes its place on the world stage.

The company has a strong presence in this leading luxury marketplace in Canada. Mizrahi Developments' condominium boutique buildings in Yorkville, Toronto's beloved, historic midtown neighborhood, were quickly recognized for a level of craftsmanship and attention to detail more commonly found in single luxury homes than in condominiums. With sound-proof, UV-protected windows, walls that were three times thicker than required by building codes, high, coffered ceilings and superior finishing details, the suites at 133 Hazelton and 181 Davenport have the established old-world presence and beauty of a stand-alone home. Both buildings, clad in pale limestone, were 100% sold before construction began. These two adjacent properties, which represent the last of their kind in this popular midtown neighborhood, underscored the company's skill in working within urban heritage quarters in close collaboration with engaged community groups and municipal authorities to bring about an outcome that enhances and complements the existing streetscape.

Mizrahi Developments is a partnership built on values of excellence, integrity and responsibility. Led by Sam Mizrahi, the company is committed to building on its strong reputation and luxury brand with a variety of highend, mixed-use projects around the world.

MIZRAHI QUALIFICATIONS



Mizrahi Developments specializes in creating a luxury experience in the built environment. The company is comprised of a group of passionate, hands-on individuals who have created a brand recognized for its superior craftsmanship,

innovation and attention to detail at all stages of a project's life cycle, establishing a valuable niche in the high-end design-build market.

For each project, Mizrahi Developments carefully selects a team of architects, designers and consultants to work together to bring about its successful completion on-time and on-budget. The company takes a proactive approach to project management, working on various aspects of development, such as zoning, design and marketing, concurrently in order to maximize efficiency and shorten time frames. It is part of the company's core philosophy to continually evaluate construction and development practices, which may be standard in the industry, but which it feels could be more efficient or improved upon in order to optimize the quality and delivery of the project.

Mizrahi Developments has earned a reputation over the past 20 years as a company that works in meaningful collaboration with communities, helping to bring about a vision for property development that benefits all stakeholders. Of particular note has been the company's experience in heritage neighborhoods, where local restrictions and resident concerns have presented challenges about new development. Mizrahi Developments prides itself on working closely with community and municipal stakeholders in a collaborative rather than adversarial fashion.

In the last five years, a growing momentum has seen the company execute several high-profile projects in Canada's leading luxury marketplace in Toronto. At Yonge and Bloor, the most important intersection in Toronto, THE ONE is a mixed-use, 80-storey tower designed by Foster +

Partners, one of the world's most innovative architectural firms. Celebrated as a visionary collaboration that clearly signals the city's emergence onto the global stage, THE ONE redefines the luxury experience with innovative architectural features and invigorates the civic experience with beautiful public spaces. The midtown neighborhood of Toronto has the highest condominium real estate value in Canada, and Mizrahi Developments has played a significant role in enhancing this popular urban location. The company's mixed-use, midrise projects in Yorkville, a highly-prized neighborhood with heritage buildings, were created to look as if they had always been there. With pale limestone exteriors, the adjacent buildings enhanced the streetscape with old-world charm, offering urban sanctuaries that were unparalleled for their attention to detail. The luxury residences in both buildings, all of which were custom-designed, achieved record-breaking sales in one of the most competitive real estate marketplaces in North America.

Part of the company's commitment to the communities in which it works is to put an emphasis on site cleanliness. High-quality maintenance of a building site while under construction is as important as the final outcome of the project, and Mizrahi Developments works diligently to ensure the least disruption in the high-density urban neighborhoods in which it works. High-design hoarding is installed for marketing purposes, cleanliness and also safety of local residents and business tenants. The sidewalks around the site are power-washed every week.

Above all other requirements, Mizrahi Developments puts an emphasis on health and safety. Twice a week – more than is required by industry regulations – we bring consultants to our building sites to do an audit of all health and safety issues. Our corporate structure dictates that this regular overview of the site is seen by all senior partners of Mizrahi Developments in order to ensure that any issues that arise are dealt with promptly. This approach also helps encourage optimal responsibility and diligence from sub-contracted trades on site.

MIZRAHI CERTIFICATIONS

GREENHOUSE CERTIFICATION



The GreenHouse certification demonstrates the commitment of Mizrahi Developments to delivering optimal health in the built environment and to working to superior environmental practices.

In GreenHouse certified spaces, high-quality ventilation and filtration systems act like a fine sieve, screening out bacteria, pollens and other irritants. Toxins are reduced in choices of finishes, including paints, tiles and carpeting. Stringent guidelines for energy efficiency are followed with heat ventilation recovery systems and appliances that conserve water.

Builders are required to adhere to environmentally-responsible construction practices. On site, recycling of waste materials helps reduce landfill. Careful planning and ordering – “measure twice, cut once” – guarantees efficient use of materials, practices which save money. A GreenHouse-certified building is a commitment to living in an optimal interior environment and to contributing to the health of the environment at large.

For more information, please visit www.greenhousecertified.ca

ENERGY STAR



The EnergyStar certification helps reduce greenhouse gas emissions generated from energy consumed in a building and creates greater cost-efficiency on energy costs.

With advanced construction techniques, an EnergyStar building is warmer in winter, cooler in summer, quieter and draft-free. High-efficiency furnaces and air-conditioning units, quality appliances and the latest lighting technology together contribute to a building that will produce two-to-three tonnes less greenhouse emissions per year.

For more information, please visit www.esnewhomes.ca

TARION



The Tarion Warranty is part of the Ontario New Home Warranty Program and was put into place by law, required for all builders of new homes in Ontario. Based on extensive research with consumers and ongoing consultations with the Ontario Home Builders

Association, Tarion protects homeowners from defects in work and materials for up to seven years and will intercede if builders fail to honor their warranty obligations. Mizrahi Developments is proud to participate in the Tarion Warranty as it gives homeowners insurance on the quality of workmanship and materials used.

For more information, please visit www.tarion.com

ISO9001



The ISO9001 certification, is a quality management system from a Swiss-based regulatory body that collects best practices from global representatives of various industries. Mizrahi Developments is the only builder in Canada and one of only a handful in the United States with this international certification.

Clients are asked to fill out a questionnaire on a weekly or monthly basis to assess the company's performance. Is the site clean? Are completion deadlines being met? Is the contract being fulfilled as promised? It guarantees trust. Customers have the assurance that rigorous accountability measures are in place and that as builders, Mizrahi Developments is committed to excellence by standardizing the best processes and methods. Everything is documented and set out in manuals, which are followed by every member of the Mizrahi Developments team.

TORONTO CONSTRUCTION ASSOCIATION



Membership in the Toronto Construction Association (TCA), which was founded in 1867, underscores Mizrahi Developments' commitment to the highest

possible standards of professional integrity and ethics in a hypercompetitive industry. The TCA has grown over the years to address many different aspects of the construction industry with the goal of promoting superior health and safety regulations; establishing recommended practices for fair and ethical contracting; and fostering a spirit of cooperation, among all parties in the business, that holds everyone involved to a high level of character, integrity and trust.

For more information, please visit www.tcaconnect.com

BILD




The Building Industry and Land Development Association (BILD) is a group of like-minded business professionals who engage in the construction industry with a similar code of ethics and who work together to discuss issues and facilitate communication between stakeholders, including all levels of government.

For more information, please visit www.bildgta.ca

AWARDS

Mizrahi Developments is proud to have been nominated and to have won several BILD awards including BILD Pinnacle Award - Project of the Year and nominated for Mid/High rise - Tarion Ernest Assaly award for suite design and marketing.

PROJECT ORGANIZATION CHART

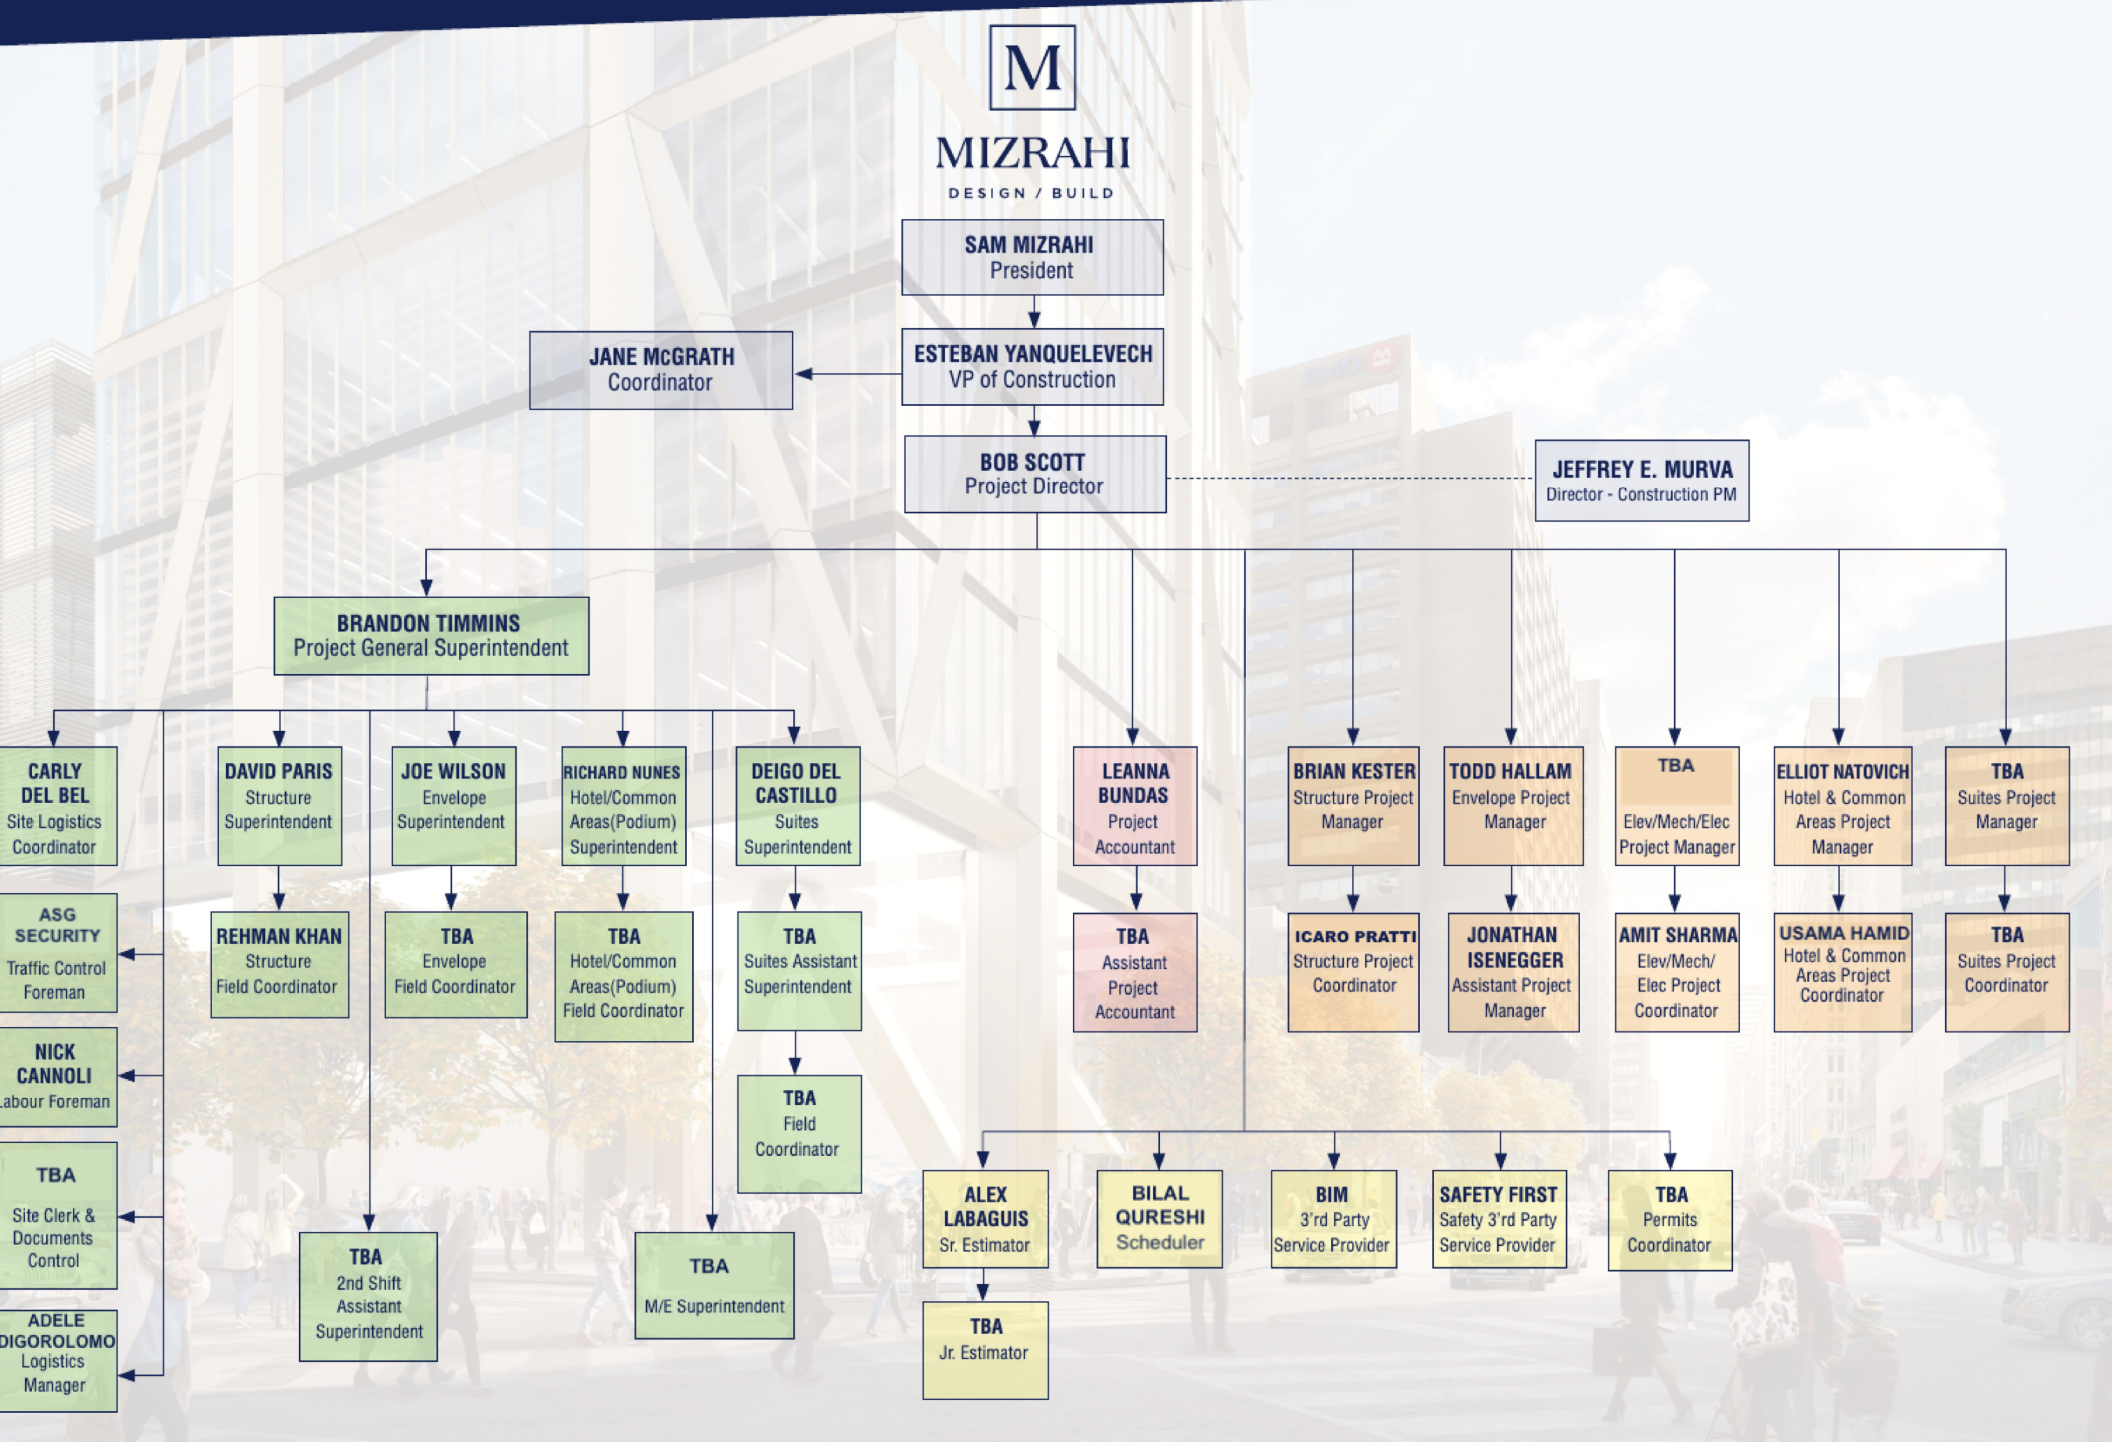

26 YEARS EXPERIENCE IN CONSTRUCTION FINISHING HIGH END LUXURY BUILDINGS

TECHNICAL ARCHITECT AND PROJECT MANAGER

Vast experience in design and managing construction of high-end projects in Toronto, Canada and abroad. Demonstrated and proven professional ability to direct projects from concept to delivery stage, from residential houses to high end condominiums. Effective and efficient capabilities to complete work on time, on budget and always with an added value to both, the developer and the client. Great ability to negotiate and act as a leader to ensure a good team work within the respective trades and consultants.

CORE COMPETENCIES

Project Design / Management Expertise • Team Leadership

On-time / On- Budget • Cost Tracking

Residential and High end Condominiums

Extensive knowledge of coordination and analysis of architectural, electrical, mechanical, structural, landscape, interior design and shop drawings.

Excellent Quality Control from Concept to Occupancy

Great relationship with different teams and purchasers

PROJECT ACCOMPLISHMENTS

Mizrahi Developments – 2015 - Present

129 Hazelton Avenue - A new high end 3-storey Home.

Responsibilities included:

- Guiding the existing Project Manager with the completion of the house, with the quality and standards of a Mizrahi home.
- Overlooking and coordinating layouts, design and working drawings.
- Ensuring that all agreements of purchaser of sales are coordinated with working drawings and specs.
- Overlooking quality and ensuring that the construction team finalizes all deficiencies.
- Reviewing all existing contracts to ensure the right scope of work is in place.
- Reviewing all Invoices.

133 Hazelton Avenue A new high end 9-storey condominium residence.

Responsibilities as a Senior Project Manager included:

- Taking over the project and taking it to final occupancy.
- Overlooking and coordinating layouts, design, and working drawings.
- Ensuring that all agreements of purchaser of sale are coordinated with working drawings and specs.
- Overlooking quality and ensuring that the construction team finalizes all deficiencies.
- Reviewing all existing contracts to make sure the right scope of work was in place.
- Reviewing all Invoices.
- Negotiating all outstanding extras with trades.

181 Davenport Road A new high end 12-storey condominium residence.

Responsibilities as a Vice President included:

- Taking over the project and taking it to partial Occupancy and Registration.
- Overlooking and coordinating layouts, design and working drawings.
- Ensuring that all agreements of purchaser of sale are coordinated with working drawings and specs.
- Overlooking quality and ensuring that the construction team finalizes all deficiencies.
- Reviewing all existing contracts to ensure the right scope of work was in place.
- Reviewing all Invoices.
- Negotiating all outstanding extras with trades.
- Preparing Outstanding scope of work and contracts with trades.
- Conducting a walk through with all city Inspectors.
- Coordinating occupancy and registration with all trades.
- Supervising and overlooking the entire construction team and sight.

128 Hazelton Avenue A new high end 9-storey condominium residence.

Responsibilities as a Vice President included:

- Working along side the Vice President of Developments to get the project to the construction stage.
 - Overlooking and coordinating layouts, design and working drawings.
 - Ensuring that all agreements of purchaser of sale are coordinated with working drawings and specs.
 - Overlooking quality to ensure construction team finalizes all Deficiencies.
- Preparing all scope of works and contracts for the project.

Elad Canada – 2012 to 2014

Parkway Forest Reurbanization – A master plan community including multiple Rental Buildings and a Community Centre.

Assistant Project Manager, in charge of finalizing a rental building (130 Parkway Forest), Community Center for the City of Toronto , Demolition of 114 Townhouses , new rental Building (106 Parkway Forest) and a new road to connect Forest Manor and Don Mills.

Responsibilities included:

- Preparing, with construction team, scope of resources, milestones, schedules and budget.
- Job site startup, together with site supervisor in setting up the site trailers, hording and gates.
- Coordinate with planer and ensure all permits are ready and on time to start construction.
- Ensuring all working drawings are coordinated within consultants.
- Serving as a consultant to trades, and coworkers to ensure all deadlines, schedules, budgets, and finishes were reached efficiently and on time
- Monitoring and reviewing project budget at periodic reviews ensuring the project is proceeding on track.
- Identifying manages and resolves project issues.

- Organizing and conduct regular meetings with construction team and other coworkers to share information.
- Organizing and conduct regular meetings with trades and consultants to ensure all issues are brought forward and that all details are addressed.
- Ensuring municipal job site inspections are being completed during construction phase.
- Walking through site inspections to ensure steady progress.
- Preparing and disseminate information to all necessary parties.
- Monitoring and reviewing project budget and extras to ensure the project is proceeding on track.
- Managing all changes and ensures all necessary information is shared within trades and consultants.
- Supervising and ensure that the building exceeds quality levels.
- Ensuring requirements of full occupancy are submitted and accepted by the municipality and consultants.
- Developing together with customer service schedule for pre-PDI, PDI and occupancy dates.
- Managing the turn over to property management and ensure they received as built drawings, operating manuals, warranties and operating schedules.
- Reviewing with the property management department the completion of building deficiencies to conform with the technical audit.
- Overseeing the completion of all PDI deficiencies.

Elad Canada New Head Office

Responsibilities included:

- Assisting Project Manager assigned to the project.
- Overlooking Initial layouts, design and working drawings coordination.
- Overlooking quality and ensure that construction team finalizes all deficiencies.

Mall Renovation in Whitby – New store for Bad Boy, new hallway for mall and renovation for Urban Planet

Responsibilities included:

- Being In charge of design concept and working drawings.
- Overseeing budget, schedules, with all trades and consultants
- Negotiating to ensure savings for the developer.
- Conducting Quality control of the entire project in the Interest of developer and Tenants.
- Ensuring all working drawings are coordinated within consultants and all requirements are coordinated with working drawings and specifications.
- Identifying, managing, and resolving project issues.
- Organizing and conducting regular meetings with construction team and other coworkers to share information.
- Ensuring municipal job site inspections are being completed during construction phase.
- Walking through site inspections to ensure steady progress.
- Preparing and disseminate information to all necessary parties.
- Monitoring and reviewing project budget and extras to ensure the project is proceeding on track.
- Managing all changes and ensures all necessary information is shared within trades and consultants.
- Supervising and ensure that the building exceeds quality levels.

- Ensuring requirements of full occupancy are submitted and accepted by the municipality and consultants.
- Managing the turn over to property management.
- Overseeing the completion of all PDI deficiencies.

Camrost Felcorp- 2006 to 2012

The Avenue - Distinctively Forest Hill – A distinguished new high end 19-storey condominium residence. As project manager, in charge of full development of the project ensuring a functional project team with excellent communication between all managers, trades, consultants and purchasers.

Responsibilities included:

- Preparing with construction team, scope of resources, milestone, schedules and budget.
- Job site startup, together with site supervisor in setting up the site trailers, crane location, hoist, hording and gates.
- Preparing with marketing hording location, design and information to be put in.
- Coordinate with planer and ensure all permits are ready and on time to start construction.
- Ensuring all working drawings are coordinated within consultants and all agreements of purchaser of sale are coordinated with working drawings and specifications.
- Serving as a consultant to trades, purchasers, and coworkers to ensure all deadlines, schedules, budgets, and finishes were reached efficiently and on time
- Conducting management safety inspections.
- Monitoring and reviewing project budget at periodic reviews ensuring the project is proceeding on track.
- Reviewing and approval of all shop drawings and distribution to consultants and municipalities for approval.
- Maintaining shop drawings log.
- Identifying manages and resolves project issues.
- Organizing and conduct regular meetings with construction team and other coworkers to share information.
- Organizing and conduct regular meetings with trades and consultants to ensure all issues are brought forward and that all details are addressed.
- Ensuring municipal job site inspections are being completed during construction phase.
- Walking through site inspections to ensure steady progress.
- Preparing and disseminate information to all necessary parties.
- Monitoring and reviewing project budget and extras to ensure the project is proceeding on track.
- Managing all changes and ensures all necessary information is shared within trades and consultants.
- Supervising and ensure that the building exceeds quality levels.
- Ensuring requirements of full occupancy are submitted and accepted by the municipality and consultants.
- Developing together with customer service schedule for pre-PDI, PDI and occupancy dates.
- Managing the turn over to property management and ensure they received as built drawings, operating manuals, warranties and operating schedules.
- Reviewing with the property management department the completion of building deficiencies to conform with the technical audit.
- Overseeing the completion of all PDI deficiencies.

Imperial Plaza – Distinctively Forest Hill (Imperial Oil Building) – Historical Conversion of one of the most important buildings in Toronto in to a 23 storey Condominium residence.

Responsibilities included:

- Being In charge of design concept and working drawings.
- Overseeing budget, schedules, all trades and consultants
- Negotiating to ensure savings for the developer.
- Conducting Quality control of the entire project in the Interest of developer and purchasers
- Ensuring all working drawings are coordinated within consultants and all agreements of purchaser of sale are coordinated with working drawings and specifications.
- Identifying manages and resolves project issues.
- Organizing and conducting regular meetings with construction team and other coworkers to share information.
- Organizing and conduct regular meetings with trades and consultants to ensure all issues are brought forward and that all details are addressed

Private Cottage and Boat House – Muskoka - A 7500 sq.ft. Home in the Muskoka region outside Toronto. Responsibilities as a Project Manager involved from initial design to completion. Interfacing with Construction Manager.

I loft at Mystic Point - A high- rise condominium in Etobicoke, Toronto. As a Project Manager

Responsibilities included:

- Assisting Project Manager Assign to the project.
- Overlooking Initial layouts, design and working drawings coordination.
- Ensuring that all agreements of purchaser of sale are coordinated with working drawings and specs.
- Overlooking quality and ensure that construction team finalizes all deficiencies.

Red Hot Condos – A low - rise condominium in Toronto. As a Project Manager

Responsibilities included:

- Assisting Project Manager Assign to the project.
- Overlooking Initial layouts, design and working drawings coordination.
- Ensuring that all agreements of purchaser of sale are coordinated with working drawings and specs.
- Overlooking quality and ensure that construction team finalizes all deficiencies.

California Condos – A high- rise condominium in Etobicoke, Toronto. As a Project Manager

Responsibilities Included:

- Assisting Project Manager Assign to the project.
- Overlooking Initial layouts, design and working drawings coordination.
- Ensuring that all agreements of purchaser of sale are coordinated with working drawings and specs.
- Overlooking quality and ensure that construction team finalizes all deficiencies.

Private Residence in Palm Beach (Florida) – A 2 Bedrooms + Den Condominium - As Project Manager**Responsibilities included:**

- Developing Initial design.
- Discussing Selection of materials and finishes
- Preparing schedule for construction team
- Coordinating all drawings, schedules with Construction Company.

Private Residence in Ontario- 2010 to 2014**As a Technical Architect, Interior Design and Project Manager.**

- Renovation of Bungalow in Toronto (Bloor and Islington).
- Renovation of 2 storey House in Toronto (Prince Edwards and Bloor).
- Interior Finishes 2 storey House in Toronto (Prince Edwards and Bloor).
- Renovation of 2 storey House in Toronto (Royal York and The Queensway).
- Renovation of 2 storey House in Toronto (St. Clair Avenue East and Kingston Rd).
- Renovation of 3 Bedrooms Bungalow in Toronto (Royal York and theQueensway)
- Basement Renovation of 2 storey House in Toronto (Bloor and Jane).
- Interior Finishes of 2 storey House in Toronto (Prince Edwards and Bloor).
- Renovation of 2 storey House in Toronto (Dundas and Royal York).
- Renovation of 3 Bedrooms Bungalow in Mississauga (QEW and Hurontario St)
- Interior Finishes in 3 storey House in Toronto (Finch and Bathurst)
- Interior Renovation of a Heritage 3 storey House (Avenue Road and Davenport)
- Interior Renovation of Suite at 133 Hazelton Avenue
- Renovation of a Bungalow (Bathurst and Wilson)
- Interior Renovation of Suite at 255 Richmond Street
- Interior finishes of Suite at Imperial Plaza (St. Clair Avenue west and Avenue road)

Responsibilities included:

- Designing Development: create architectural and interior design drawings.
- Presenting: schedules, details, selection of finishes.
- Coordinating: coordinate drawings and specifications with construction team and consultants.
- Conducting Site inspections to ensure all work are done according to working drawings and specifications and satisfaction of clients.

Private Residences in Buenos Aires, Argentina- 2000 to 2006**As a Technical Architect, Interior Design, Project Manager and Developer.**

- One Two storey 3230 Sq.Ft. Private Residence
- Remodeling and interior design of residential apartments and lobbies
- Maintainace and quality control of 40 residential buldings
- Two, two storey 4850 Sq.Ft. private residence.
- One, two storey 13.000 Sq.Ft. Clothing factory.

Responsibilities included:

- Purchasing of the land.
- Developing preliminary site plan, architectural drawings to achieve an ideal building and design.

- Leading a review of the project's scope of work, schedules and budget.
- Supervising construction.
- Creating marketing material
- Supervising finishes and quality control
- Supervising the turn – over to purchasers.

PROFESSIONAL EXPERIENCE

- 26 years of field experience – including project management, architectural design and interior design
- Revision and study of land before purchase; a complete statistical and thorough evaluation of land to determine re sale and building benefits.
- Working side by side with consultants to determine the final design of the building.
- Co-ordination between consulting drawings and final plans.
- Revision of contracts and scope of work.
- Meeting with purchasers in the early stages to ensure customer satisfaction and discuss any upgrades and individual design needs.
- Meeting with purchasers, which include redesign of certain suite elements, including finishes.
- Incorporating all of the purchaser's changes into working drawings and specifications. Control on site to ensure that current drawings are at par with purchasers changes and that these changes are being brought forth correctly and accurately.
- Ensure that construction on site is following consulting drawings and resolve any discrepancies and trouble shooting any concerns and doubts that may arise.
- Pre-p.d.i inspections to ensure suites are ready for purchaser inspection. Follow up with P.D.I deficiencies and ensure these errors are corrected.

EDUCATION

- Degree in – Technical Architect. O.R.T. - Buenos Aires, Argentina.
- Certificate in Autocad. - CTEC - Buenos Aires, Argentina.
- Certificate in 3D Studio. - University of Buenos Aires, Argentina.
- Certificate in Sanitary installations. O.R.T. – Buenos Aires, Argentina.
- Certificate in Landscape Photography - University of Buenos Aires, Argentina.

SKILLS AND COMPUTER KNOWLEDGE:

- Excellent ability to read drawings, find errors and create solutions
- Excellent ability to read construction documents
- Very strong personable skills – dealing with purchasers, trades, consultants and co-workers
- Excellent command on site – dealing with trouble shooting
- AutoCAD.
- 3d Studio.
- Adobe Illustrator.
- Photoshop.
- Corel draw.
- Microsoft Word, Excel and PowerPoint.

LANGUAGES

- Spanish: read, written, spoken.
- English: read, written, spoken.

BACKGROUND

Bob has worked in the construction industry for over 46 years. He assumes responsibility for all construction operations, manpower, schedule and costs of the project and ensures a safe and timely completion to all phases of any project that he is assigned. Throughout his career, Bob has been accountable for many delivery teams on a majority of prestigious projects in the Greater Toronto Area. His experience provides for an unparalleled capability and market knowledge and has well established relationships with all key subcontractors and consultants throughout Canada. Bob very much believes and practices “say what you do....do what you say”. He has always been conscious of carrying out his given mandate with great emphasis on safety, schedule and budget, and just as importantly, with the absolute minimum disruption to the public and surrounding neighbourhoods.

SELECTIVE PROJECT EXPERIENCE

Hotel “X” Toronto, ON
The Trump
International Hotel
and Residences
Toronto, ON
Bay Adelaide Centre
Office Tower
Toronto, ON
The Bow Office Tower
Calgary, AB
Lester B. Pearson
International Airport
Terminals 1 & 3
Elgin & Winter
Garden Theatre
Toronto, ON
Petronas Towers K.L
Malaysia

CORE COMPETENCIES

Relevant Experience to the Project

Highlighted are previously executed projects that were under Bob’s responsibility. These can be considered comparable and all have had similar complex issues alike to the “One Bloor Project” being constructed in a downtown restricted access location.

Hotel “X” Toronto, Ontario

A Resort Hotel located on the Toronto Waterfront Project Value at \$325M Completed 2018 Client - Library Group Critical Elements – reset the project when client dismissed general contractor.

Trump International Hotel and Residences, Toronto, Ontario

Luxury Condo / Hotel Project Location in the Financial District downtown Toronto Project valued at \$300M Completion 2014 Client – V Leviton Critical Elements - located at a major intersection, reset the project when client dismissed the general contractor.

Bay Adelaide Centre Office Towers, Toronto, Ontario

Location in the Financial District downtown Toronto Project valued at \$600M Completed 1st Tower 2007; 2nd Tower 2015 Client – Brookfield Office Properties Critical Elements - the underground PATH and parking garage were accessible to the public during all construction phases.

“The Bow” Office Tower, Calgary, Alberta

Located in the centre of Calgary’s critical downtown transportation network Project value at \$1.6B Completed 2011 Client – H & R Developments Critical Elements - built in a dense area of office towers and major intersections. Restart of the project once it was out of the ground.

Lester B. Pearson International Airport – Terminal 1

Located outside of downtown Toronto at the hub of Highway 401 & 427 Project valued at \$3B Completed 2005 Client – Greater Toronto Airport Authority (GTAA) Critical Elements – required functioning within an operating terminal environment and accommodating all ground transportation links in and out of the terminal while managing up to 2500 construction workers on site.

SUMMARY

Accomplished energetic engineer with 32 years experience in managing the development, design and construction of award winning commercial, institutional, and residential high-rise building projects. An energetic successful leader with experience in managing project delivery teams in the delivery of large and small projects and programs across North America. A focused principal in developing and implementing corporate strategic plans with a history of numerous successes. A balanced mentor and problem solver with experience in managing site development, design management, fast-track projects, estimating, and contract administration. Established a reputation as a dynamic charismatic leader with a track record of turning around team performance, morale, culture, and setting best in class practices and processes. Also known as being outstanding in working with challenging project conditions, successfully leading the completion of complex projects, concurrently leading large teams on multiple projects, while exceeding, at times doubling, target profits.

Value of Projects Managed: \$ 5,251 Million over 16,976,000 SF (Commercial and Residential)

Including Residential Projects Managed: \$ 4,215 Million over 15,051,000 SF with 13,348 units

PROFESSIONAL EXPERIENCE

J MURVA CONSULTING LTD.

2019 - Present

Development and Construction Consulting Services

President

Providing Owner's Representative services, Pre-Construction services, site selection and evaluation, preliminary financial modeling, Entitlement Phase management, Design management, Procurement, Construction oversight, Customer Care oversight, project closeout and deficiency for mid-high-rise residential, retail, and commercial projects within the GTA.

Project planning of:

- Burlington – Fairview Development, 7 mixed use towers, height ranges 29 – 37 storeys, 2,494 condo and rental units, 93,500 SF retail, estimated construction cost of \$ 1,187 Million
- 473 Albert St., Ottawa, 12 storey mixed use retrofit building, 150 rental units, 8,000 SF of retail space, estimated construction cost \$ 32 Million
- 1256 Markham Rd., Toronto, 2 tower mixed use residential building, height ranges 28 – 30 storeys, 605 rental units, 14,000 SF Retail/Office, estimated construction cost of \$ 186 Million

Construction of:

- 480 Yonge Street, 40 storeys mixed use building, 453 rental and condo units, heritage building component, 24,000 SF of retail space, project construction cost \$ 133 Million
- 593 Yonge Street, 46 storeys mixed use building, 525 condo units, 33,207 SF of retail space, estimated construction cost \$ 145 Million

FIRSTCON GROUP LTD.

2013 - 2018

Division of Freed Group of Companies

Construction Management / General Contractor in Toronto area

President

Responsible for the strategic and tactical management and delivery of construction services for the midhigh-rise residential, retail, and commercial projects within the GTA. Managed the delivery of residential, commercial, and retail projects.

- Oversaw the construction of 4 mixed use residential projects comprising of 6 towers totaling 1,998,200 SF, 1,648 residential units, for a total construction cost of \$ 366 Million
- Provided preconstruction services for 3 mixed use residential projects comprising of 15 towers, a community centre, and new city roads, totaling 4,102,500 SF, 4,754 residential units, for a total construction cost of \$ 1.502 Billion

FREED DEVELOPMENTS INC.

2013 - 2018

Residential high-rise developer in Toronto area

Vice President Construction

Responsible for the oversight of all construction activities and projects by the Freed Group of Companies. The executive level role included participation in shaping the corporate direction, daily corporate operational issues, and establishment of corporate policies/procedures. Tactical role included working with other group leaders in the pursuit of projects, building relationships with financial partners and investors, relationship management with strategic partners, assisting in the procurement of design services, assisting the management of project designs, resolving project legacy issues, assisting with customer care issues and management of customer care field staff, assisting with the resolution of past project legal issues, assisting in the sale of completed project assets, and the establishment of corporate standard contract documents.

- In addition to the projects delivered by FirstCon, oversaw the construction of 2 mixed use residential projects comprising of 2 towers totaling 773,000 SF, 979 residential units, for a total construction cost of \$ 197 Million
- Provided preconstruction services for 4 mixed use residential projects comprising of 15 towers, a community centre, 80 townhouses, and new city roads, totaling 4,262,500 SF, 4,754 residential units, for a total construction cost of \$ 1.526 Billion
- Closed out and resolved legacy issues on 3 mixed use residential projects
- Assisted in the sale of 23,000 SF of leased retail and office space for \$ 28 Million

CBRE Limited Global Corporate Services.

2010 - 2013

Infrastructure Ontario Account (CBRE's most significant account)

North American Project Management Group

Director

- Managed a direct report staff of 5 and overall team of 46 across Ontario
- Managed the delivery of 700 small projects valued at \$ 700 Million
- Achieved substantial EBITDA after three years of losses
- Achieve all KPIs
- Turned around client satisfaction rating from red to green

PROFILE

A Senior Project Manager with over 25 years of domestic and international experience in custom curtain wall systems, construction contract management and global sourcing of custom materials. Responsible for managing projects to achieve positive project results to ensure work is performed safely, on schedule, within budget and to the highest standards of quality and customer satisfaction. Possesses and maintains sound knowledge of construction management, current wall systems technology, construction laws, industry standards and worker safety regulations.

PROFESSIONAL HISTORY

The One Project, 1 Bloor Street West, Toronto. (2017 to Present) **Project Manager – Exterior Building Envelope Specialty**

Responsible to manage all of the building envelope contract work for this iconic mixed-use project.

- Prepared and distributed tender documents for curtain wall, structural glazing, waterproofing and façade access equipment scopes.
- Negotiated and awarded the work.
- Managing the envelope trades through pre-construction and project work.

Oldcastle BuildingEnvelope® (2015 - 2017) Senior Project Manager

Improved project profitability, performance and quality by introducing major improvements to existing project management practices, inter-departmental cooperation and total project performance. Also implemented a comprehensive global sourcing process to provide the highest level of project quality and profitability.

- Midtown Center, Washington, DC. A \$43million custom glass curtain wall project involving copper panels with a post manufactured patina application.
- Project won a 2018 Washington Building Conference Craftsmanship Award.
- Found innovative solutions for material supply for glass from two fabricators in Spain, custom metals, grills, panels and copper (architectural bronze) extrusions from Asia improving profitability and maintaining top quality.

Josef Gartner Canada (Bleu Tech Montreal Inc.), a division of Permasteelisa North America Toronto, Ontario, Canada (2014 - 2015) Senior Project Manager

Responsible to manage the Erin Mills Town Centre Redevelopment, York University Subway Station, Square One South Expansion and Halifax Shopping Centre Redevelopment projects in the Canadian market for a one-year term.

- Erin Mills Town Centre project included the supply and installation of a 30m diameter steel and structural glass sphere over the centre court area of the mall in addition to large structural steel and glass entrances and glass bridge.

Tucker HiRise Construction Inc., Toronto, Ontario, Canada (2012 - 2014) Senior Project Manager – Building Envelope

Responsible to administer the \$27million curtain wall and glazing contract that Tucker had with a Chinese supply and installation contractor for the One Bloor Street Project, Toronto, Ontario, a 78 storey luxury residential tower.

- Hired to closely monitor and control the curtain wall, structural glass wall system and railings contract with a Chinese contractor.
- Oversee and advise on the development of shop drawings and coordination of drawings and technical issues with the project team (Architect, Consultant, Construction Manager and Owner).
- Monitored the design development, submittals, performance mock-up, testing and production of the wall system production in China and Mexico.
- Created and implemented an extensive production monitoring program. Hired and trained the local production and quality monitoring staff in China.
- Acquired an online data inventory program system tracking over 19,000 wall system components from manufacture through installation.

Global Architectural Metals, Welland, Ontario (2010 - 2011) Contracts Manager

Managed and supervised the project management and installation teams for all contract work in the Toronto area.

- Established project scope from estimates, assigned and managed project managers and site staff.
- Coordinated project work with engineering, shop drawings, production and installation.
- Responsible to establish and monitor project budgets.

EDUCATION

1980 – 1984 Ryerson University, Toronto, Ontario, Canada Civil Engineering Technology Diploma

1985 Roofing Industry Educational Institute Basic Roofing Technology

1987 Dale Carnegie & Associates
Effective Speaking and Human Relations

1991 Learning International Professional Selling Skills

CURRENT IN:

- Construction safety and fall protection.
- WHMIS – Workplace Hazardous Materials Information Systems.
- Fire extinguisher training
- First Aid and CPR certified
- Inventory Management systems

PROFESSIONAL ACCREDITATION

Certified Engineering Technologist (C.E.T.)

- Fully accredited as a Certified Engineering Technologist since 1986.
- Received Quarter Century Award as a member of the Ontario Association of Certified Engineering Technicians and Technologists (OACETT) in 2008.

AREAS OF EXPERTISE AND CORE STRENGTHS

- Exceptional leadership, problem solving and communication skills
- Outstanding ability to work under pressure to ensure timelines are met both independently and as part of a team
- Academic and professional background in construction management, construction engineering and Political Science
- Analyzing and assessing blue prints
- Budget maintenance
- Quality assurance and control
- WHIMS and Safety Certified
- Proficient with Microsoft project, excel, and ALL Construction scheduling tools

EMPLOYMENT EXPERIENCE
Project Management / Site Superintendent
STAFFORD HOMES LTD.
July 2016 to 2019**Project Scope:**

- 100 units – 4 storey stacked townhouses with 1 level underground parking garage
- Total Budget Of 25 million
- Project management duties included but not limited to permits, contracts, scopes of work, occupancy packages, complete construction schedules, construction budget, fire rating schedule, 4 storey design build for the added sprinkler system, design build for the fire proofing assembly etc.
- Supervised all construction – rough carpentry, brick / stucco façade, exterior hardscape, interior finishing, waterproofing, PDI / closing schedules, occupancy inspections, etc.

Project Manager**Project Scope:**

- 38 stacked townhomes
- 25,000 square feet of commercial space with 10 townhomes above
- Construction budget, contracts, scopes of work, wood panel design, commercial curtain wall window details and shop drawings

Site Superintendent / Project Manger
Dominus Construction Group, Toronto
March 2013 – 2016

- Project Scope:
- PIER 27 WATERFRONT COMMUNITY - 450 Units - Two 15 story buildings
- High end finishes
- \$450 million project budget
- Supervise all aspects of the construction process
- Manage the structural, mechanical, and electrical engineers due to the very high degree of difficulty of the construction design
- Liaise with project Architect on a daily basis
- Adapt to ongoing changes - Window supplier and installer contract was changed midway through the construction process

- Many structural issues within the 12 story building. Concrete beams and steel cross members which are taking the load of the cantilevered “bridge” extension
- Custom Unit changes – Purchasers making large changes to their units after construction
- Electrical customizations, including surround sound, electric shutters, gas fireplaces, Mechanical customizations including vertical heat pumps in exchange for horizontal

Finishing Superintendent

June 2012 - 2012

The ONNI Group of Companies, Toronto

Project Scope:

- 242 unit - 12 story tower o 28 unit floor plate o Moderate to high end finishes
- \$45 million dollar project budget – (Garrison @ The Yards)
- Managed all trade scheduling and organization from suite rough in to PDI
- Ensured occupancy dates were met due to finishing schedule
- Suites were completed on time with minimal PDI deficiencies
- Brought the building to occupancy with no Tarion penalties

Assistant Site Superintendent/Finishing Superintendent

Sept 2010 - 2012

Dominus Construction

240 Unit, 10 story building o 26 suite floor plate

- Moderate suite finishes, including high end lobby
- \$35 million dollar project budget – (Bathurst Street & Patricia Apartments)
- Was a part of construction from footings to finishes
- Worked closely with all trades -organized and scheduled all aspects of the construction process from ordering steel and concrete to countertop and hardwood install

Assistant Site Superintendent & Construction Clerk

Sept 2005 to August 2006

Dominus Construction Group, Toronto

88 Broadway Condominiums (\$70 million dollar project budget)

- Managed all site paperwork
- Administered all on site trades and deadlines
- Organized site files and permits
- Scheduled all construction site meetings
- Scheduled all steel and concrete deliveries
- Oversaw all aspects of the construction process

Construction Labor

February 2003 to August 2004

Dominus Construction Group, Toronto

- Cleaning the site
 - Laying down tarp and setting up heaters to make sure the concrete sets over night
- Helping any of the trades on site with anything that was necessary

HIGHLIGHTS OF QUALIFICATIONS

- Over 15 years of local construction experience in High Rise and ICI industry
- Handled an accumulated value over \$850 Million of awarded tenders and projects
- Completed Civil Engineering and certificate in Project Management and Estimating
- Handled Design and Build, Stipulated Sum and Construction Management projects
- Team player, self-starter and with computer skills on Word, Excel and MS Project

PROFESSIONAL EXPERIENCE**2019- 2020****Senior Estimator****Pomerleau Inc.**

General Contractor- Canadian Building Operations

- Handled Design and Build, Stipulated Sum and Construction Management tenders
- Serve as lead estimator, team player and mentor junior estimators.
- Call trades, discuss construction schedule, logistics and review lead letters
- Search for bid opportunities, call for bonding and insurance

2018- 2019**Senior Estimator****Lanterra Developments**

Developer & Construction Management- High Rise Residential projects

- Manage tender packages, review scope with Trades and analyze value engineering
- Coordinate project schedule, site logistics, construction approach with the Trades
- Respond to trade RFI, review and coordinate drawings and specs with the operations
- Handled Trade change orders, review, evaluate, costing and negotiations.

2015- 2018**Senior Estimator****Pre-Eng Contracting**

General Contractor- New School construction and Renovations

- Handled hard bid estimating, trade RFI's and attend site visits
- Call trades, discuss construction approach, scope, schedule, and logistics
- Call and coordinate bid bond, insurance, and other tender submission documents
- Review lead letters, call for clarifications and assist the team during tender closing.

2013- 2015**Asst Project Manager / Estimator****Lomax Management Inc.**

Construction Management- High Rise Residential projects

- Managed tender packages, meet, and discuss scope with Trades
- Assisted in issuing subcontracts, evaluation, and negotiation of change order
- Managed the flow and distribution of construction documents and shop drawings
- Project coordination, coordinate drawings and details consultants and trade meetings

2010- 2013**Estimator****Tucker Hi-Rise Construction**

Construction Management- High Rise Residential projects

- Manage tender packages, review scope with Trades and analyze value engineering
- Coordinate project schedule, site logistics, construction approach with the Trades
- Respond to trade RFI, review and coordinate drawings and specs with the operations
- Assist in preparing budget, costing of design changes and analyze value engineering

2009- 2010

Senior Estimator

YORK Contracting Ltd.

General Contractor on retrofit construction and commercial works

- Handled hard bid estimating, attended mandatory site visits
- Managed tender forms, analyze cost and finalize amount of bid

2005- 2009

Estimator and Project Coordinator

LOMAX Management Inc.

Construction Management- High Rise Residential projects

- Prepared direct cost budget including quantity take off
- Responded to client clarification, adjusted cost estimates on design changes
- Involved in coordination with owner, consultants and trade contractors
- Routine visit to site, assess the construction progress and make report

1995- 2002

Senior Estimator

Singapore

General Contractor on Industrial and Commercial

1990-1995

Estimator

Saudi Arabia

General Contractor on Industrial, Oil and Gas

EDUCATIONAL BACKGROUND

- | | |
|---|-----------------|
| • Construction Estimating Certificate | Toronto, Canada |
| • Project Management Certificate | Toronto, Canada |
| • Project Planning and Control Techniques | Singapore |
| • Construction Cost Management | Singapore |
| • BS Engineering (Civil) | Philippines |

PROFESSIONAL AFFILIATION

Ontario Association of Certified Engineering Technician & Technologist



125 Hazelton Avenue, Toronto, Ontario M5R 2E4
T. 416 922 4200 | 1 866 300 0219 | sam@mizrahidevelopments.ca

www.mizrahidevelopments.ca



MIZRAHI

DESIGN / BUILD

APPENDIX C


Mizrahi Developments Permit Tracker					Project Name: The One Project Number: 1709BB03 Owner: Mizrahi Inc			
Item No.	Site Permits	Description	Party Responsible	Status	Action By:	Permit No.	Expiration Date	Additional Notes
1	Site Plan Approval (SPA)	Site Plan Approval	COLE	Approved	City of Toronto/ Jim Laughlin			SPA submission to the City of Toronto was on August 29, 2018. All Engineering Drawings by COLE was approved the City. MECP approval also received from the City.
2	Historical Facade Retention	Heritage	CORE/GCBA	Approved	CORE/GCBA	16 246196 BLD		Submitted and Approved by the City
3	Temporary/Permanent Discharge	Permanent and Temporary Sanitary Discharge Agreement	Terraprobe/Atlas/Cole/MCW	Approved	Mizrahi		2023-04-29	The Temporary Sanitary Discharge agreement was amended on January 30th 2023, and expires on April 29, 2023.
4	Toronto Water	Mizrahi to arrange temporary service	Mizrahi	Approved	Mizrahi			Coordination with City of Toronto on-going
5	Gas/Enbridge	Mizrahi to arrange temporary service	Mizrahi	Approved	Mizrahi			Natural gas bulk metre has been installed. Emergency station has been installed. Interior Finishes of the ERR are in progress. TSSA will be called once complete.
Item No.	Building Permits	Description	Party Responsible	Status	Action By:	Permit No.	Expiration Date	Additional Notes
6	Shoring	Permit has been obtained and posted in the Contruction Site Office	Terraprobe/RJC	Approved		15 260226 BLD 04 BA		Shoring Consultant on record has been changed from Terraprobe to Isherwood. Revised drawings from Isherwood have been submitted to the City of Toronto and was approved by the City as of September 10, 2019.
7	Underslab Drainage Permit	Understab Drainage System	CORE/MCW	Approved	City of Toronto	19 106142 DRN 00 DR		The Underslab Drainage Permit was applied for on September 28, 2018. Issuance of Long Term Discharge Agreement is required as a predecessor to underslab drainage review. The Drainage Permit is listed as Issued by City of Toronto on March 4, 2020.
8	Foundation Permit	Below Grade Structure	RJC	Approved	Jim Laughlin	18 207252 FND 00 CP		The Partial Foundation Permit was accepted on August 10, 2018 and is under review. Status of temporary structures permit unknown. Foundation Permit is listed as Inspection by City of Toronto as of August 17, 2020.
9	Building Permit	For full structure including life safe systems for all fitups	CORE/ Jensen Hughes/ City of Toronto	Approved	City of Toronto	19 106142 BLD 00 NB		Issued by City of Toronto in full on August 4th, 2022.
10	Plumbing Permit	Plumbing Systems	MCW	Approved	City of Toronto	19 106142 PLB 00 PS		The Plumbing Permit was received on Friday, November 13, 2020.
11	HVAC Permit Electrical Safety Authority (ESA)	Mechanical Systems	MCW	Approved	City of Toronto	19 106142 HVA 00 MS		The HVAC Permit was issued on Friday, November 13, 2020.
12			OZZ	Not Submitted	OZZ			Will be initiated in later years when the building is almost complete.
13	Electromagnetic Locks		City of Toronto / Core	Not Submitted	CORE/ MCW			On-hold until Conditional Permit is extended to incorporate cladding, sprinklers and other fitouts.
Item No.	Temporary Permits	Description	Party Responsible	Status	Action By:	Permit No.	Expiration Date	Additional Notes
14	Crane	Temporary Crane Swing Permit	Mizrahi	Submitted	NAV/CAN, Transportation Canada and City of Toronto	Pending		Mizrahi team has submitted documentation to NAV/CAN and Transportation Canada. NAV/CAN has sent an approval letter back to Mizrahi dated July 20, 2023. Jim Laughlin is following up with Transport Canada, and are awaiting the approved permit.
15	Electrical Safety Authority (ESA)	Temporary Power Substation - 16kV/a	OZZ	Approved				
16	Electrical Safety Authority (ESA)	Temporary Power Substation - 400a	OZZ	Approved				
17	Temporary Street Occupancy	Construction Staging on Balmuto St.	Mizrahi	Approved	City of Toronto	85909205	12/31/2023	The updated construction staging permit expires on December 31, 2023. Kindly note that Mizrahi has been working with Councilor Sae's office and the neighbours of 1 Bloor W to mitigate noise from the concrete pump, and a structure has been built surrounding the pump. This did not require an additional permit.
18	Temporary Street Occupancy - Hoarding	Covered Walkway/Staging on Bloor St.W and Yonge St and Rear Laneway	Jim Laughlin	Approved	City of Toronto	76124910	2023-12-31	The updated construction staging permit expires on December 31, 2023. Kindly note paid duty officers are on site daily for assistance with Hoisting on Yonge St, as per the permit requirements.
19	Cut Permit	Balmuto Lane	Jim Laughlin	Approved	City of Toronto	15 224289 DST 00 DS 76124903		The city has issued the permit on May 16, 2021.
20	Streetscape Permit	Streetscape work along Yonge and Bloor	Jim Laughlin	Approved		License No. 908102	12/31/2023	An extension application was submitted and ROW staff have issued a new permit which expires on December 31, 2023. Jane has followed up with Jim Laughlin who has already submitted a renewal request for the new year.



MIZRAHI

DESIGN / BUILD


APPENDIX D

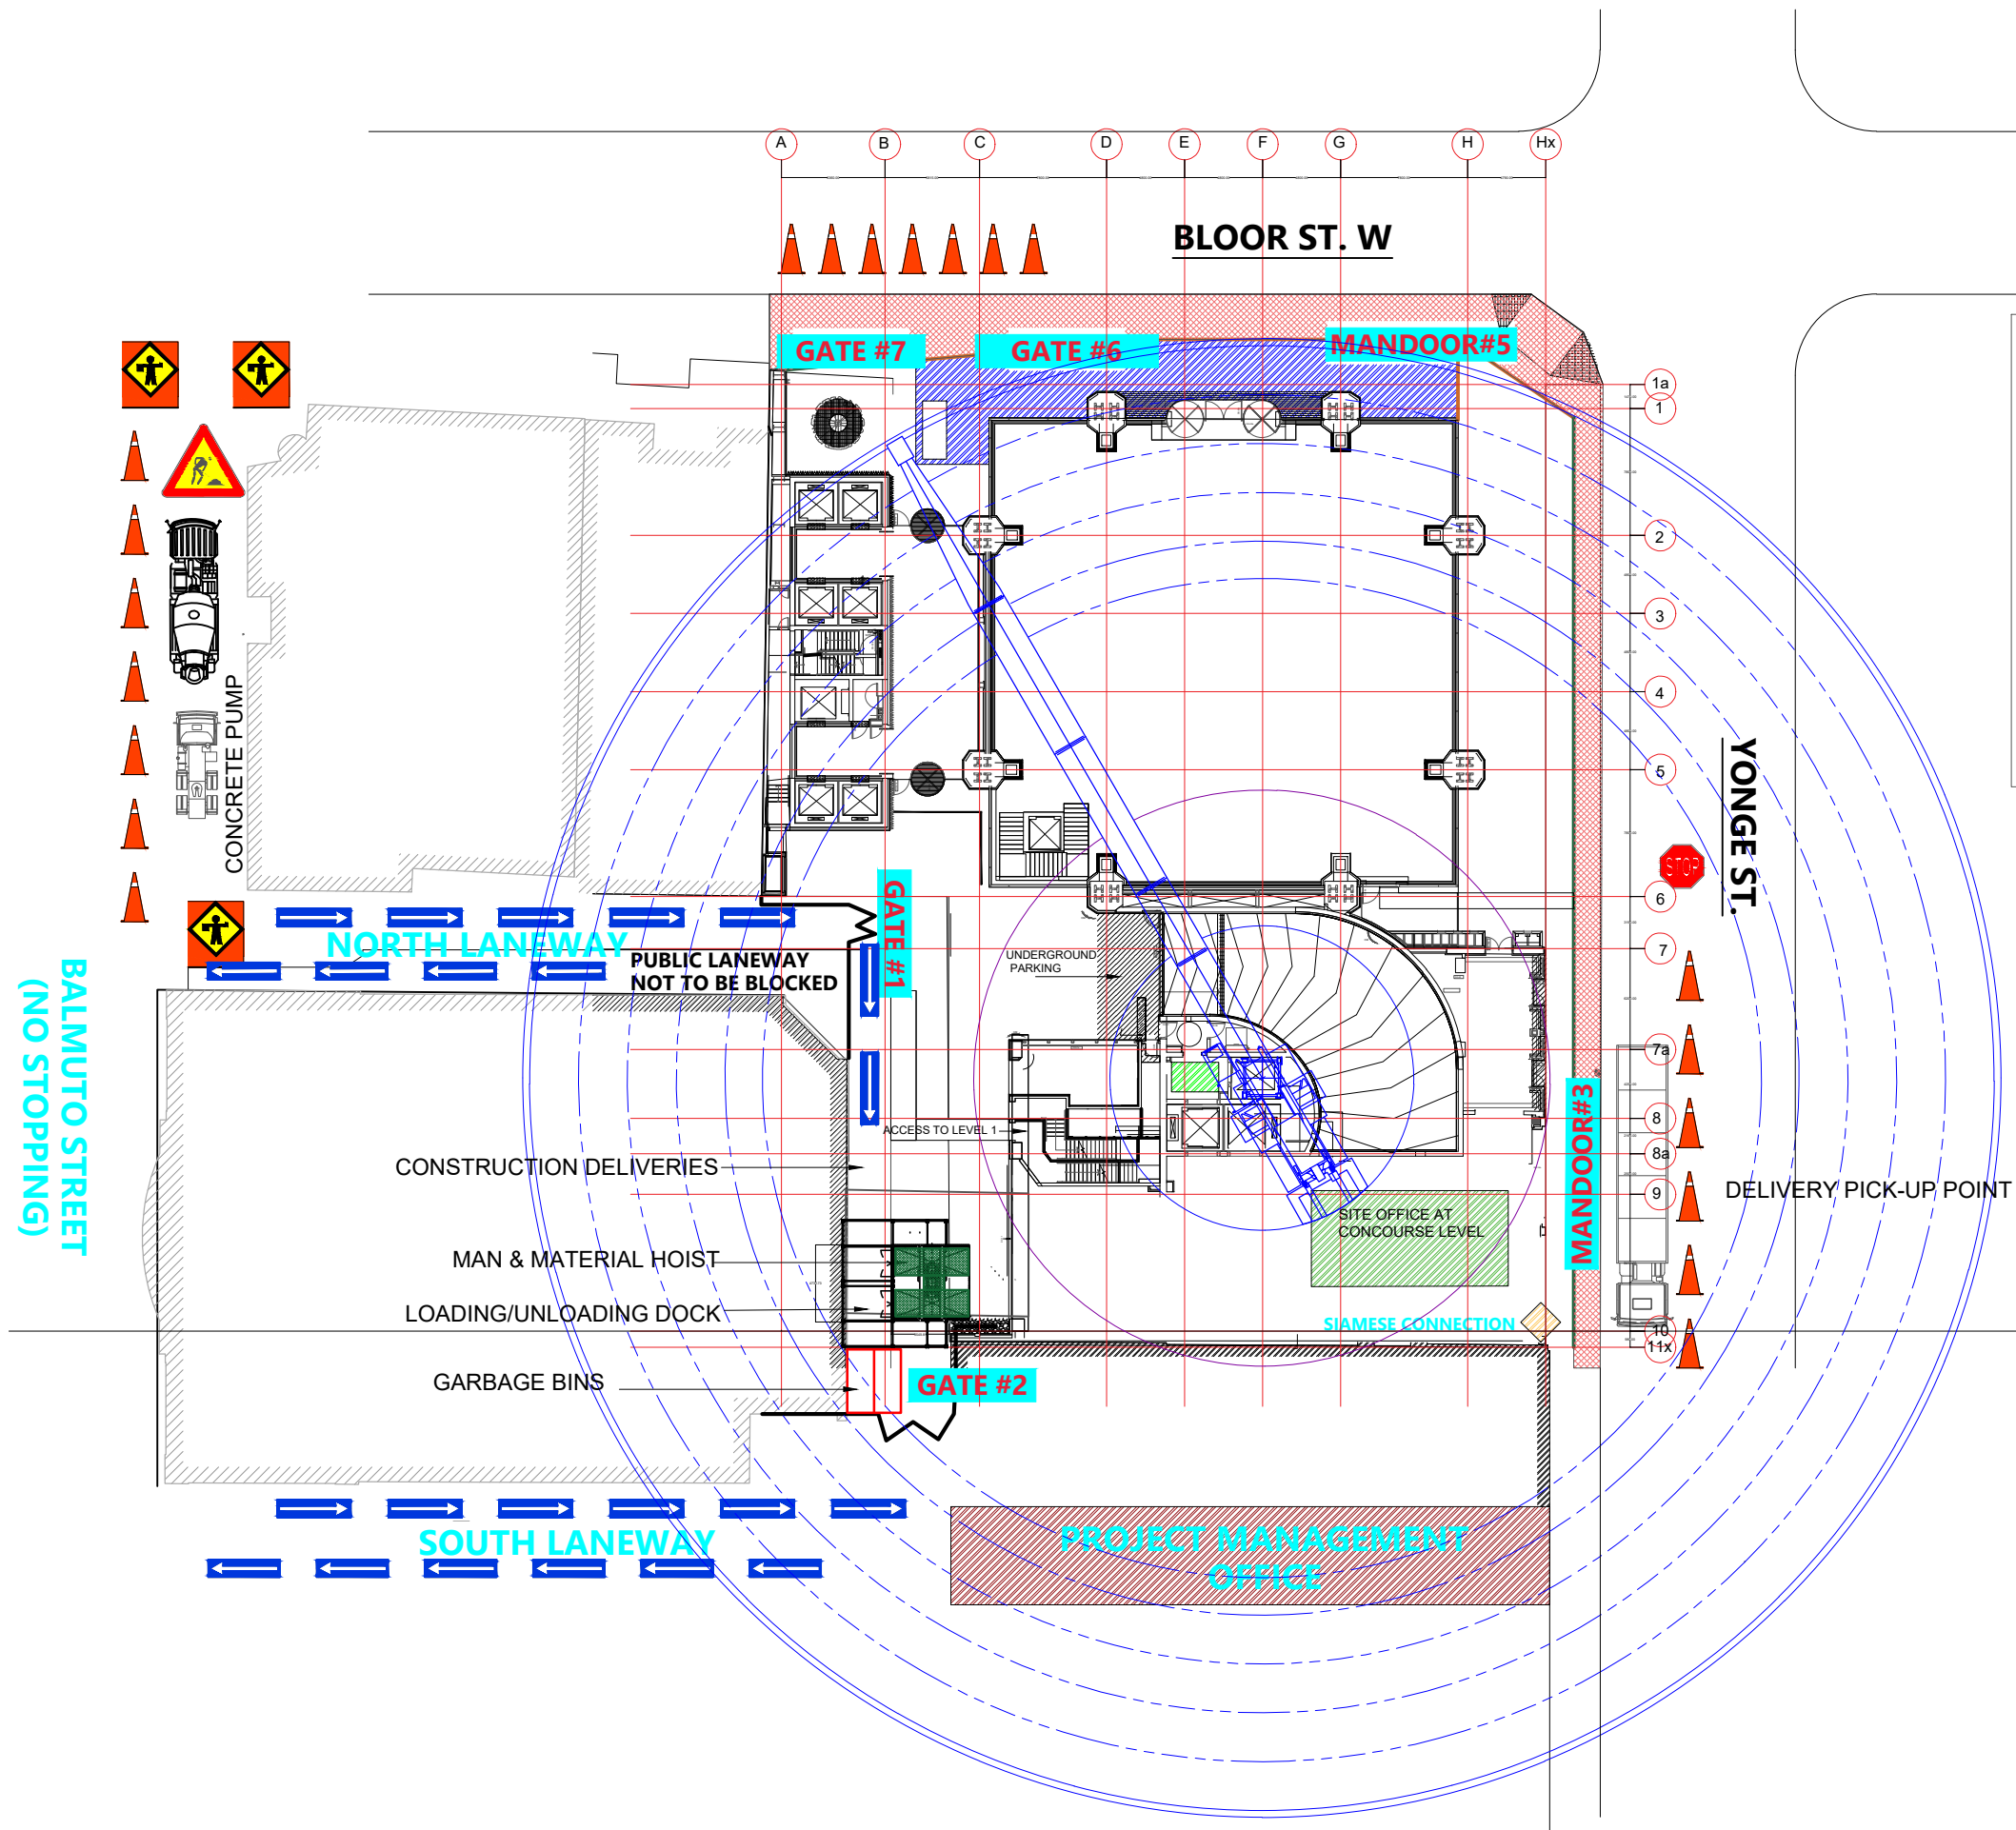

LEGEND

- Apple work area
- Project Management Office
- Over-Head Protection
- MAN & MATERIAL HOIST
- SIAMESE CONNECTION


ONE BLOOR STREET WEST
TORONTO, ON



DRAWN	SCALE 1:75
CHECKED	DATE 2022-03-02

TITLE
GROUND LEVEL
LOGISTICS PLAN
PHASE-2

PROJECT NO.
DRAWING NO.
A205

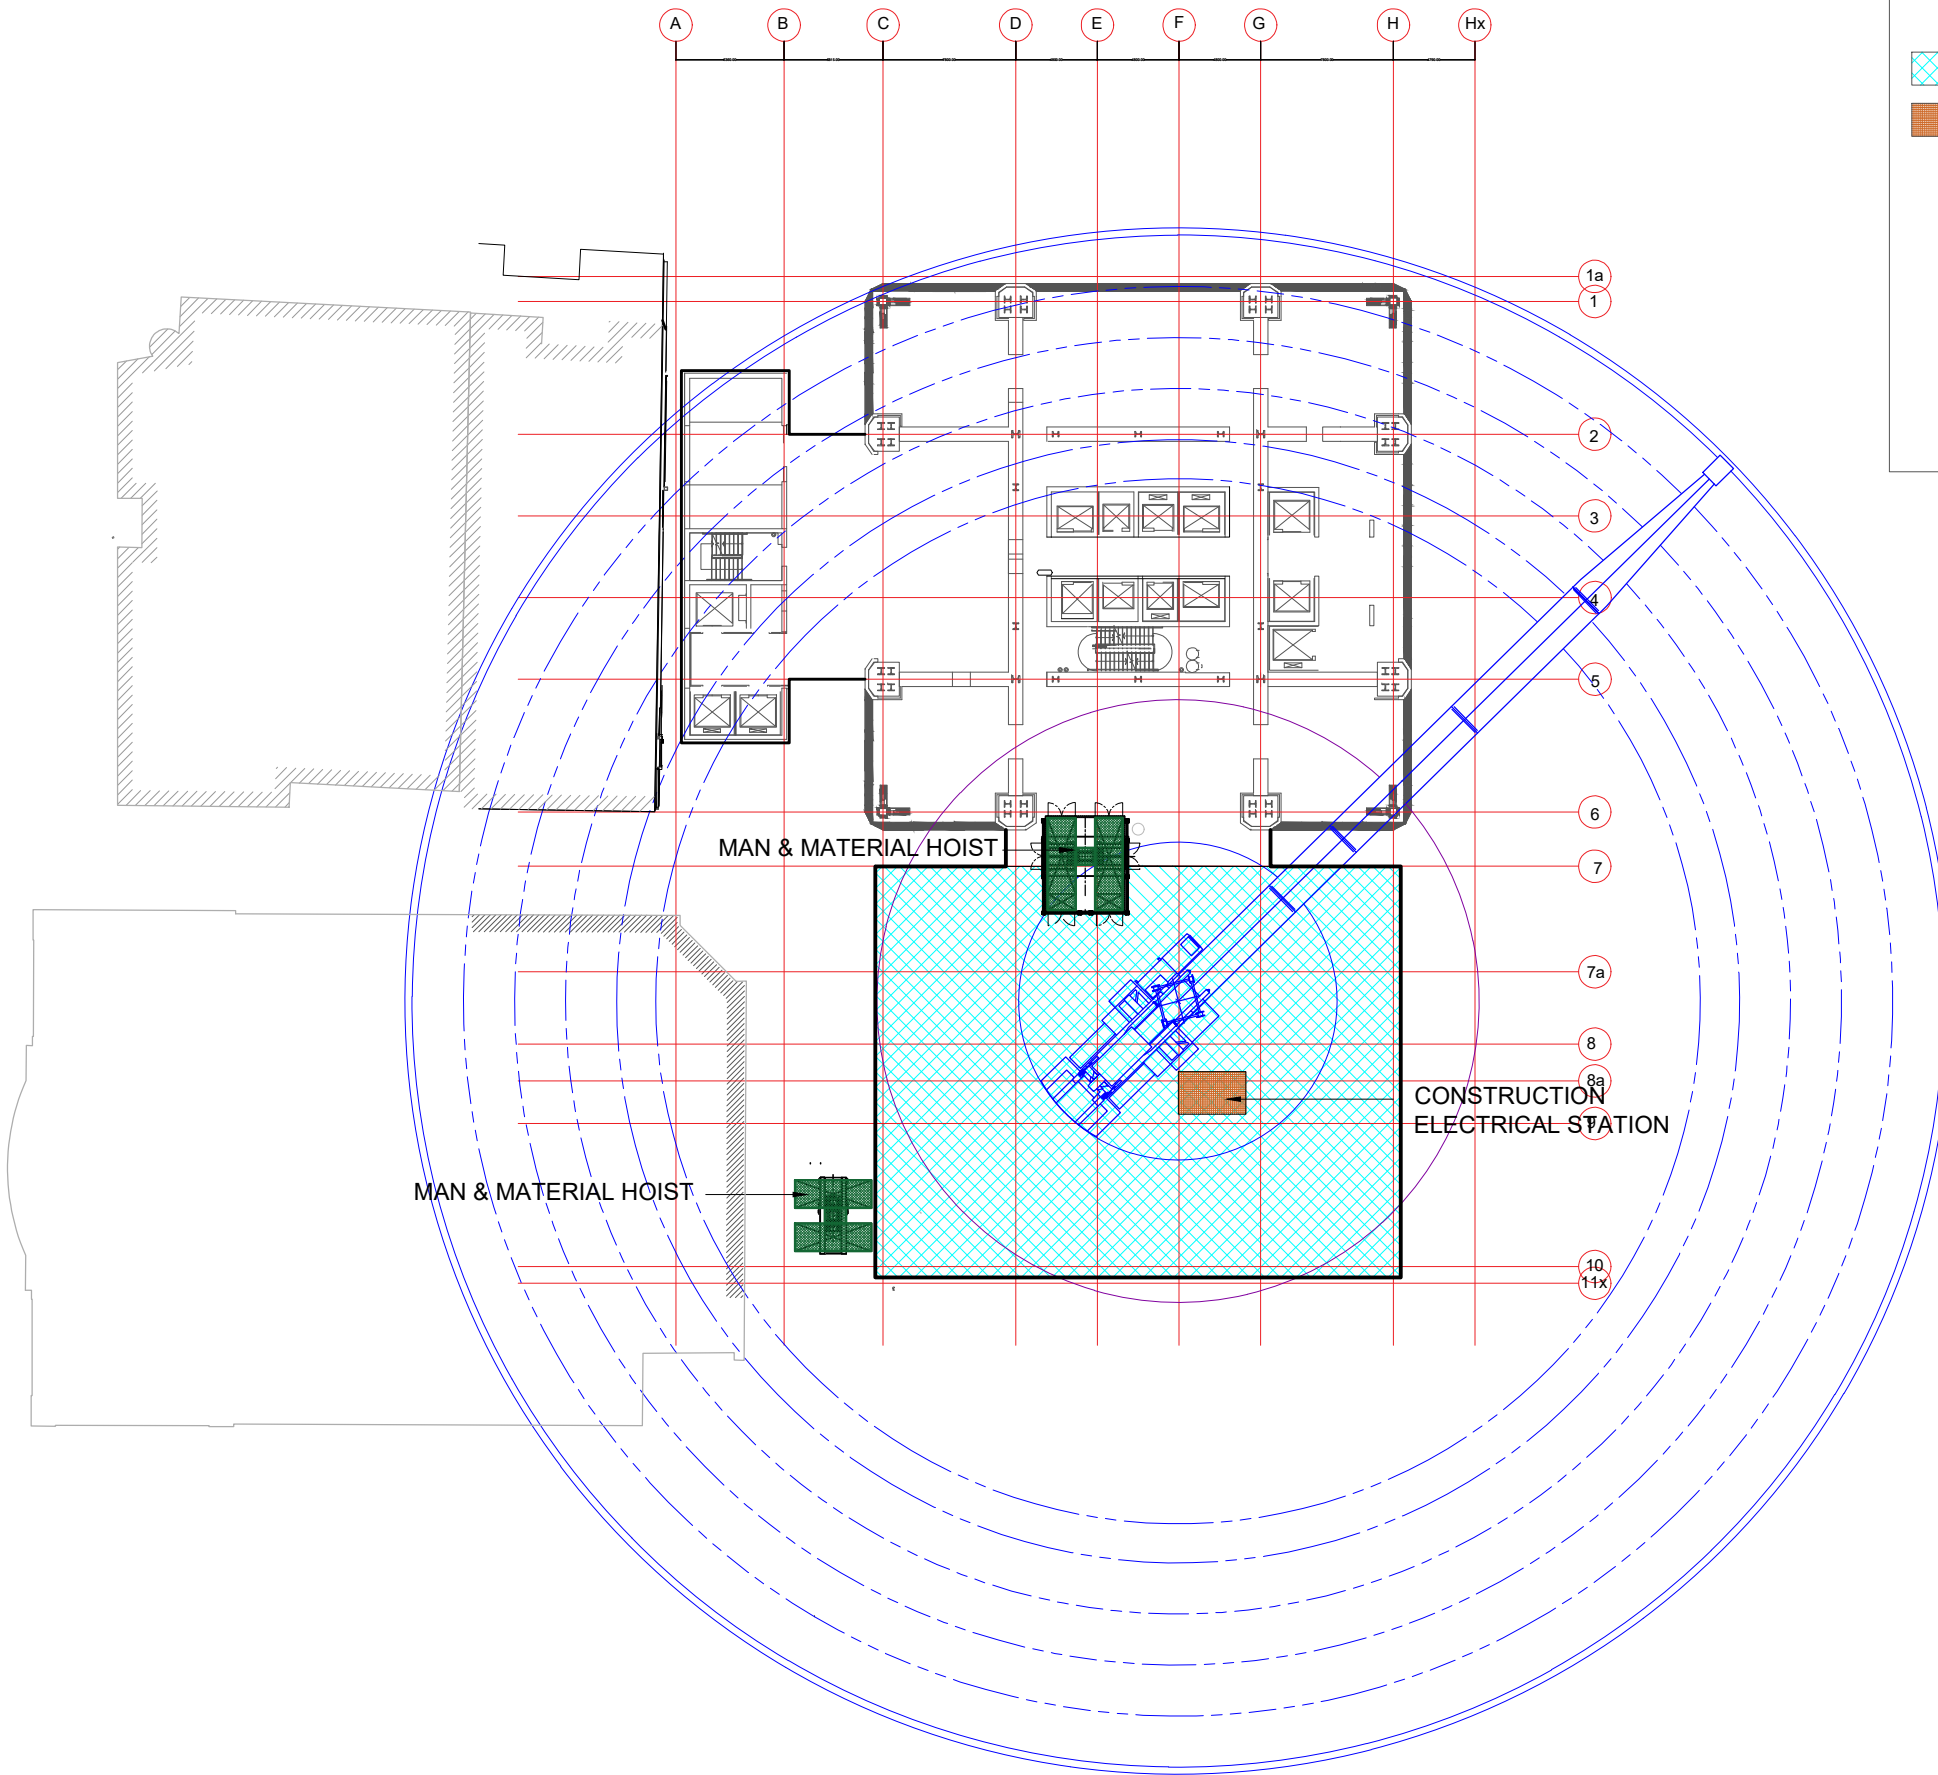


LEGEND

 STAGING PLATFORM

 CONSTRUCTION ELECTRICAL STATION

ONE BLOOR STREET WEST
TORONTO, ON



DRAWN	SCALE 1:1.75
CHECKED	DATE 2022-03-02
TITLE 6TH FLOOR LOGISTICS PLAN PHASE-2	
PROJECT NO.	DRAWING NO. A206



MIZRAHI

DESIGN / BUILD

APPENDIX E



Mizrahi Inc.
125 Hazelton Avenue
Toronto, Ontario M5R 2E4
Canada


Printed on Wed Nov 1, 2023 at 12:05 am EDT

Job #: 1709BB03 The One
2 Bloor Street West
Toronto Ontario. M4W3E2
4169224200

Daily Log Manpower Report

Manpower Graph

Amherst Group Bass Installation ES Fox Constructors Ltd GNI Management Group Inc. Gamma Windows & Walls International Inc. Hardwall Construction
 LMB Mechanical Mizrahi inc. Design-Build Modern Niagara OZZ Electric Inc. Onyx Sprinklers Otis Ltd. SCAF-TECH
 Safety First Consulting Professional Corporation MCC Group United Drywall Limited Turbo McIntosh Perry Sunbrite Drapery Walters Inc.
 Clifford Restoration Federal Wireless Handverk Design Klaus Multiparking Inc. Riverside Group KRCMAR BlockWall Masonry 18 Inc.
 Bothwell-Accurate Black and McDonald Trisan Luis Painting & Decorating Cult Iron Works Limited Great Northern Insulation

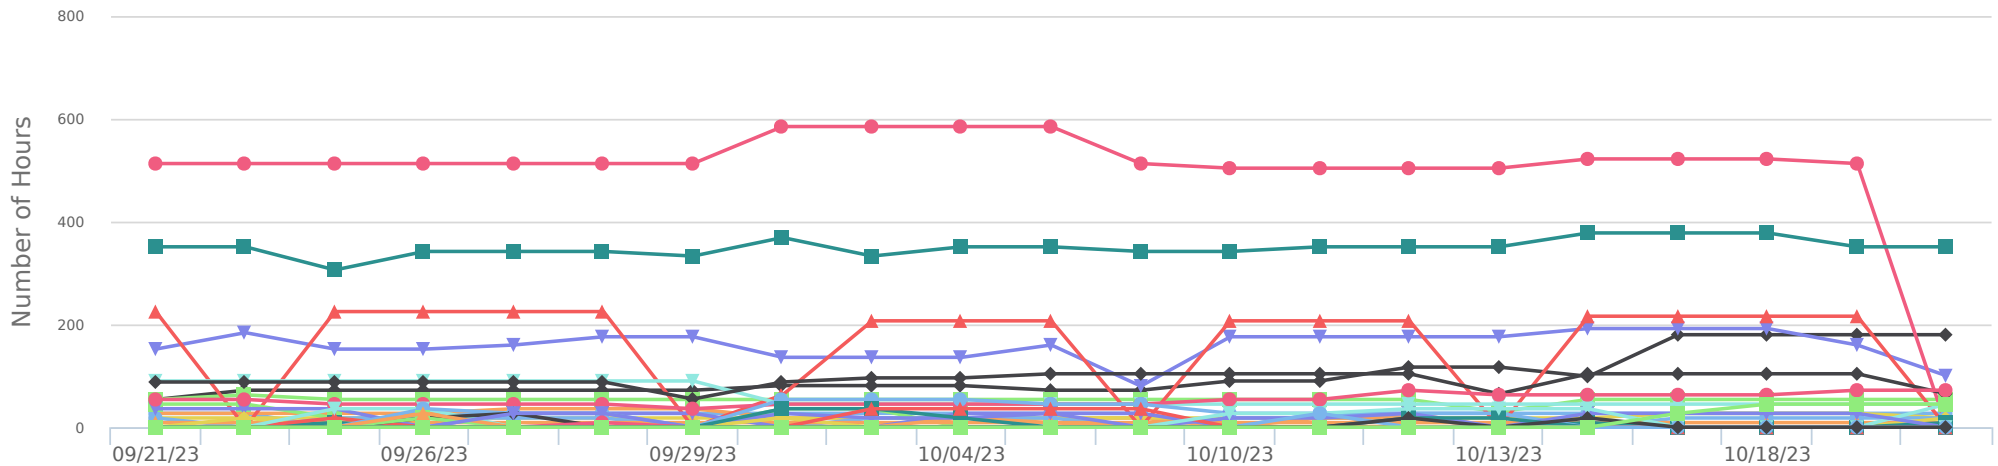

Date	Created By	Company	Workers	Hours	Cost Code	Location	Comments	Attachments	Total Hours
10/20/23	Adele DiGirolomo	Mizrahi inc. Design-Build	15	9.0			Site Supervisors x PM's x Logistics		135.0
10/20/23	Adele DiGirolomo	Mizrahi inc. Design-Build	8	9.0			Traffic Control + Security: On a daily basis Traffic control assists with deliveries, both scheduled and unscheduled. As well, they provide traffic control for the immediate vicinity. Note: The hours only reflect up to 3:00pm.		72.0
10/20/23	Adele DiGirolomo	Safety First Consulting Professional Corporation	1	9.0					9.0
10/20/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Crane Operator(s)		18.0
10/20/23	Adele DiGirolomo	Mizrahi inc. Design-Build	9	9.0			General Labourers: Today the team performed their standard duties of running the hoists, assisting with deliveries, operating Bobcat and forklift. Cleaning and maintaining washrooms and Covid spraying. Site clean up, garbage removal and any other tasks requested by their Supervisor.		81.0
10/20/23	Adele	Mizrahi inc. Design-	4	9.0			Hoist Operators		36.0



Mizrahi Inc.
125 Hazelton Avenue
Toronto, Ontario M5R 2E4
Canada

Printed on Wed Nov 1, 2023 at 12:05 am EDT

Job #: 1709BB03 The One
2 Bloor Street West
Toronto Ontario. M4W3E2
4169224200

Date	Created By	Company	Workers	Hours	Cost Code	Location	Comments	Attachments	Total Hours
	DiGirolomo	Build							
10/20/23	Adele DiGirolomo	Hardwall Construction	0	9.0			Team not on site today due to the Crane raise.		0.0
10/20/23	Adele DiGirolomo	Gamma Windows & Walls International Inc.	20	5.0			Due to rain team moved inside and worked on moving materials and clean up. Finished work at 12:30pm.		100.0
10/20/23	Adele DiGirolomo	ES Fox Constructors Ltd	6	9.0			Team continuing checking fences on site and preparation for the next RCS jump.		54.0
10/20/23	Adele DiGirolomo	Otis Ltd.	13	5.0			Team continued working on working in the HR -LR shafts. Finished work at 12:30pm.		65.0
10/20/23	Adele DiGirolomo	Modern Niagara	0	9.0			Not on site on Friday's.		0.0
10/20/23	Adele DiGirolomo	OZZ Electric Inc.	5	9.0			Team continued working on the following: Laying conduit on the Slab ongoing, Level 18 Mechanical, Levels 19 to 33, preparing for install of fixtures in stairways , and heat tracing.		45.0
10/20/23	Adele DiGirolomo	Amherst Group	3	9.0			On site concrete pump and pump station.		27.0
10/20/23	Adele DiGirolomo	LMB Mechanical	2	9.0			Team continued working on sleeving walls and slab as required, coordination with Modern Niagara and material handling.		18.0
10/20/23	Adele DiGirolomo	Onyx Sprinklers	2	9.0			Not on site on Friday's.		18.0
10/20/23	Adele DiGirolomo	Bass Installation	20	9.0			Team worked on Mechanical Levels, heat tracing, HM shack out, Stage install north face, vertical mullions installed and 17 men working for Gamma on location of frames with 0 frames installed yesterday.		180.0
10/20/23	Adele DiGirolomo	United Drywall Limited	8	9.0			Drywall installation on L2 near Stair F / Housekeeping at various locations / Continued shaft wall for ductwork on the south side of L5 / Shaft work on L5 for the stair press duct.		72.0
10/20/23	Adele DiGirolomo	Mizrahi inc. Design-Build	1	9.0			Off duty Police assisting with traffic control at Gates 3 and 4.		9.0
10/20/23	Adele DiGirolomo	Riverside Group	0	9.0			Not on site on Friday's.		0.0
10/20/23	Adele DiGirolomo	Great Northern Insulation	5	9.0			Team continuing fire spraying Level 3 late afternoon /early evening and material clean up.		45.0
10/20/23	Adele DiGirolomo	Turbo	2	9.0			On site coring for Bass on Level 11.		18.0
10/20/23	Adele DiGirolomo	Walters Inc.	5	9.0			On site preparing for Crane raise. Welding steel and organizing equipment and materials.		45.0
10/20/23	Adele DiGirolomo	McIntosh Perry	1	9.0			Inspecting Level 3 fire spraying.		9.0
10/19/23	Adele DiGirolomo	Mizrahi inc. Design-Build	15	9.0			Site Supervisors x PM's x Logistics		135.0
10/19/23	Adele DiGirolomo	Mizrahi inc. Design-Build	8	9.0			Traffic Control + Security: On a daily basis Traffic control assists with deliveries, both scheduled and unscheduled. As well, they provide traffic control for the immediate vicinity. Note: The hours only reflect up to 3:00pm.		72.0
10/19/23	Adele DiGirolomo	Safety First Consulting Professional Corporation	1	9.0					9.0
10/19/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Crane Operator(s)		18.0
10/19/23	Adele DiGirolomo	Mizrahi inc. Design-Build	9	9.0			General Labourers: Today the team performed their standard duties of running the hoists, assisting with deliveries, operating Bobcat and forklift. Cleaning and maintaining washrooms and Covid spraying. Site clean up, garbage removal and any other tasks requested by their Supervisor.		81.0
10/19/23	Adele DiGirolomo	Mizrahi inc. Design-Build	4	9.0			Hoist Operators		36.0



Mizrahi Inc.
125 Hazelton Avenue
Toronto, Ontario M5R 2E4
Canada

Printed on Wed Nov 1, 2023 at 12:05 am EDT

Job #: 1709BB03 The One
2 Bloor Street West
Toronto Ontario. M4W3E2
4169224200

Date	Created By	Company	Workers	Hours	Cost Code	Location	Comments	Attachments	Total Hours
10/19/23	Adele DiGirolomo	Hardwall Construction	57	9.0			Today Hardwall worked on finishing deck for Level 41 Tower slab, started standing Mega columns and removing south ACS windscreen platforms for Level 36 crane tie-in. Continued formwork for Level 36 lobby and poured Level 34 corners.		513.0
10/19/23	Adele DiGirolomo	Gamma Windows & Walls International Inc.	20	8.0			Team focused on SouthWest Cladding, Southeast Wall and Level 10 Cladding Removal.		160.0
10/19/23	Adele DiGirolomo	ES Fox Constructors Ltd	6	9.0			Team continuing checking fences on site and preparation for the next RCS jump.		54.0
10/19/23	Adele DiGirolomo	Otis Ltd.	13	8.0			Team continued working on HR, LR & Hotel elevators.		104.0
10/19/23	Adele DiGirolomo	Modern Niagara	24	9.0			Teams continuing work on Levels 17-18 Mechanical room, levels 2,5 + 6, temp gas, sleeving as required and material handling.		216.0
10/19/23	Adele DiGirolomo	OZZ Electric Inc.	5	9.0			Team continued working on the following: Laying conduit on the Slab ongoing, Level 18 Mechanical, Levels 19 to 33, preparing for install of fixtures in stairways and receiving materials.		45.0
10/19/23	Adele DiGirolomo	Amherst Group	3	9.0			On site assisting with today's pour.		27.0
10/19/23	Adele DiGirolomo	LMB Mechanical	3	9.0			Team continued working on sleeving walls and slab as required, coordination with Modern Niagara and material handling.		27.0
10/19/23	Adele DiGirolomo	Onyx Sprinklers	2	9.0			Ongoing sleeving and working on pipe risers, high pressure temp riser continuing and material handling.		18.0
10/19/23	Adele DiGirolomo	Bass Installation	20	9.0			Team worked on Mechanical levels and on Level 10 installing Gamma windows.		180.0
10/19/23	Adele DiGirolomo	United Drywall Limited	8	9.0			Insulation on the West Bank Elevators / Housekeeping at various locations / Portion of shaft wall on L5 for stair press ductwork / Installation of drywall at the ceiling on L18 Make Up Air Room / Continued shaft wall for ductwork on the south side of L5.		72.0
10/19/23	Adele DiGirolomo	Mizrahi inc. Design-Build	1	9.0			Off duty Police assisting with traffic control at Gates 3 and 4.		9.0
10/19/23	Adele DiGirolomo	Riverside Group	3	9.0			Team working on SouthWest corner installing blue skin and clips.		27.0
10/19/23	Adele DiGirolomo	Great Northern Insulation	5	9.0			Team continuing fire spraying Level 3 late afternoon /early evening and material clean up.		45.0
10/18/23	Adele DiGirolomo	Mizrahi inc. Design-Build	15	9.0			Site Supervisors x PM's x Logistics		135.0
10/18/23	Adele DiGirolomo	Mizrahi inc. Design-Build	10	9.0			Traffic Control + Security: On a daily basis Traffic control assists with deliveries, both scheduled and unscheduled. As well, they provide traffic control for the immediate vicinity. Note: The hours only reflect up to 3:00pm.		90.0
10/18/23	Adele DiGirolomo	Safety First Consulting Professional Corporation	1	9.0					9.0
10/18/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Crane Operator(s)		18.0
10/18/23	Adele DiGirolomo	Mizrahi inc. Design-Build	9	9.0			General Labourers: Today the team performed their standard duties of running the hoists, assisting with deliveries, operating Bobcat and forklift. Cleaning and maintaining washrooms and Covid spraying. Site clean up, garbage removal and any other tasks requested by their Supervisor. NOTE: team installed additional netting to scaffolding.		81.0
10/18/23	Adele DiGirolomo	Mizrahi inc. Design-Build	4	9.0			Hoist Operators		36.0
10/18/23	Adele DiGirolomo	Hardwall Construction	58	9.0			Today Hardwall worked on finishing deck for Level 41 Tower slab, finished rebar and setting up for Level 34's pour tomorrow. Stripped level 35-36 Lobby walls and started deck on level 36 Lobby slab and received a delivery from Salit.		522.0
10/18/23	Adele DiGirolomo	Gamma Windows & Walls International Inc.	24	8.0			Team focused on installing windows on Level 2 of Heritage, SouthWest cladding, V.Wall West bank, Cladding removal East side of Level 10.		192.0
10/18/23	Adele DiGirolomo	ES Fox Constructors Ltd	6	9.0			Team continuing checking fences on site and moving Suspension shoes.		54.0
10/18/23	Adele DiGirolomo	Otis Ltd.	13	8.0			Team continued working on HR, LR & Hotel elevators.		104.0



Mizrahi Inc.
125 Hazelton Avenue
Toronto, Ontario M5R 2E4
Canada

Printed on Wed Nov 1, 2023 at 12:05 am EDT

Job #: 1709BB03 The One
2 Bloor Street West
Toronto Ontario. M4W3E2
4169224200

Date	Created By	Company	Workers	Hours	Cost Code	Location	Comments	Attachments	Total Hours
10/18/23	Adele DiGirolomo	Modern Niagara	24	9.0			Teams continuing work on Levels 17-18 Mechanical room, levels 2,5 + 6, temp gas, sleeving as required and material handling.		216.0
10/18/23	Adele DiGirolomo	OZZ Electric Inc.	5	9.0			Team continued working on the following: Laying conduit on the Slab ongoing, Level 18 Mechanical, Levels 19 to 33, preparing for install of fixtures in stairways and receiving materials.		45.0
10/18/23	Adele DiGirolomo	Amherst Group	3	9.0			On site servicing pump station		27.0
10/18/23	Adele DiGirolomo	LMB Mechanical	3	9.0			Team continued working on sleeving walls and slab as required, coordination with Modern Niagara and material handling.		27.0
10/18/23	Adele DiGirolomo	Onyx Sprinklers	2	9.0			Ongoing sleeving and working on pipe risers, high pressure temp riser continuing and material handling.		18.0
10/18/23	Adele DiGirolomo	Bass Installation	20	9.0			Team worked on Mechanical levels, back pans caulking, mullion shack out on Level 17, anchors north side, vertical blue skin, and had 16ppl on Level 10 installing Gamma windows.		180.0
10/18/23	Adele DiGirolomo	United Drywall Limited	7	9.0			Insulation on the high rise elevator shafts from L7-L13 / Housekeeping at various locations / Portion of shaft wall on Concourse at Stair B / Installation of drywall at the ceiling on L18 Make Up Air Room / Started shaft wall for ductwork on the south side of L5.		63.0
10/18/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Off duty Police assisting with traffic control at Gates 3 and 4.		18.0
10/18/23	Adele DiGirolomo	Riverside Group	3	9.0			Team working on South West corner and organizing the materials.		27.0
10/18/23	Adele DiGirolomo	Great Northern Insulation	5	9.0			Team continuing fire spraying Level 3 late afternoon /early evening and material clean up.		45.0
10/17/23	Adele DiGirolomo	Mizrahi inc. Design-Build	15	9.0			Site Supervisors x PM's x Logistics		135.0
10/17/23	Adele DiGirolomo	Mizrahi inc. Design-Build	10	9.0			Traffic Control + Security: On a daily basis Traffic control assists with deliveries, both scheduled and unscheduled. As well, they provide traffic control for the immediate vicinity. Note: The hours only reflect up to 3:00pm.		90.0
10/17/23	Adele DiGirolomo	Safety First Consulting Professional Corporation	1	9.0					9.0
10/17/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Crane Operator(s)		18.0
10/17/23	Adele DiGirolomo	Mizrahi inc. Design-Build	9	9.0			General Labourers: Today the team performed their standard duties of running the hoists, assisting with deliveries, operating Bobcat and forklift. Cleaning and maintaining washrooms and Covid spraying. Site clean up, garbage removal and any other tasks requested by their Supervisor.		81.0
10/17/23	Adele DiGirolomo	Mizrahi inc. Design-Build	4	9.0			Hoist Operators		36.0
10/17/23	Adele DiGirolomo	Hardwall Construction	58	9.0			Today Hardwall poured Level 35 to 36 Lobby walls, continued decking corner slab Level 34 and receiving materials from Salit.		522.0
10/17/23	Adele DiGirolomo	Gamma Windows & Walls International Inc.	24	8.0			Team focused on installing windows on Level 2 of Heritage, SouthWest cladding, V.Wall West bank, Cladding removal East side of Level 10.		192.0
10/17/23	Adele DiGirolomo	ES Fox Constructors Ltd	6	9.0			Team continuing checking fences on site and moving Suspension shoes.		54.0
10/17/23	Adele DiGirolomo	Otis Ltd.	13	8.0			Team continued working on HR & LR shaft.		104.0
10/17/23	Adele DiGirolomo	Modern Niagara	24	9.0			Teams continuing work on Levels 17-18 Mechanical room, levels 2,5 + 6, temp gas, sleeving as required and material handling.		216.0
10/17/23	Adele DiGirolomo	OZZ Electric Inc.	5	9.0			Team continued working on the following: Laying conduit on the Slab ongoing, Level 18 Mechanical, Levels 19 to 33, preparing for install of fixtures in stairways and receiving materials.		45.0
10/17/23	Adele DiGirolomo	Amherst Group	3	9.0			On site assisting with today's pour.		27.0
10/17/23	Adele DiGirolomo	LMB Mechanical	3	9.0			Team continued working on sleeving walls and slab as required, coordination with Modern Niagara and material handling.		27.0



Mizrahi Inc.
125 Hazelton Avenue
Toronto, Ontario M5R 2E4
Canada

Printed on Wed Nov 1, 2023 at 12:05 am EDT

Job #: 1709BB03 The One
2 Bloor Street West
Toronto Ontario. M4W3E2
4169224200

Date	Created By	Company	Workers	Hours	Cost Code	Location	Comments	Attachments	Total Hours
10/17/23	Adele DiGirolomo	Onyx Sprinklers	2	9.0			Ongoing sleeving and working on pipe risers, high pressure temp riser continuing and material handling.		18.0
10/17/23	Adele DiGirolomo	Bass Installation	20	9.0			Team worked on Mechanical Level and Level 10 gamma install windows.		180.0
10/17/23	Adele DiGirolomo	United Drywall Limited	7	9.0			Caulking on the north high rise elevator shafts / Housekeeping at various locations / Stud wall installation on the south wall on the east room on L17 / Installation of drywall at the ceiling on L18 Boiler Room / Insulation at the Make Up Air room on L18.		63.0
10/17/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Off duty Police assisting with traffic control at Gates 3 and 4.		18.0
10/17/23	Adele DiGirolomo	Riverside Group	3	9.0			Team working on wrapping Mega Walls on Levels 5 & 6.		27.0
10/17/23	Adele DiGirolomo	Great Northern Insulation	3	9.0			Team continuing fire spraying Level 3 late afternoon /early evening.		27.0
10/16/23	Adele DiGirolomo	Mizrahi inc. Design-Build	15	9.0			Site Supervisors x PM's x Logistics		135.0
10/16/23	Adele DiGirolomo	Mizrahi inc. Design-Build	10	9.0			Traffic Control + Security: On a daily basis Traffic control assists with deliveries, both scheduled and unscheduled. As well, they provide traffic control for the immediate vicinity. Note: The hours only reflect up to 3:00pm.		90.0
10/16/23	Adele DiGirolomo	Safety First Consulting Professional Corporation	1	9.0					9.0
10/16/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Crane Operator(s)		18.0
10/16/23	Adele DiGirolomo	Mizrahi inc. Design-Build	9	9.0			General Labourers: Today the team performed their standard duties of running the hoists, assisting with deliveries, operating Bobcat and forklift. Cleaning and maintaining washrooms and Covid spraying. Site clean up, garbage removal and any other tasks requested by their Supervisor.		81.0
10/16/23	Adele DiGirolomo	Mizrahi inc. Design-Build	4	9.0			Hoist Operators		36.0
10/16/23	Adele DiGirolomo	Hardwall Construction	58	9.0			Today Hardwall pouring mega walls for Level 40-41, decking corner slab Level 34, pouring lobby slab Level 35 and receiving materials from Salit.		522.0
10/16/23	Adele DiGirolomo	Gamma Windows & Walls International Inc.	24	8.0			Team focused on Southwest cladding install, Southeast V.Wall Install, West V.Wall, Level 10 East cladding removal due to Bass install windows to high and Install Windows at Heritage .		192.0
10/16/23	Adele DiGirolomo	ES Fox Constructors Ltd	6	9.0			Team continuing checking fences on site and moving Suspension shoes on the West side.		54.0
10/16/23	Adele DiGirolomo	Otis Ltd.	13	8.0			Team continued working on installing Frames on HR shaft, working on LR shaft and hotel install shaft.		104.0
10/16/23	Adele DiGirolomo	Modern Niagara	24	9.0			Team continuing working on Level 16 & 17 riser duct work shaft, sleeving as required in walls and slabs ongoing and lastly, material handling.		216.0
10/16/23	Adele DiGirolomo	OZZ Electric Inc.	5	9.0			Team continued working on the following: Laying conduit on the Slab ongoing, Level 18 Mechanical, Levels 19 to 33. They were on site yesterday performing a full power shut down and successfully were able to turn over power on the Level 18.		45.0
10/16/23	Adele DiGirolomo	Amherst Group	3	9.0			On site assisting with today's pour.		27.0
10/16/23	Adele DiGirolomo	LMB Mechanical	2	9.0			Team continued working on sleeving walls and slab as required, coordination with Modern Niagara and material handling.		18.0
10/16/23	Adele DiGirolomo	Onyx Sprinklers	0	9.0			Not on site today.		0.0
10/16/23	Adele DiGirolomo	Bass Installation	11	9.0			Team worked on Mechanical Levels, Blue skin repair Level 17, Upper Blue skin install Level 17north, Loading back pans on Levels 17-24, back pan bird screen install and 15 men working on Level 10 install for Gamma.		99.0
10/16/23	Adele DiGirolomo	United Drywall Limited	7	9.0			Caulking on the north high rise elevator shafts on L10 and L12 / Housekeeping at various locations / Stud wall installation on the south wall on the east room on L17 / Installation of drywall at the ceiling on L18 Boiler Room.		63.0
10/16/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Off duty Police assisting with traffic control at Gates 3 and 4.		18.0



Mizrahi Inc.
125 Hazelton Avenue
Toronto, Ontario M5R 2E4
Canada

Printed on Wed Nov 1, 2023 at 12:05 am EDT

Job #: 1709BB03 The One
2 Bloor Street West
Toronto Ontario. M4W3E2
4169224200

Date	Created By	Company	Workers	Hours	Cost Code	Location	Comments	Attachments	Total Hours
10/16/23	Adele DiGirolomo	Riverside Group	3	9.0			Team worked on Level 17 floor under Level 19 installing framing.		27.0
10/16/23	Adele DiGirolomo	Trisan	4	9.0			Team assisted with concrete pour at the landscape area as well received confirmation from the City inspector they removed 150mm, 100mm and 13mm services.		36.0
10/16/23	Adele DiGirolomo	Cult Iron Works Limited	2	9.0			Returned to site installing the top of house GL1-2.		18.0
10/16/23	Adele DiGirolomo	McIntosh Perry	1	9.0			On site for inspection of drywall assemblies at various locations.		9.0
10/13/23	Adele DiGirolomo	Mizrahi inc. Design-Build	14	9.0			Site Supervisors x PM's x Logistics		126.0
10/13/23	Adele DiGirolomo	Mizrahi inc. Design-Build	8	9.0			Traffic Control + Security: On a daily basis Traffic control assists with deliveries, both scheduled and unscheduled. As well, they provide traffic control for the immediate vicinity. Note: The hours only reflect up to 3:00pm.		72.0
10/13/23	Adele DiGirolomo	Safety First Consulting Professional Corporation	1	9.0					9.0
10/13/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Crane Operator(s)		18.0
10/13/23	Adele DiGirolomo	Mizrahi inc. Design-Build	9	9.0			General Labourers: Today the team performed their standard duties of running the hoists, assisting with deliveries, operating Bobcat and forklift. Cleaning and maintaining washrooms and Covid spraying. Site clean up, garbage removal and any other tasks requested by their Supervisor.		81.0
10/13/23	Adele DiGirolomo	Mizrahi inc. Design-Build	4	9.0			Hoist Operators		36.0
10/13/23	Adele DiGirolomo	Hardwall Construction	56	9.0			Today Hardwall poured Level 40 tower slab, finished rebar for Level 35 lobby slab and raised ACS corner screens.		504.0
10/13/23	Adele DiGirolomo	Gamma Windows & Walls International Inc.	22	8.0			Team continued working on installing at West bank V.Wall.		176.0
10/13/23	Adele DiGirolomo	ES Fox Constructors Ltd	6	5.0			Team working on dropdowns , East RCS installation and checking the fence.		30.0
10/13/23	Adele DiGirolomo	Otis Ltd.	13	5.0			Team continued working on HR, LR and Hotel elevators.		65.0
10/13/23	Adele DiGirolomo	Modern Niagara	0	9.0			Not on site on Friday's.		0.0
10/13/23	Adele DiGirolomo	OZZ Electric Inc.	5	9.0			Team continued working on the following: Laying conduit on the Slab ongoing, Level 18 Mechanical, Levels 19 to 33 and setting up heaters throughout the building.		45.0
10/13/23	Adele DiGirolomo	Amherst Group	3	9.0			On site assisting with today's pour.		27.0
10/13/23	Adele DiGirolomo	LMB Mechanical	2	9.0			Team continued working on sleeving walls and slab as required, coordination with Modern Niagara and material handling.		18.0
10/13/23	Adele DiGirolomo	Onyx Sprinklers	0	9.0			Not on site on Friday's.		0.0
10/13/23	Adele DiGirolomo	Bass Installation	13	9.0			Team worked on Mechanical floor, blueskin north side, blueskin west side off swing stage and Back pans from Level 24 to Level 17. 8 panels were installed yesterday.		117.0
10/13/23	Adele DiGirolomo	United Drywall Limited	7	9.0			Shaft wall installation on the north high rise elevator shafts on L10 and L12 / Housekeeping at various locations / Hanger installs at underside of L19 at Fluid Cooler Room / Started the installation of drywall at the ceiling on L18 Boiler Room.		63.0
10/13/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Off duty Police assisting with traffic control at Gates 3 and 4.		18.0
10/13/23	Adele DiGirolomo	Clifford Restoration	3	9.0			Team focused on priming the roof top and getting ready for the Mock up snow guards.		27.0
10/13/23	Adele DiGirolomo	Riverside Group	0	9.0			Not on site on Friday's.		0.0



Mizrahi Inc.
125 Hazelton Avenue
Toronto, Ontario M5R 2E4
Canada

Printed on Wed Nov 1, 2023 at 12:05 am EDT

Job #: 1709BB03 The One
2 Bloor Street West
Toronto Ontario. M4W3E2
4169224200

Date	Created By	Company	Workers	Hours	Cost Code	Location	Comments	Attachments	Total Hours
10/13/23	Adele DiGirolomo	Trisan	4	9.0			Team starting at 10pm tonight to perform the water disconnect.		36.0
10/13/23	Adele DiGirolomo	Bothwell-Accurate	2	9.0			Completed the traffic topping install at the tree pit area on the ground floor at Bloor Street.		18.0
10/12/23	Adele DiGirolomo	Mizrahi inc. Design-Build	14	9.0			Site Supervisors x PM's x Logistics		126.0
10/12/23	Adele DiGirolomo	Mizrahi inc. Design-Build	8	9.0			Traffic Control + Security: On a daily basis Traffic control assists with deliveries, both scheduled and unscheduled. As well, they provide traffic control for the immediate vicinity. Note: The hours only reflect up to 3:00pm.		72.0
10/12/23	Adele DiGirolomo	Safety First Consulting Professional Corporation	1	9.0					9.0
10/12/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Crane Operator(s)		18.0
10/12/23	Adele DiGirolomo	Mizrahi inc. Design-Build	9	9.0			General Labourers: Today the team performed their standard duties of running the hoists, assisting with deliveries, operating Bobcat and forklift. Cleaning and maintaining washrooms and Covid spraying. Site clean up, garbage removal and any other tasks requested by their Supervisor.		81.0
10/12/23	Adele DiGirolomo	Mizrahi inc. Design-Build	4	9.0			Hoist Operators		36.0
10/12/23	Adele DiGirolomo	Hardwall Construction	56	9.0			Today Hardwall was finishing up steel for Level 40 tower slab, started standing cages and placing rebar for Level 35 Lobby slab, poured Level 33 corners and received several deliveries from Salit.		504.0
10/12/23	Adele DiGirolomo	Gamma Windows & Walls International Inc.	22	8.0			Team focused on installing at West bank V.Wall and moved panels from ground level to the west lane way.		176.0
10/12/23	Adele DiGirolomo	ES Fox Constructors Ltd	6	9.0			Team continuing preparation for RCS jump, checking fences and working on Suspension shoes modification.		54.0
10/12/23	Adele DiGirolomo	Otis Ltd.	13	8.0			Team continued working on HR & LR shafts.		104.0
10/12/23	Adele DiGirolomo	Modern Niagara	23	9.0			Team continuing working on Level 16 & 17 riser duct work shaft, sleeving as required in walls and slabs ongoing and lastly, material handling.		207.0
10/12/23	Adele DiGirolomo	OZZ Electric Inc.	5	9.0			Team continued working on the following: Laying conduit on the Slab ongoing, Level 18 Mechanical, Levels 19 to 33 and on P levels.		45.0
10/12/23	Adele DiGirolomo	Amherst Group	3	9.0			On site assisting with today's pour.		27.0
10/12/23	Adele DiGirolomo	LMB Mechanical	2	9.0			Team continued working on sleeving walls and slab as required, coordination with Modern Niagara , material handling and lastly, scanning and coring holes.		18.0
10/12/23	Adele DiGirolomo	Onyx Sprinklers	2	9.0			Sleeving ongoing, working on elevator shafts and mechanical floors as required and high pressure temporary riser continuing.		18.0
10/12/23	Adele DiGirolomo	Bass Installation	13	9.0			Team worked on Mechanical Levels, installing Blue skin Upper Level 17 North, Swing Stage Level 17 West, Back Pans Shack out (L 24 to 17th), Back Panel install Level 17 west. Working with Gamma install on Level 10 and were able to install 8 frames yesterday.		117.0
10/12/23	Adele DiGirolomo	United Drywall Limited	8	9.0			Firestopping at the west bank elevator shafts / Building corridor/Stair walls on 1M and L2 at Stair F / Housekeeping at various locations / Hanger installs at underside of L19 at Fluid Cooler Room / Started the ceiling insulation on L18 Boiler Room.		72.0
10/12/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Off duty Police assisting with traffic control at Gates 3 and 4.		18.0
10/12/23	Adele DiGirolomo	Clifford Restoration	3	9.0			Team focused on painting the flashing.		27.0
10/12/23	Adele DiGirolomo	Riverside Group	3	9.0			Team worked on instal Level 3.		27.0
10/12/23	Adele DiGirolomo	Trisan	4	9.0			Team had a Hydro Vacuum truck clearing around a line that was damaged and will need to be fixed.		36.0
10/12/23	Adele DiGirolomo	Klaus Multiparking Inc.	2	9.0			Working with TSSA inspector on the inspection of the car stackers in the parking levels.		18.0



Mizrahi Inc.
125 Hazelton Avenue
Toronto, Ontario M5R 2E4
Canada

Printed on Wed Nov 1, 2023 at 12:05 am EDT

Job #: 1709BB03 The One
2 Bloor Street West
Toronto Ontario. M4W3E2
4169224200

Date	Created By	Company	Workers	Hours	Cost Code	Location	Comments	Attachments	Total Hours
10/12/23	Adele DiGirolomo	Cult Iron Works Limited	2	9.0			Returned to site working in GL1-2.		18.0
10/12/23	Adele DiGirolomo	GNI Management Group Inc.	3	9.0			Team continuing fireproofing level three this evening.		27.0
10/12/23	Adele DiGirolomo	Bothwell-Accurate	2	9.0			Traffic topping install at the tree pit area on the ground floor at Bloor Street.		18.0
10/11/23	Adele DiGirolomo	Mizrahi inc. Design-Build	14	9.0			Site Supervisors x PM's x Logistics		126.0
10/11/23	Adele DiGirolomo	Mizrahi inc. Design-Build	8	9.0			Traffic Control + Security: On a daily basis Traffic control assists with deliveries, both scheduled and unscheduled. As well, they provide traffic control for the immediate vicinity. Note: The hours only reflect up to 3:00pm.		72.0
10/11/23	Adele DiGirolomo	Safety First Consulting Professional Corporation	1	9.0					9.0
10/11/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Crane Operator(s)		18.0
10/11/23	Adele DiGirolomo	Mizrahi inc. Design-Build	9	9.0			General Labourers: Today the team performed their standard duties of running the hoists, assisting with deliveries, operating Bobcat and forklift. Cleaning and maintaining washrooms and Covid spraying. Site clean up, garbage removal and any other tasks requested by their Supervisor.		81.0
10/11/23	Adele DiGirolomo	Mizrahi inc. Design-Build	4	9.0			Hoist Operators		36.0
10/11/23	Adele DiGirolomo	Hardwall Construction	56	9.0			Today Hardwall finished deck and started placing rebar, continued standing mega columns, finished deck for Level 35 lobby, landed interior elevator cage steel, finished rebar for Level 33 corners and received several deliveries from Salit.		504.0
10/11/23	Adele DiGirolomo	Gamma Windows & Walls International Inc.	22	8.0			Team continued working on Northeast Cladding install on Level 10, Fire Stop, Interior V.Wall. Heritage windows install and Southwest return cladding.		176.0
10/11/23	Adele DiGirolomo	ES Fox Constructors Ltd	6	9.0			Team continuing preparation or RCS jump on the East side on Thursday, install suspension shoes north face, checking fences and cutting beams at elevators.		54.0
10/11/23	Adele DiGirolomo	Otis Ltd.	13	8.0			Team continued working on HR & LR shafts.		104.0
10/11/23	Adele DiGirolomo	Modern Niagara	23	9.0			Team continuing working on Level 16 & 17 riser duct work shaft, sleeving as required in walls and slabs ongoing and lastly, material handling.		207.0
10/11/23	Adele DiGirolomo	OZZ Electric Inc.	5	9.0			Team continued working on the following: Laying conduit on the Slab ongoing, Level 18 Mechanical, Levels 19 to 33 and on P levels.		45.0
10/11/23	Adele DiGirolomo	Amherst Group	3	9.0			On site preparing for tomorrow's pour.		27.0
10/11/23	Adele DiGirolomo	LMB Mechanical	2	9.0			Team continued working on sleeving walls and slab as required, coordination with Modern Niagara , material handling and lastly, scanning and coring holes.		18.0
10/11/23	Adele DiGirolomo	Onyx Sprinklers	2	9.0			Sleeving ongoing, working on elevator shafts and mechanical floors as required and high pressure temporary riser continuing.		18.0
10/11/23	Adele DiGirolomo	Bass Installation	10	9.0			Team worked on Mechanical Level, Blueskinning Level 17 North, Stage HM install Level 17 West, VM install Level 17 and back panels shake out Level 17 West.		90.0
10/11/23	Adele DiGirolomo	United Drywall Limited	6	9.0			Firestopping at the west bank elevator shafts / Building corridor/Stair walls on 1M and L2 at Stair F / Housekeeping at various locations / Delivery of studs for L17 arrived to site today .		54.0
10/11/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Off duty Police assisting with traffic control at Gates 3 and 4.		18.0
10/11/23	Adele DiGirolomo	Clifford Restoration	3	9.0			Team continuing install of the ice guards and finishing the flashing.		27.0
10/11/23	Adele DiGirolomo	Riverside Group	2	9.0			Team continued working on the Level 19 under-slab, finishing up the east side today and then jumping to the West side.		18.0
10/11/23	Adele DiGirolomo	Trisan	3	9.0			Team continued with removing debris and dirt from landscaping area on ground level.		27.0



Mizrahi Inc.
125 Hazelton Avenue
Toronto, Ontario M5R 2E4
Canada

Printed on Wed Nov 1, 2023 at 12:05 am EDT

Job #: 1709BB03 The One
2 Bloor Street West
Toronto Ontario. M4W3E2
4169224200

Date	Created By	Company	Workers	Hours	Cost Code	Location	Comments	Attachments	Total Hours
10/11/23	Adele DiGirolomo	Klaus Multiparking Inc.	2	9.0			Working with TSSA inspector on the inspection of the car stackers in the parking levels.		18.0
10/11/23	Adele DiGirolomo	Luis Painting & Decorating	3	9.0			Prepping and primed the ceiling of the parking ramp ceiling.		27.0
10/10/23	Adele DiGirolomo	Mizrahi inc. Design-Build	13	9.0			Site Supervisors x PM's x Logistics		117.0
10/10/23	Adele DiGirolomo	Mizrahi inc. Design-Build	8	9.0			Traffic Control + Security: On a daily basis Traffic control assists with deliveries, both scheduled and unscheduled. As well, they provide traffic control for the immediate vicinity. Note: The hours only reflect up to 3:00pm.		72.0
10/10/23	Adele DiGirolomo	Safety First Consulting Professional Corporation	1	9.0					9.0
10/10/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Crane Operator(s)		18.0
10/10/23	Adele DiGirolomo	Mizrahi inc. Design-Build	9	9.0			General Labourers: Today the team performed their standard duties of running the hoists, assisting with deliveries, operating Bobcat and forklift. Cleaning and maintaining washrooms and Covid spraying. Site clean up, garbage removal and any other tasks requested by their Supervisor.		81.0
10/10/23	Adele DiGirolomo	Mizrahi inc. Design-Build	4	9.0			Hoist Operators		36.0
10/10/23	Adele DiGirolomo	Hardwall Construction	56	9.0			Today Hardwall finished decking for Level 40 Tower slab and started standing mega walls. Continued formwork for Level 35 Lobby, finishing deck for level 33 corners and received deliveries from Salit.		504.0
10/10/23	Adele DiGirolomo	Gamma Windows & Walls International Inc.	22	8.0			Team worked on Northeast Cladding install on Level 10, Fire Stop, Interior V.Wall. Heritage windows install and Southwest return cladding.		176.0
10/10/23	Adele DiGirolomo	ES Fox Constructors Ltd	6	9.0			Team preparing for RCS jump on the East side on Thursday, Installing sheet metal patches in screen and anchoring strut bases on Level 13.		54.0
10/10/23	Adele DiGirolomo	Otis Ltd.	13	8.0			Team continued working on HR & LR shafts.		104.0
10/10/23	Adele DiGirolomo	Modern Niagara	23	9.0			Team continuing working on Level 16 & 17 riser duct work shaft, sleeving as required in walls and slabs ongoing and lastly, material handling.		207.0
10/10/23	Adele DiGirolomo	OZZ Electric Inc.	5	9.0			Team continued working on the following: Laying conduit on the Slab ongoing, Level 18 Mechanical, Levels 19 to 33 and on P levels.		45.0
10/10/23	Adele DiGirolomo	Amherst Group	0	9.0			Not on site today.		0.0
10/10/23	Adele DiGirolomo	LMB Mechanical	2	9.0			Team continued working on sleeving walls and slab as required, coordination with Modern Niagara , material handling and lastly, scanning and coring holes.		18.0
10/10/23	Adele DiGirolomo	Onyx Sprinklers	2	9.0			Sleeving ongoing, working on elevator shafts and mechanical floors as required and high pressure temporary riser continuing.		18.0
10/10/23	Adele DiGirolomo	Bass Installation	10	9.0			Team worked on Mechanical Levels floors, Blue Skinning bird screens, Stage HM level 17 West, VM & HM7 Back Panels shakeout and orientation for RCS training.		90.0
10/10/23	Adele DiGirolomo	United Drywall Limited	6	9.0			Firestopping at the west bank elevator shafts / Building corridor/Stair walls on 1M and L2 at Stair F / Housekeeping at various locations .		54.0
10/10/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Off duty Police assisting with traffic control at Gates 3 and 4.		18.0
10/10/23	Adele DiGirolomo	Clifford Restoration	3	9.0			Team installing the ice guards and finishing the flashing.		27.0
10/10/23	Adele DiGirolomo	Riverside Group	2	9.0			Team working on Level 19 underside of slab framing North East & West sides. Received a delivery of materials as well.		18.0
10/10/23	Adele DiGirolomo	Trisan	3	9.0			Team on site and have started on Yonge St removal of the water mains.		27.0
10/06/23	Adele DiGirolomo	Mizrahi inc. Design-Build	13	9.0			Site Supervisors x PM's x Logistics		117.0



Mizrahi Inc.
125 Hazelton Avenue
Toronto, Ontario M5R 2E4
Canada

Printed on Wed Nov 1, 2023 at 12:05 am EDT

Job #: 1709BB03 The One
2 Bloor Street West
Toronto Ontario. M4W3E2
4169224200

Date	Created By	Company	Workers	Hours	Cost Code	Location	Comments	Attachments	Total Hours
10/06/23	Adele DiGirolomo	Mizrahi inc. Design-Build	8	9.0			Traffic Control + Security: On a daily basis Traffic control assists with deliveries, both scheduled and unscheduled. As well, they provide traffic control for the immediate vicinity. Note: The hours only reflect up to 3:00pm.		72.0
10/06/23	Adele DiGirolomo	Safety First Consulting Professional Corporation	1	9.0					9.0
10/06/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Crane Operator(s)		18.0
10/06/23	Adele DiGirolomo	Mizrahi inc. Design-Build	9	9.0			General Labourers: Today the team performed their standard duties of running the hoists, assisting with deliveries, operating Bobcat and forklift. Cleaning and maintaining washrooms and Covid spraying. Site clean up, garbage removal and any other tasks requested by their Supervisor.		81.0
10/06/23	Adele DiGirolomo	Mizrahi inc. Design-Build	4	9.0			Hoist Operators		36.0
10/06/23	Adele DiGirolomo	Hardwall Construction	57	9.0			Today Hardwall continued building tables for Level 40 Tower slab, finished stripping Level 34-35 elevator walls and started deck for Level 35 Lobby. They also were building deck for Level 33 corners and poured the remainder of Level 31 upstand beams.		513.0
10/06/23	Adele DiGirolomo	Gamma Windows & Walls International Inc.	16	5.0			Prepping Heritage area windows, Cladding East side half way completed. Finished at 12:30pm today.		80.0
10/06/23	Adele DiGirolomo	ES Fox Constructors Ltd	6	9.0			Team continued working on RCS. Finished at 12:30pm today.		54.0
10/06/23	Adele DiGirolomo	Otis Ltd.	13	8.0			Team continued working on installing frames. Finished at 12:30pm today.		104.0
10/06/23	Adele DiGirolomo	Modern Niagara	0	9.0			Not on site on Friday's.		0.0
10/06/23	Adele DiGirolomo	OZZ Electric Inc.	5	9.0			Team worked on the following: Laying conduit on the Slab ongoing, Level 18 Mechanical, Levels 19 to 33 and on P levels.		45.0
10/06/23	Adele DiGirolomo	Amherst Group	3	9.0			On site assisting with today's pour.		27.0
10/06/23	Adele DiGirolomo	LMB Mechanical	2	9.0			Team continued working on sleeving walls and slab as required, coordination with Modern Niagara , material handling.		18.0
10/06/23	Adele DiGirolomo	Onyx Sprinklers	0	9.0			Not on site on Friday's.		0.0
10/06/23	Adele DiGirolomo	Bass Installation	8	9.0			Team continued working on Mechanical Level, Level 17 layout, Level17 West VM & HM install. 15 people working on Gamma window install.		72.0
10/06/23	Adele DiGirolomo	United Drywall Limited	5	9.0			Firestopping at the west bank elevator shafts / Installing hangers and pins for insulation on the underside of L19 / Housekeeping at various locations.		45.0
10/06/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Off duty Police assisting with traffic control at Gates 3 and 4.		18.0
10/06/23	Adele DiGirolomo	GNI Management Group Inc.	2	9.0			Continued on Level 3.		18.0
10/06/23	Adele DiGirolomo	Clifford Restoration	5	9.0			Team painting and patching the flashing today.		45.0
10/06/23	Adele DiGirolomo	Riverside Group	0	9.0			Not on site on Friday's.		0.0
10/06/23	Adele DiGirolomo	Black and McDonald	4	9.0			Team continued with installation of hand wells and lines.		36.0
10/06/23	Adele DiGirolomo	UCC Group	3	9.0			Today they focused on housekeeping items. Moving materials and clean up.		27.0
10/05/23	Adele DiGirolomo	Mizrahi inc. Design-Build	13	9.0			Site Supervisors x PM's x Logistics		117.0
10/05/23	Adele DiGirolomo	Mizrahi inc. Design-Build	9	9.0			Traffic Control + Security: On a daily basis Traffic control assists with deliveries, both scheduled and unscheduled. As well, they provide traffic control for the immediate vicinity. Note: The hours only reflect up to 3:00pm.		81.0



Mizrahi Inc.
125 Hazelton Avenue
Toronto, Ontario M5R 2E4
Canada

Printed on Wed Nov 1, 2023 at 12:05 am EDT

Job #: 1709BB03 The One
2 Bloor Street West
Toronto Ontario. M4W3E2
4169224200

Date	Created By	Company	Workers	Hours	Cost Code	Location	Comments	Attachments	Total Hours
10/05/23	Adele DiGirolomo	Safety First Consulting Professional Corporation	1	9.0					9.0
10/05/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Crane Operator(s)		18.0
10/05/23	Adele DiGirolomo	Mizrahi inc. Design-Build	9	9.0			General Labourers: Today the team performed their standard duties of running the hoists, assisting with deliveries, operating Bobcat and forklift. Cleaning and maintaining washrooms and Covid spraying. Site clean up, garbage removal and any other tasks requested by their Supervisor.		81.0
10/05/23	Adele DiGirolomo	Mizrahi inc. Design-Build	4	9.0			Hoist Operators		36.0
10/05/23	Adele DiGirolomo	Hardwall Construction	65	9.0			Today Hardwall were building tables for Level 40 slab/stripping mega columns, started stripping elevator walls, continued raiser corner ACS screens and received a delivery of materials.		585.0
10/05/23	Adele DiGirolomo	Gamma Windows & Walls International Inc.	20	8.0			Team continued worked on Curtain Wall & Southeast interior V.Wall, East Cladding install, and Southeast Wall.		160.0
10/05/23	Adele DiGirolomo	ES Fox Constructors Ltd	6	9.0			Team jumped the West RCS system then started installing struts.		54.0
10/05/23	Adele DiGirolomo	Otis Ltd.	13	8.0			Team continued working on HR & LR shafts.		104.0
10/05/23	Adele DiGirolomo	Modern Niagara	23	9.0			Team continuing working on Level 16 & 17 riser duct work shaft, Scaffolding on Level 17 West, sleeving as required in walls and slabs ongoing and lastly, material handling.		207.0
10/05/23	Adele DiGirolomo	OZZ Electric Inc.	5	9.0			Team worked on the following: Laying conduit on the Slab ongoing, Level 18 Mechanical, Levels 19 to 33 and on P levels.		45.0
10/05/23	Adele DiGirolomo	Amherst Group	3	9.0			On site assisting with today's pour.		27.0
10/05/23	Adele DiGirolomo	LMB Mechanical	2	9.0			Team continued working on sleeving walls and slab as required, coordination with Modern Niagara , material handling and lastly, scanning and coring holes.		18.0
10/05/23	Adele DiGirolomo	Onyx Sprinklers	2	9.0			Sleeving ongoing, working on elevator shafts and mechanical floors as required and high pressure temporary riser continuing.		18.0
10/05/23	Adele DiGirolomo	Bass Installation	8	9.0			Team continued working on Mechanical Levels, on Level 17 East side caulking and louver adaptors shackout , also on Level 17 west with VM & HM install. Lastly, installed Gamma windows on Level 11.		72.0
10/05/23	Adele DiGirolomo	United Drywall Limited	5	9.0			Firestopping at the west bank elevator shafts / Building shaft wall on L2 on south west side / Housekeeping at various locations.		45.0
10/05/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Off duty Police assisting with traffic control at Gates 3 and 4.		18.0
10/05/23	Adele DiGirolomo	GNI Management Group Inc.	2	9.0			Continued on Level 3.		18.0
10/05/23	Adele DiGirolomo	Clifford Restoration	5	9.0			Team now worked on priming the flashing.		45.0
10/05/23	Adele DiGirolomo	Riverside Group	3	9.0			Team continued working on Level 17th installing and under side of Level 19th.		27.0
10/05/23	Adele DiGirolomo	Black and McDonald	4	9.0			Team continued with installation of hand wells and lines.		36.0
10/05/23	Adele DiGirolomo	UCC Group	3	9.0			Today they poured concrete on the landscaping.		27.0
10/05/23	Adele DiGirolomo	Klaus Multiparking Inc.	1	9.0			Prepping Car stackers for TSSA inspections.		9.0
10/04/23	Adele DiGirolomo	Mizrahi inc. Design-Build	13	9.0			Site Supervisors x PM's x Logistics		117.0
10/04/23	Adele DiGirolomo	Mizrahi inc. Design-Build	9	9.0			Traffic Control + Security: On a daily basis Traffic control assists with deliveries, both scheduled and unscheduled. As well, they provide traffic control for the immediate vicinity. Note: The hours only reflect up to 3:00pm.		81.0



Mizrahi Inc.
125 Hazelton Avenue
Toronto, Ontario M5R 2E4
Canada

Printed on Wed Nov 1, 2023 at 12:05 am EDT

Job #: 1709BB03 The One
2 Bloor Street West
Toronto Ontario. M4W3E2
4169224200

Date	Created By	Company	Workers	Hours	Cost Code	Location	Comments	Attachments	Total Hours
10/04/23	Adele DiGirolomo	Safety First Consulting Professional Corporation	1	9.0					9.0
10/04/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Crane Operator(s)		18.0
10/04/23	Adele DiGirolomo	Mizrahi inc. Design-Build	9	9.0			General Labourers: Today the team performed their standard duties of running the hoists, assisting with deliveries, operating Bobcat and forklift. Cleaning and maintaining washrooms and Covid spraying. Site clean up, garbage removal and any other tasks requested by their Supervisor.		81.0
10/04/23	Adele DiGirolomo	Mizrahi inc. Design-Build	4	9.0			Hoist Operators		36.0
10/04/23	Adele DiGirolomo	Hardwall Construction	65	9.0			Today Hardwall poured Level 39-40 mega columns/walls, started stripping Level 34-35 elevator walls, started raising ACS corner screens and receiving materials.		585.0
10/04/23	Adele DiGirolomo	Gamma Windows & Walls International Inc.	17	8.0			Team continued worked on West V. Wall install, Curtain Wall install on Level 11, Cladding East (Shut Down) Air Seal and lastly, Stack Head / Fire Stop.		136.0
10/04/23	Adele DiGirolomo	ES Fox Constructors Ltd	6	9.0			Team preparing for the RCS jump planned for tomorrow.		54.0
10/04/23	Adele DiGirolomo	Otis Ltd.	12	8.0			Team continued working on HR frames and LR rails.		96.0
10/04/23	Adele DiGirolomo	Modern Niagara	23	9.0			Team continuing working on Level 16 & 17 riser duct work shaft, Scaffolding on Level 17 West, sleeving as required in walls and slabs ongoing and lastly, material handling.		207.0
10/04/23	Adele DiGirolomo	OZZ Electric Inc.	5	9.0			Team worked on the following: Laying conduit on the Slab ongoing, Level 18 Mechanical, Levels 19 to 33 and on P levels.		45.0
10/04/23	Adele DiGirolomo	Amherst Group	3	9.0			On site assisting with today's pour.		27.0
10/04/23	Adele DiGirolomo	LMB Mechanical	2	9.0			Team continued working on sleeving walls and slab as required, coordination with Modern Niagara , material handling and lastly, scanning and coring holes.		18.0
10/04/23	Adele DiGirolomo	Onyx Sprinklers	2	9.0			Sleeving ongoing, working on elevator shafts and mechanical floors as required and high pressure temporary riser continuing.		18.0
10/04/23	Adele DiGirolomo	Bass Installation	9	9.0			Team continued working on Mechanical floor, Level 17th East doing Bottom backpan install, L17th West VM & HM install.		81.0
10/04/23	Adele DiGirolomo	United Drywall Limited	5	9.0			Firestopping at the west bank elevator shafts / Building shaft wall on L2 on south west side / Housekeeping at various locations.		45.0
10/04/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Off duty Police assisting with traffic control at Gates 3 and 4.		18.0
10/04/23	Adele DiGirolomo	GNI Management Group Inc.	2	9.0			Now onto Level 3.		18.0
10/04/23	Adele DiGirolomo	Clifford Restoration	6	9.0			Continued working on roof top flashing.		54.0
10/04/23	Adele DiGirolomo	Riverside Group	2	9.0			Team continued working on Level 17 framing under the slab.		18.0
10/04/23	Adele DiGirolomo	Bothwell-Accurate	2	9.0			Application of traffic topping at various locations.		18.0
10/04/23	Adele DiGirolomo	Black and McDonald	4	9.0			Team began installing hand wells.		36.0
10/04/23	Adele DiGirolomo	UCC Group	3	9.0			Today they worked on Installing forms and grading.		27.0
10/04/23	Adele DiGirolomo	Klaus Multiparking Inc.	2	9.0			Working with the TSSA inspector on the inspection of the car stackers in P2 and P3 / Car stacker work after inspections were complete.		18.0
10/03/23	Adele DiGirolomo	Mizrahi inc. Design-Build	12	9.0			Site Supervisors x PM's x Logistics		108.0



Mizrahi Inc.
125 Hazelton Avenue
Toronto, Ontario M5R 2E4
Canada

Printed on Wed Nov 1, 2023 at 12:05 am EDT

Job #: 1709BB03 The One
2 Bloor Street West
Toronto Ontario. M4W3E2
4169224200

Date	Created By	Company	Workers	Hours	Cost Code	Location	Comments	Attachments	Total Hours
10/03/23	Adele DiGirolomo	Mizrahi inc. Design-Build	8	9.0			Traffic Control + Security: On a daily basis Traffic control assists with deliveries, both scheduled and unscheduled. As well, they provide traffic control for the immediate vicinity. Note: The hours only reflect up to 3:00pm.		72.0
10/03/23	Adele DiGirolomo	Safety First Consulting Professional Corporation	1	9.0					9.0
10/03/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Crane Operator(s)		18.0
10/03/23	Adele DiGirolomo	Mizrahi inc. Design-Build	9	9.0			General Labourers: Today the team performed their standard duties of running the hoists, assisting with deliveries, operating Bobcat and forklift. Cleaning and maintaining washrooms and Covid spraying. Site clean up, garbage removal and any other tasks requested by their Supervisor.		81.0
10/03/23	Adele DiGirolomo	Mizrahi inc. Design-Build	4	9.0			Hoist Operators		36.0
10/03/23	Adele DiGirolomo	Hardwall Construction	65	9.0			Today Hardwall closed Mega walls/Columns 39-40, pouring Level 34-35 elevator walls and poured Level 32 corners. Lastly also received a delivery of materials.		585.0
10/03/23	Adele DiGirolomo	Gamma Windows & Walls International Inc.	17	8.0			Team worked on West V. Wall install, Curtain Wall install on Level 11, Cladding East (Shut Down) Air Seal and lastly, Stack Head / Fire Stop.		136.0
10/03/23	Adele DiGirolomo	ES Fox Constructors Ltd	6	9.0			Team worked on West Bank RCS.		54.0
10/03/23	Adele DiGirolomo	Otis Ltd.	12	8.0			Team continued working on HR frames and LR rails.		96.0
10/03/23	Adele DiGirolomo	Modern Niagara	23	9.0			Team continuing working on Level 16 & 17 riser duct work shaft, Scaffolding on Level 17 West, sleeving as required in walls and slabs ongoing and lastly, material handling.		207.0
10/03/23	Adele DiGirolomo	OZZ Electric Inc.	5	9.0			Team worked on the following: Laying conduit on the Slab ongoing, Level 18 Mechanical, Levels 19 to 33 and on P levels.		45.0
10/03/23	Adele DiGirolomo	Amherst Group	3	9.0			On site assisting with today's pour.		27.0
10/03/23	Adele DiGirolomo	LMB Mechanical	2	9.0			Team continued working on sleeving walls and slab as required, coordination with Modern Niagara , material handling and lastly, scanning and coring holes.		18.0
10/03/23	Adele DiGirolomo	Onyx Sprinklers	2	9.0			Sleeving ongoing, working on elevator shafts and mechanical floors as required and high pressure temporary riser continuing.		18.0
10/03/23	Adele DiGirolomo	Bass Installation	9	9.0			Team worked on Mechanical floor, Level 17th East doing Bottom backpan install, Dutchies removal, L17th West starting and VM & HM install.		81.0
10/03/23	Adele DiGirolomo	United Drywall Limited	5	9.0			Pins for ceiling insulation on underside on L19 / Working on the shaft for duct work at GL1 Elevator lobby on L4 / Housekeeping at various locations / Continuation of wall on L2 south side.		45.0
10/03/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Off duty Police assisting with traffic control at Gates 3 and 4.		18.0
10/03/23	Adele DiGirolomo	GNI Management Group Inc.	2	9.0			Now onto Level 3 and finishing clean up on Level 2.		18.0
10/03/23	Adele DiGirolomo	Clifford Restoration	6	9.0			Continued working on roof top flashing.		54.0
10/03/23	Adele DiGirolomo	Riverside Group	2	9.0			Today the team worked on Level 17 starting framing under the slab.		18.0
10/03/23	Adele DiGirolomo	Bothwell-Accurate	4	9.0			Prepping for traffic topping at various locations.		36.0
10/03/23	Adele DiGirolomo	SCAF-TECH	4	9.0			Team returned to re-work the Yonge St Hoarding.		36.0
10/03/23	Adele DiGirolomo	Black and McDonald	4	9.0			Team preparing for the install and running lines.		36.0
10/02/23	Adele DiGirolomo	Mizrahi inc. Design-Build	14	9.0			Site Supervisors x PM's x Logistics		126.0



Mizrahi Inc.
125 Hazelton Avenue
Toronto, Ontario M5R 2E4
Canada

Printed on Wed Nov 1, 2023 at 12:05 am EDT

Job #: 1709BB03 The One
2 Bloor Street West
Toronto Ontario. M4W3E2
4169224200

Date	Created By	Company	Workers	Hours	Cost Code	Location	Comments	Attachments	Total Hours
10/02/23	Adele DiGirolomo	Mizrahi inc. Design-Build	10	9.0			Traffic Control + Security: On a daily basis Traffic control assists with deliveries, both scheduled and unscheduled. As well, they provide traffic control for the immediate vicinity. Note: The hours only reflect up to 3:00pm.		90.0
10/02/23	Adele DiGirolomo	Safety First Consulting Professional Corporation	1	9.0					9.0
10/02/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Crane Operator(s)		18.0
10/02/23	Adele DiGirolomo	Mizrahi inc. Design-Build	9	9.0			General Labourers: Today the team performed their standard duties of running the hoists, assisting with deliveries, operating Bobcat and forklift. Cleaning and maintaining washrooms and Covid spraying. Site clean up, garbage removal and any other tasks requested by their Supervisor.		81.0
10/02/23	Adele DiGirolomo	Mizrahi inc. Design-Build	4	9.0			Hoist Operators		36.0
10/02/23	Adele DiGirolomo	Hardwall Construction	65	9.0			Today Hardwall poured Level 39 tower slab, closing elevator cages on level 34035, placing steel for Level 32, started forming Level 31 and Level 31 upstand beams.		585.0
10/02/23	Adele DiGirolomo	Gamma Windows & Walls International Inc.	17	8.0			Team worked on West Bank Blueskin, Cladding on the East, Cladding Preparation for Southwest, anchor setting on V.Wall East Return and misc clean up.		136.0
10/02/23	Adele DiGirolomo	ES Fox Constructors Ltd	6	9.0			Team worked on installing plywood and sheet metal on screens.		54.0
10/02/23	Adele DiGirolomo	Otis Ltd.	11	8.0			Team continued working in LR & HR shaft.		88.0
10/02/23	Adele DiGirolomo	Modern Niagara	7	9.0			Team continuing working on Level 16 & 17 riser duct work shaft and material handling. Note: The Plumbing team was not on site due to Federal Stat holiday.		63.0
10/02/23	Adele DiGirolomo	OZZ Electric Inc.	5	9.0			The entire team worked on laying conduit on the Slab.		45.0
10/02/23	Adele DiGirolomo	Amherst Group	3	9.0			On site assisting with today's pour.		27.0
10/02/23	Adele DiGirolomo	LMB Mechanical	2	9.0			Team continued working on sleeving walls and slab as required, coordination with Modern Niagara and material handling.		18.0
10/02/23	Adele DiGirolomo	Onyx Sprinklers	0	9.0			Not on site due to Federal Stat holiday.		0.0
10/02/23	Adele DiGirolomo	Bass Installation	9	9.0			Team worked on Mechanical floor, Installing Curtain Wall and remove duchess. Lastly shake out and applying blueskin.		81.0
10/02/23	Adele DiGirolomo	United Drywall Limited	5	9.0			Taping joints at shaft for emergency gas line / Working on the shaft for duct work at GL1 Elevator lobby on L4 / Housekeeping at various locations.		45.0
10/02/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Off duty Police assisting with traffic control at Gate 3.		18.0
10/02/23	Adele DiGirolomo	GNI Management Group Inc.	2	9.0			Today they cleaned up Level 2 and are now moving onto Level 3.		18.0
10/02/23	Adele DiGirolomo	Clifford Restoration	6	9.0			Today team worked on roof top flashing.		54.0
10/02/23	Adele DiGirolomo	Riverside Group	3	9.0			Continued installing blue skin on Level 6		27.0
10/02/23	Adele DiGirolomo	Bothwell-Accurate	4	9.0			Prepping for traffic topping at various locations.		36.0
10/02/23	Adele DiGirolomo	BlockWall Masonry 18 Inc.	2	9.0			Worked on blocking up Mezzanine and Level 2.		18.0
10/02/23	Adele DiGirolomo	SCAF-TECH	4	9.0			Back on site working on relocating the Hoarding on Yonge St.		36.0
09/29/23	Adele DiGirolomo	Mizrahi inc. Design-Build	13	9.0			Site Supervisors x PM's x Logistics		117.0



Mizrahi Inc.
125 Hazelton Avenue
Toronto, Ontario M5R 2E4
Canada

Printed on Wed Nov 1, 2023 at 12:05 am EDT

Job #: 1709BB03 The One
2 Bloor Street West
Toronto Ontario. M4W3E2
4169224200

Date	Created By	Company	Workers	Hours	Cost Code	Location	Comments	Attachments	Total Hours
09/29/23	Adele DiGirolomo	Mizrahi inc. Design-Build	8	9.0			Traffic Control + Security: On a daily basis Traffic control assists with deliveries, both scheduled and unscheduled. As well, they provide traffic control for the immediate vicinity. Note: The hours only reflect up to 3:00pm.		72.0
09/29/23	Adele DiGirolomo	Safety First Consulting Professional Corporation	1	9.0					9.0
09/29/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Crane Operator(s)		18.0
09/29/23	Adele DiGirolomo	Mizrahi inc. Design-Build	9	9.0			General Labourers: Today the team performed their standard duties of running the hoists, assisting with deliveries, operating Bobcat and forklift. Cleaning and maintaining washrooms and Covid spraying. Site clean up, garbage removal and any other tasks requested by their Supervisor.		81.0
09/29/23	Adele DiGirolomo	Mizrahi inc. Design-Build	4	9.0			Hoist Operators		36.0
09/29/23	Adele DiGirolomo	Hardwall Construction	57	9.0			Today Hardwall placed rebar for Level 39 Tower slab, poured Level 34 Lobby slab and received multiple deliveries.		513.0
09/29/23	Adele DiGirolomo	Gamma Windows & Walls International Inc.	22	8.0			Team worked on West finishing interior V.Wall Southwest air seal, V.Wall blue Skin and stack head multi areas.		176.0
09/29/23	Adele DiGirolomo	ES Fox Constructors Ltd	6	9.0			Team worked on material consolidation clean up.		54.0
09/29/23	Adele DiGirolomo	Otis Ltd.	11	5.0			Team continued working in LR & HR shaft and installing frames.		55.0
09/29/23	Adele DiGirolomo	Modern Niagara	0	9.0			Not on site on Friday's.		0.0
09/29/23	Adele DiGirolomo	OZZ Electric Inc.	10	9.0			Team continued working on laying conduit on the Slab, Level 18 mechanical and P levels.		90.0
09/29/23	Adele DiGirolomo	Amherst Group	3	9.0			On site assisting with today's pour.		27.0
09/29/23	Adele DiGirolomo	LMB Mechanical	2	9.0			This past week the team completed the following: Sleeving on level 39, sleeving on level 32 corner bays, Staging, distribution and planning of materials on 27th - 30th floors.		18.0
09/29/23	Adele DiGirolomo	Onyx Sprinklers	0	9.0			Not on site on Friday's.		0.0
09/29/23	Adele DiGirolomo	Bass Installation	8	9.0			Team worked on Level 17 East elevation, back pans, caulking, Level 17 West side elevation, and shaking out bird screens. Also had their safety rescue plan course earlier today.		72.0
09/29/23	Adele DiGirolomo	United Drywall Limited	4	9.0			Installed drywall on the underside of the gas shaft on L6 / Installing pins for ceiling insulation on underside of L19 / Housekeeping at various locations.		36.0
09/29/23	Adele DiGirolomo	UCC Group	3	9.0			Team continued the digging process for the Silver Cells for installation and debris removal.		27.0
09/29/23	Adele DiGirolomo	Mizrahi inc. Design-Build	1	9.0			Off duty Police assisting with traffic control at Gate 3.		9.0
09/29/23	Adele DiGirolomo	GNI Management Group Inc.	4	9.0			Today the team finished spraying level 2nd, and now moving up to level 3.		36.0
09/29/23	Adele DiGirolomo	Riverside Group	0	9.0			Not on site on Friday's.		0.0
09/28/23	Adele DiGirolomo	Mizrahi inc. Design-Build	14	9.0			Site Supervisors x PM's x Logistics		126.0
09/28/23	Adele DiGirolomo	Mizrahi inc. Design-Build	8	9.0			Traffic Control + Security: On a daily basis Traffic control assists with deliveries, both scheduled and unscheduled. As well, they provide traffic control for the immediate vicinity. Note: The hours only reflect up to 3:00pm.		72.0
09/28/23	Adele DiGirolomo	Safety First Consulting Professional Corporation	1	9.0					9.0
09/28/23	Adele	Mizrahi inc. Design-	2	9.0			Crane Operator(s)		18.0



Mizrahi Inc.
125 Hazelton Avenue
Toronto, Ontario M5R 2E4
Canada

Printed on Wed Nov 1, 2023 at 12:05 am EDT

Job #: 1709BB03 The One
2 Bloor Street West
Toronto Ontario. M4W3E2
4169224200

Date	Created By	Company	Workers	Hours	Cost Code	Location	Comments	Attachments	Total Hours
	DiGirolomo	Build							
09/28/23	Adele DiGirolomo	Mizrahi inc. Design-Build	9	9.0			General Labourers: Today the team performed their standard duties of running the hoists, assisting with deliveries, operating Bobcat and forklift. Cleaning and maintaining washrooms and Covid spraying. Site clean up, garbage removal and any other tasks requested by their Supervisor.		81.0
09/28/23	Adele DiGirolomo	Mizrahi inc. Design-Build	4	9.0			Hoist Operators		36.0
09/28/23	Adele DiGirolomo	Hardwall Construction	57	9.0			Today Hardwall placed rebar for Level 39 tower slab, pouring remainder of transfer beams, placing rebar for Live 34 lobby slab and cages. Finishing up deck for Level 32 corners and received delivery from Salit.		513.0
09/28/23	Adele DiGirolomo	Gamma Windows & Walls International Inc.	22	8.0			Team worked on Cladding W/ Finishing , V.Wall interior, Shake out on Level 11, Southwest air seal , West Blue Skin, and Misc air seal on Level 3.		176.0
09/28/23	Adele DiGirolomo	ES Fox Constructors Ltd	6	9.0			Team removed suspension shoes , burning extra beams in the shaft and maintenance platforms.		54.0
09/28/23	Adele DiGirolomo	Otis Ltd.	11	8.0			Team focused on working in LR & HR shaft and installing frames.		88.0
09/28/23	Adele DiGirolomo	Modern Niagara	25	9.0			Team continuing working on Level 16 & 17 riser duct work shaft, S.I work on Levels 4 & 5, Scaffolding on Level 17 West has commenced, sleeving as required in walls and slabs ongoing and lastly, material handling.		225.0
09/28/23	Adele DiGirolomo	OZZ Electric Inc.	10	9.0			Team focused on laying conduit on the Slab, Level 18 mechanical and P levels.		90.0
09/28/23	Adele DiGirolomo	Amherst Group	3	9.0			On site assisting with today's pour.		27.0
09/28/23	Adele DiGirolomo	LMB Mechanical	2	9.0			Team continued working on sleeving walls and slab as required, coordination with Modern Niagara and material handling.		18.0
09/28/23	Adele DiGirolomo	Onyx Sprinklers	2	9.0			Team continued working on high pressure temporary riser on Level 15, continuing and ongoing sleeving on the slab as needed.		18.0
09/28/23	Adele DiGirolomo	Bass Installation	8	9.0			Team worked on Level 17 East elevation, back pans, caulking, Level 17 West side elevation, and shaking out bird screens.		72.0
09/28/23	Adele DiGirolomo	United Drywall Limited	5	9.0			Framed wall on 1M near Stair G / Installing pins for ceiling insulation on underside of L19 / Completed framing of north wall on L4 podium / Housekeeping at various locations / Installed fire rated plywood at yonge street facade.		45.0
09/28/23	Adele DiGirolomo	UCC Group	3	9.0			Today the team worked on stripping the concrete forms and digging for the Silver Cells for installation.		27.0
09/28/23	Adele DiGirolomo	Mizrahi inc. Design-Build	1	9.0			Off duty Police assisting with traffic control at Gate 3.		9.0
09/28/23	Adele DiGirolomo	GNI Management Group Inc.	4	9.0			Continued Fireproofing on level 2.		36.0
09/28/23	Adele DiGirolomo	Clifford Restoration	3	9.0			Today team focused on Chimney, finishing bricks and flashing.		27.0
09/28/23	Adele DiGirolomo	Riverside Group	3	9.0			Continued installing blue skin on Level 6		27.0
09/28/23	Adele DiGirolomo	KRCMAR	1	9.0			Back on site shooting elevators and slabs. Slab edge Level 25, elevators & megas on Level 16.		9.0
09/27/23	Adele DiGirolomo	Mizrahi inc. Design-Build	14	9.0			Site Supervisors x PM's x Logistics		126.0
09/27/23	Adele DiGirolomo	Mizrahi inc. Design-Build	8	9.0			Traffic Control + Security: On a daily basis Traffic control assists with deliveries, both scheduled and unscheduled. As well, they provide traffic control for the immediate vicinity. Note: The hours only reflect up to 3:00pm.		72.0
09/27/23	Adele DiGirolomo	Safety First Consulting Professional Corporation	1	9.0					9.0
09/27/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Crane Operator(s)		18.0



Mizrahi Inc.
125 Hazelton Avenue
Toronto, Ontario M5R 2E4
Canada

Printed on Wed Nov 1, 2023 at 12:05 am EDT

Job #: 1709BB03 The One
2 Bloor Street West
Toronto Ontario. M4W3E2
4169224200

Date	Created By	Company	Workers	Hours	Cost Code	Location	Comments	Attachments	Total Hours
09/27/23	Adele DiGirolomo	Mizrahi inc. Design-Build	9	9.0			General Labourers: Today the team performed their standard duties of running the hoists, assisting with deliveries, operating Bobcat and forklift. Cleaning and maintaining washrooms and Covid spraying. Site clean up, garbage removal and any other tasks requested by their Supervisor.		81.0
09/27/23	Adele DiGirolomo	Mizrahi inc. Design-Build	4	9.0			Hoist Operators		36.0
09/27/23	Adele DiGirolomo	Hardwall Construction	57	9.0			Today Hardwall poured 1/4 of the transfer beams/ finishing rebar for remainder of t-beams on Level 39, started rebar for Level 39 Tower slab. They started laying rebar for Level 34 lobby slab and landing elevator cages. Lastly, they finished raising corner screens and building deck for Level 32 corners.		513.0
09/27/23	Adele DiGirolomo	Gamma Windows & Walls International Inc.	20	8.0			Team worked on Curtain Wall install SouthWest core Blue skin, interior V. Wall, South air seal / Southeast V.Wall anchors.		160.0
09/27/23	Adele DiGirolomo	ES Fox Constructors Ltd	6	9.0			Team fixed up and adjusted the trolleys. Removed climbing cones, recycled suspension shoes, cleaned cup strit bases and set up for future jumps.		54.0
09/27/23	Adele DiGirolomo	Otis Ltd.	11	8.0			Team focused on installing frames a Skybuild.		88.0
09/27/23	Adele DiGirolomo	Modern Niagara	25	9.0			Team continuing working on Level 16 & 17 riser duct work shaft, S.I work on Levels 4 & 5, Scaffolding on Level 17 West has commenced, sleeving as required in walls and slabs ongoing and lastly, material handling.		225.0
09/27/23	Adele DiGirolomo	OZZ Electric Inc.	10	9.0			Team focused on laying conduit on the Slab, Level 18 mechanical, P levels and tied in Pigtails on level 19 for Bass and on Level 2 for GNI.		90.0
09/27/23	Adele DiGirolomo	Amherst Group	3	9.0			On site preparing for tomorrow's pour.		27.0
09/27/23	Adele DiGirolomo	LMB Mechanical	2	9.0			Team continued working on sleeving walls and slab as required, coordination with Modern Niagara and material handling.		18.0
09/27/23	Adele DiGirolomo	Onyx Sprinklers	2	9.0			Team continued working on high pressure temporary riser continuing and ongoing sleeving on the slab as needed.		18.0
09/27/23	Adele DiGirolomo	Bass Installation	8	9.0			Team worked on 17th floor East elevation, Back pans, & caulking as well as Level 17 west elevation.		72.0
09/27/23	Adele DiGirolomo	United Drywall Limited	5	9.0			Caulking at shaft wall on L4 at the south side of the podium for ductwork / Installing pins for ceiling insulation on underside of L19 / Installing wall studs in between Stair F and G / Housekeeping at various locations.		45.0
09/27/23	Adele DiGirolomo	UCC Group	3	9.0			Poured curbs today at 7am from the West side to half to East.		27.0
09/27/23	Adele DiGirolomo	Mizrahi inc. Design-Build	1	9.0			Off duty Police assisting with traffic control at Gate 3.		9.0
09/27/23	Adele DiGirolomo	GNI Management Group Inc.	4	9.0			Continued Fireproofing on level 2.		36.0
09/27/23	Adele DiGirolomo	Clifford Restoration	3	9.0			Today team focused on building the chimney and side walls.		27.0
09/27/23	Adele DiGirolomo	Federal Wireless	3	9.0			Team started running cable from Level 4 down to Level 3.		27.0
09/27/23	Adele DiGirolomo	Riverside Group	3	9.0			Back on site and installed blue skin on Level 19 West , East and North sides.		27.0
09/26/23	Adele DiGirolomo	Mizrahi inc. Design-Build	14	9.0			Site Supervisors x PM's x Logistics		126.0
09/26/23	Adele DiGirolomo	Mizrahi inc. Design-Build	8	9.0			Traffic Control + Security: On a daily basis Traffic control assists with deliveries, both scheduled and unscheduled. As well, they provide traffic control for the immediate vicinity. Note: The hours only reflect up to 3:00pm.		72.0
09/26/23	Adele DiGirolomo	Safety First Consulting Professional Corporation	1	9.0					9.0
09/26/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Crane Operator(s)		18.0
09/26/23	Adele DiGirolomo	Mizrahi inc. Design-Build	9	9.0			General Labourers: Today the team performed their standard duties of running the hoists, assisting with deliveries, operating Bobcat and forklift. Cleaning and maintaining washrooms and Covid spraying. Site clean up, garbage removal and any other tasks requested by their Supervisor.		81.0



Mizrahi Inc.
125 Hazelton Avenue
Toronto, Ontario M5R 2E4
Canada

Printed on Wed Nov 1, 2023 at 12:05 am EDT

Job #: 1709BB03 The One
2 Bloor Street West
Toronto Ontario. M4W3E2
4169224200

Date	Created By	Company	Workers	Hours	Cost Code	Location	Comments	Attachments	Total Hours
09/26/23	Adele DiGirolomo	Mizrahi inc. Design-Build	4	9.0			Hoist Operators		36.0
09/26/23	Adele DiGirolomo	Hardwall Construction	57	9.0			Today Hardwall worked on built deck level 32 corner slabs, built deck level 34 lobby slab, placing rebar level 39 beams and received delivery from Salit.		513.0
09/26/23	Adele DiGirolomo	Gamma Windows & Walls International Inc.	19	8.0			Team worked on West Core west face, West core interior / return North Clean / Cladding Southwest Curtain Wall and blue skin on the West Bank wall.		152.0
09/26/23	Adele DiGirolomo	ES Fox Constructors Ltd	6	9.0			Team jumped the North Side from Level 9 to 10 this morning. Then continued welding on the west truss, windlocks on the east side and moving shoes as requested by Bass.		54.0
09/26/23	Adele DiGirolomo	Otis Ltd.	11	8.0			Team focused on installing frames at HR 7th floor moving up.		88.0
09/26/23	Adele DiGirolomo	Modern Niagara	25	9.0			Team continuing working on Level 16 & 17 riser duct work shaft, S.I work on Levels 4 & 5, Scaffolding on Level 17 West has commenced, sleeving as required in walls and slabs ongoing and lastly, material handling.		225.0
09/26/23	Adele DiGirolomo	OZZ Electric Inc.	10	9.0			Team focused on laying conduit on the Slab, Level 18 mechanical, P levels and tied in Pigtales on level 19 for Bass and on Level 2 for GNI.		90.0
09/26/23	Adele DiGirolomo	Amherst Group	3	9.0			On site preparing for tomorrow's pour.		27.0
09/26/23	Adele DiGirolomo	LMB Mechanical	2	9.0			Team continued working on sleeving walls and slab as required, coordination with Modern Niagara and material handling.		18.0
09/26/23	Adele DiGirolomo	Onyx Sprinklers	2	9.0			Team continued working on high pressure temporary riser continuing and ongoing sleeving on the slab as needed.		18.0
09/26/23	Adele DiGirolomo	Bass Installation	8	9.0			Team worked on level 17 East side, Caulking back pans, level 17th West, building and mobilizing swing stage and preparing for large delivery this evening.		72.0
09/26/23	Adele DiGirolomo	United Drywall Limited	5	9.0			Shaft wall work on L4 at the south side of the podium for ductwork / Installing pins for ceiling insulation on underside of L19 / Installed dense glass at the exterior of the Yonge Street Facade on L3 / Housekeeping at various locations.		45.0
09/26/23	Adele DiGirolomo	UCC Group	0	9.0			Not on site due to RCS jump overhead.		0.0
09/26/23	Adele DiGirolomo	Mizrahi inc. Design-Build	1	9.0			Off duty Police assisting with traffic control at Gate 3.		9.0
09/26/23	Adele DiGirolomo	GNI Management Group Inc.	3	9.0			Fireproofing on level 2 and moving up to level 3.		27.0
09/26/23	Adele DiGirolomo	Walters Inc.	4	9.0			Tier 6 struts now installed. Team worked on bolting and torquing.		36.0
09/26/23	Adele DiGirolomo	Klaus Multiparking Inc.	3	9.0			On site for inspections of the stacker Installations, with (2) TSSA inspectors on site.		27.0
09/26/23	Adele DiGirolomo	Clifford Restoration	4	9.0			Team has returned and started to remove the chimney and rebuild it up and starting the flashing detail at the rooftop.		36.0
09/26/23	Adele DiGirolomo	Federal Wireless	2	9.0			Team started to install wiring for radio communications to climb with the tower.		18.0
09/26/23	Adele DiGirolomo	Handverk Design	2	9.0			On site installing new vinyl panels on the exterior of the pump station.		18.0
09/25/23	Adele DiGirolomo	Mizrahi inc. Design-Build	10	9.0			Site Supervisors x PM's x Logistics		90.0
09/25/23	Adele DiGirolomo	Mizrahi inc. Design-Build	8	9.0			Traffic Control + Security: On a daily basis Traffic control assists with deliveries, both scheduled and unscheduled. As well, they provide traffic control for the immediate vicinity. Note: The hours only reflect up to 3:00pm.		72.0
09/25/23	Adele DiGirolomo	Safety First Consulting Professional Corporation	1	9.0					9.0
09/25/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Crane Operator(s)		18.0



Mizrahi Inc.
125 Hazelton Avenue
Toronto, Ontario M5R 2E4
Canada

Printed on Wed Nov 1, 2023 at 12:05 am EDT

Job #: 1709BB03 The One
2 Bloor Street West
Toronto Ontario. M4W3E2
4169224200

Date	Created By	Company	Workers	Hours	Cost Code	Location	Comments	Attachments	Total Hours
09/25/23	Adele DiGirolomo	Mizrahi inc. Design-Build	9	9.0			General Labourers: Today the team performed their standard duties of running the hoists, assisting with deliveries, operating Bobcat and forklift. Cleaning and maintaining washrooms and Covid spraying. Site clean up, garbage removal and any other tasks requested by their Supervisor.		81.0
09/25/23	Adele DiGirolomo	Mizrahi inc. Design-Build	4	9.0			Hoist Operators		36.0
09/25/23	Adele DiGirolomo	Hardwall Construction	57	9.0			Today Hardwall worked on decking lobby slab on level 34, decking tower slab on level 39, placing rebar for level 39 beams and lastly receiving and returning materials.		513.0
09/25/23	Adele DiGirolomo	Gamma Windows & Walls International Inc.	19	8.0			Team worked on Curtain Wall Panel finish southwest stage move to the S. V. Wall west gear up Interior shake out.		152.0
09/25/23	Adele DiGirolomo	ES Fox Constructors Ltd	6	9.0			Team focused on preparing for tomorrow's jump north side, welding on the west truss, as well as windlocks on the east side.		54.0
09/25/23	Adele DiGirolomo	Otis Ltd.	11	8.0			Team focused on installing frames on Level 7 and working on LR- Hotel.		88.0
09/25/23	Adele DiGirolomo	Modern Niagara	25	9.0			Team continuing working on Level 16 & 17 riser duct work shaft, S.I work on Levels 4 & 5, Scaffolding on Level 17 West has commenced, sleeving as required in walls and slabs ongoing and lastly, material handling.		225.0
09/25/23	Adele DiGirolomo	OZZ Electric Inc.	10	9.0			Team focused on laying conduit on the Slab, Level 18 mechanical and P levels.		90.0
09/25/23	Adele DiGirolomo	Amherst Group	0	9.0			Not on site today		0.0
09/25/23	Adele DiGirolomo	LMB Mechanical	2	9.0			Team continued working on sleeving walls and slab as required, coordination with Modern Niagara and material handling.		18.0
09/25/23	Adele DiGirolomo	Onyx Sprinklers	2	9.0			Team continued working on P1 valve, high pressure temporary riser continuing and ongoing sleeving on the slab as needed.		18.0
09/25/23	Adele DiGirolomo	Bass Installation	8	9.0			Team worked on level 17 East side, Caulking back pans, level 17th West, building and mobilizing swing stage.		72.0
09/25/23	Adele DiGirolomo	United Drywall Limited	5	9.0			Housekeeping at various locations / Shaft wall work on L4 at the south side of the podium for ductwork / Installing pins for ceiling insulation on underside of L19.		45.0
09/25/23	Adele DiGirolomo	UCC Group	4	9.0			Team continued installing silver cells.		36.0
09/25/23	Adele DiGirolomo	Mizrahi inc. Design-Build	1	9.0			Off duty Police assisting with traffic control at Gate 3.		9.0
09/25/23	Adele DiGirolomo	GNI Management Group Inc.	3	9.0			Fireproofing now complete in the heritage building and have moved over to level 2 and setting up .		27.0
09/25/23	Adele DiGirolomo	SCAF-TECH	2	9.0			On site to remove material.		18.0
09/25/23	Adele DiGirolomo	Walters Inc.	4	9.0			Continued working on the Tier 6 steel strut installation		36.0
09/25/23	Adele DiGirolomo	Sunbrite Drapery	2	9.0			Installing blinds at the mock up suite.		18.0
09/25/23	Adele DiGirolomo	McIntosh Perry	1	9.0			On site inspections for various locations.		9.0
09/22/23	Adele DiGirolomo	Mizrahi inc. Design-Build	15	9.0			Site Supervisors x PM's x Logistics		135.0
09/22/23	Adele DiGirolomo	Mizrahi inc. Design-Build	8	9.0			Traffic Control + Security: On a daily basis Traffic control assists with deliveries, both scheduled and unscheduled. As well, they provide traffic control for the immediate vicinity. Note: The hours only reflect up to 3:00pm.		72.0
09/22/23	Adele DiGirolomo	Safety First Consulting Professional Corporation	1	9.0					9.0
09/22/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Crane Operator(s)		18.0



Mizrahi Inc.
125 Hazelton Avenue
Toronto, Ontario M5R 2E4
Canada

Printed on Wed Nov 1, 2023 at 12:05 am EDT

Job #: 1709BB03 The One
2 Bloor Street West
Toronto Ontario. M4W3E2
4169224200

Date	Created By	Company	Workers	Hours	Cost Code	Location	Comments	Attachments	Total Hours
09/22/23	Adele DiGirolomo	Mizrahi inc. Design-Build	9	9.0			General Labourers: Today the team performed their standard duties of running the hoists, assisting with deliveries, operating Bobcat and forklift. Cleaning and maintaining washrooms and Covid spraying. Site clean up, garbage removal and any other tasks requested by their Supervisor.		81.0
09/22/23	Adele DiGirolomo	Mizrahi inc. Design-Build	4	9.0			Hoist Operators		36.0
09/22/23	Adele DiGirolomo	Hardwall Construction	57	9.0			Today Hardwall continued decking for Level 39, stripped interior elevator cages, preparing to start deck and material handling.		513.0
09/22/23	Adele DiGirolomo	Gamma Windows & Walls International Inc.	23	8.0			Team worked on Curtain Wall install Level 9, Cladding Finishing Southwest side, Cladding replacement Northwest Mega, stack head pre work and Stage set up.		184.0
09/22/23	Adele DiGirolomo	ES Fox Constructors Ltd	7	9.0			Team worked on installing Suspension shoes West side and jumped the RCS on the east side.		63.0
09/22/23	Adele DiGirolomo	Otis Ltd.	11	8.0			Team continued with installing LR shaft with rails.		88.0
09/22/23	Adele DiGirolomo	Modern Niagara	0	9.0			Not on site on Friday's.		0.0
09/22/23	Adele DiGirolomo	OZZ Electric Inc.	10	9.0			Team focused on laying conduit on the Slab, Level 18 mechanical, P levels and material handling.		90.0
09/22/23	Adele DiGirolomo	Amherst Group	3	9.0			On site servicing pump station.		27.0
09/22/23	Adele DiGirolomo	LMB Mechanical	2	9.0			Team continued working on sleeving walls and slab as required, coordination with Modern Niagara and material handling.		18.0
09/22/23	Adele DiGirolomo	Onyx Sprinklers	0	9.0			Not on site on Friday's.		0.0
09/22/23	Adele DiGirolomo	Bass Installation	8	9.0			Team worked on Gamma install on Level 10 and layout on Level 13.		72.0
09/22/23	Adele DiGirolomo	United Drywall Limited	6	9.0			Housekeeping at various locations / Elevator shaft installs on L12 and L10 for HR-05 and HR-08 / Installed flashing at Heritage column Ground Floor.		54.0
09/22/23	Adele DiGirolomo	UCC Group	4	9.0			Team delivered Strut Soil today and installed 1 foot lift.		36.0
09/22/23	Adele DiGirolomo	Mizrahi inc. Design-Build	1	9.0			Off duty Police assisting with traffic control at Gate 3.		9.0
09/22/23	Adele DiGirolomo	GNI Management Group Inc.	3	9.0			Team worked on masking Level 2.		27.0
09/22/23	Adele DiGirolomo	SCAF-TECH	5	9.0			Completed the installation of the scaffolding on the North West corner of L17.		45.0
09/22/23	Adele DiGirolomo	Turbo	2	9.0			Back on site scanning & coring the West Bank area, holes are 2 at 4inch		18.0
09/21/23	Adele DiGirolomo	Mizrahi inc. Design-Build	15	9.0			Site Supervisors x PM's x Logistics		135.0
09/21/23	Adele DiGirolomo	Mizrahi inc. Design-Build	8	9.0			Traffic Control + Security: On a daily basis Traffic control assists with deliveries, both scheduled and unscheduled. As well, they provide traffic control for the immediate vicinity. Note: The hours only reflect up to 3:00pm.		72.0
09/21/23	Adele DiGirolomo	Safety First Consulting Professional Corporation	1	9.0					9.0
09/21/23	Adele DiGirolomo	Mizrahi inc. Design-Build	2	9.0			Crane Operator(s)		18.0
09/21/23	Adele DiGirolomo	Mizrahi inc. Design-Build	9	9.0			General Labourers: Today the team performed their standard duties of running the hoists, assisting with deliveries, operating Bobcat and forklift. Cleaning and maintaining washrooms and Covid spraying. Site clean up, garbage removal and any other tasks requested by their Supervisor.		81.0
09/21/23	Adele DiGirolomo	Mizrahi inc. Design-Build	4	9.0			Hoist Operators		36.0



Mizrahi Inc.
125 Hazelton Avenue
Toronto, Ontario M5R 2E4
Canada

Printed on Wed Nov 1, 2023 at 12:05 am EDT

Job #: 1709BB03 The One
2 Bloor Street West
Toronto Ontario. M4W3E2
4169224200

Date	Created By	Company	Workers	Hours	Cost Code	Location	Comments	Attachments	Total Hours
09/21/23	Adele DiGirolomo	Hardwall Construction	57	9.0			Today Hardwall continued decking for Level 39, closed and poured Level 33 to 34 elevator walls, Poured Level 31 upstanding beams and material handling.		513.0
09/21/23	Adele DiGirolomo	Gamma Windows & Walls International Inc.	19	8.0			Team worked on V. Wall anchors, Curtain Wall Install on Level 9 North West, Finishing up Cladding on South West and lastly V.Wall panel.		152.0
09/21/23	Adele DiGirolomo	ES Fox Constructors Ltd	6	9.0			Team focused on cutting beams at elevator fronts, relocating Struts from 10th to 12th floor and installing Suspension shoes on West side for next climb.		54.0
09/21/23	Adele DiGirolomo	Otis Ltd.	11	8.0			Team focused on installing LR shaft with rails.		88.0
09/21/23	Adele DiGirolomo	Modern Niagara	25	9.0			Team continuing working on Level 16 & 17 riser duct work shaft, S.I work on Levels 4 & 5, Scaffolding on Level 17 West has commenced, sleeving as required in walls and slabs ongoing and lastly, material handling.		225.0
09/21/23	Adele DiGirolomo	OZZ Electric Inc.	10	9.0			Team focused on laying conduit on the Slab, Level 18 mechanical, P levels and on landscaping.		90.0
09/21/23	Adele DiGirolomo	Amherst Group	3	9.0			On site assisting with today's pour.		27.0
09/21/23	Adele DiGirolomo	LMB Mechanical	2	9.0			Team continued working on sleeving walls and slab as required, coordination with Modern Niagara and material handling.		18.0
09/21/23	Adele DiGirolomo	Onyx Sprinklers	2	9.0			Team continued working on P1 valve, high pressure temporary riser continuing and ongoing sleeving on the slab as needed.		18.0
09/21/23	Adele DiGirolomo	Bass Installation	6	9.0			Team worked on Level 17 Mechanical, Installing 10th floor for Gamma 5 and lastly, layout on level 13.		54.0
09/21/23	Adele DiGirolomo	United Drywall Limited	6	9.0			Shaft wall assembly for Elevators SH1, SH2 and SH3 / Housekeeping at various locations / Elevator shaft installs on L13 for HR-06 and HR-07 / sanding walls and ceilings at Elevator Lobbies in the parking levels.		54.0
09/21/23	Adele DiGirolomo	UCC Group	4	9.0			Team continued installing silver cells.		36.0
09/21/23	Adele DiGirolomo	Mizrahi inc. Design-Build	1	9.0			Off duty Police assisting with traffic control at Gate 3.		9.0
09/21/23	Adele DiGirolomo	GNI Management Group Inc.	3	9.0			Back on site and fire proofing Heritage area.		27.0
09/21/23	Adele DiGirolomo	SCAF-TECH	5	9.0			Installing scaffolding on the North West corner of L17.		45.0



MIZRAHI

DESIGN / BUILD

APPENDIX F

MONTHLY HEALTH AND SAFETY REPORT



Site 1 Bloor St West

Date: October 2023

Number of Site Orientations	51	
Number of Safety First Inspections	25	September 16, 2022 - October 15, 2023
Safety Item	This Month	Total to Date
First Aids	1	24
Medical Aids	0	25
Critical Injuries	0	0
Near Misses	1	40
Other Incidents	0	49
MOL Visits	1	20
MOECC Visits	0	1
JHSC Meeting Held	1	40
WTC Meeting Held	1	32

Notes

JHSC and WTC meetings were held on October 5th, 2023. First aid: worker cut his finger moving a cable. First Aid done on site, no lost time. Near Miss/MOL visit: Shoring Jack fell to 2 Bloor Street, investigation and corrective actions done.

Notes

Site documentation must be submitted to the safety office each week:

- Minimum of 1 Daily Crew Safety Talk completed each day
- Minimum of 1 Toolbox Talk per week

Company	Daily Crew Safety Talks Completed (Total)	Weekly Toolbox Talks Completed
Blockwall	0	0
Bothwell Accurate	0	0
Clonard	26	4
Elembe (LMB) Mechanical Ltd.	23	4
Gamma	27	4
Hardwall	25	4
Mizrahi	0	4
Modern Niagara	23	4
Onyx	23	4
Otis	33	4
OZZ	23	4
Riverside	0	0
United Drywall	20	4
Walters	0	0
Total	223	44



MIZRAHI

DESIGN / BUILD

APPENDIX G

ID	Task Name	Duration	Start	Finish	Resource Names	Predecessors																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															
							'23 Jun 28 04 11 18 25	'23 Jul 02 09 16 23 30	'23 Aug 06 13 20 27	'23 Sep 03 10 17 24	'23 Oct 01 08 15 22	'23 Nov 29 05 12 19 26	'23 Dec 03 10 17 24	'24 Jan 31 07 14 21 28	'24 Feb 04 11 18 25	'24 Mar 02 09 16 23 30	'24 Apr 06 13 20 27	'24 May 03 10 17 24	'24 Jun 01 08 15 22	'24 Jul 29 05 12 19 26	'24 Aug 03 10 17 24	'24 Sep 01 08 15 22	'24 Oct 29 05 12 19 26	'24 Nov 03 10 17 24	'24 Dec 01 08 15 22	'25 Jan 29 05 12 19 26	'25 Feb 03 10 17 24	'25 Mar 01 08 15 22	'25 Apr 29 05 12 19 26	'25 May 03 10 17 24	'25 Jun 01 08 15 22	'25 Jul 29 05 12 19 26	'25 Aug 03 10 17 24	'25 Sep 01 08 15 22	'25 Oct 29 05 12 19 26	'25 Nov 03 10 17 24	'25 Dec 01 08 15 22	'26 Jan 29 05 12 19 26	'26 Feb 03 10 17 24	'26 Mar 01 08 15 22	'26 Apr 29 05 12 19 26	'26 May 03 10 17 24	'26 Jun 01 08 15 22	'26 Jul 29 05 12 19 26	'26 Aug 03 10 17 24	'26 Sep 01 08 15 22	'26 Oct 29 05 12 19 26	'26 Nov 03 10 17 24	'26 Dec 01 08 15 22	'27 Jan 29 05 12 19 26	'27 Feb 03 10 17 24	'27 Mar 01 08 15 22	'27 Apr 29 05 12 19 26	'27 May 03 10 17 24	'27 Jun 01 08 15 22	'27 Jul 29 05 12 19 26	'27 Aug 03 10 17 24	'27 Sep 01 08 15 22	'27 Oct 29 05 12 19 26	'27 Nov 03 10 17 24	'27 Dec 01 08 15 22	'28 Jan 29 05 12 19 26	'28 Feb 03 10 17 24	'28 Mar 01 08 15 22	'28 Apr 29 05 12 19 26	'28 May 03 10 17 24	'28 Jun 01 08 15 22	'28 Jul 29 05 12 19 26	'28 Aug 03 10 17 24	'28 Sep 01 08 15 22	'28 Oct 29 05 12 19 26	'28 Nov 03 10 17 24	'28 Dec 01 08 15 22	'29 Jan 29 05 12 19 26	'29 Feb 03 10 17 24	'29 Mar 01 08 15 22	'29 Apr 29 05 12 19 26	'29 May 03 10 17 24	'29 Jun 01 08 15 22	'29 Jul 29 05 12 19 26	'29 Aug 03 10 17 24	'29 Sep 01 08 15 22	'29 Oct 29 05 12 19 26	'29 Nov 03 10 17 24	'29 Dec 01 08 15 22	'30 Jan 29 05 12 19 26	'30 Feb 03 10 17 24	'30 Mar 01 08 15 22	'30 Apr 29 05 12 19 26	'30 May 03 10 17 24	'30 Jun 01 08 15 22	'30 Jul 29 05 12 19 26	'30 Aug 03 10 17 24	'30 Sep 01 08 15 22	'30 Oct 29 05 12 19 26	'30 Nov 03 10 17 24	'30 Dec 01 08 15 22	'31 Jan 29 05 12 19 26	'31 Feb 03 10 17 24	'31 Mar 01 08 15 22	'31 Apr 29 05 12 19 26	'31 May 03 10 17 24	'31 Jun 01 08 15 22	'31 Jul 29 05 12 19 26	'31 Aug 03 10 17 24	'31 Sep 01 08 15 22	'31 Oct 29 05 12 19 26	'31 Nov 03 10 17 24	'31 Dec 01 08 15 22	'32 Jan 29 05 12 19 26	'32 Feb 03 10 17 24	'32 Mar 01 08 15 22	'32 Apr 29 05 12 19 26	'32 May 03 10 17 24	'32 Jun 01 08 15 22	'32 Jul 29 05 12 19 26	'32 Aug 03 10 17 24	'32 Sep 01 08 15 22	'32 Oct 29 05 12 19 26	'32 Nov 03 10 17 24	'32 Dec 01 08 15 22	'33 Jan 29 05 12 19 26	'33 Feb 03 10 17 24	'33 Mar 01 08 15 22	'33 Apr 29 05 12 19 26	'33 May 03 10 17 24	'33 Jun 01 08 15 22	'33 Jul 29 05 12 19 26	'33 Aug 03 10 17 24	'33 Sep 01 08 15 22	'33 Oct 29 05 12 19 26	'33 Nov 03 10 17 24	'33 Dec 01 08 15 22	'34 Jan 29 05 12 19 26	'34 Feb 03 10 17 24	'34 Mar 01 08 15 22	'34 Apr 29 05 12 19 26	'34 May 03 10 17 24	'34 Jun 01 08 15 22	'34 Jul 29 05 12 19 26	'34 Aug 03 10 17 24	'34 Sep 01 08 15 22	'34 Oct 29 05 12 19 26	'34 Nov 03 10 17 24	'34 Dec 01 08 15 22	'35 Jan 29 05 12 19 26	'35 Feb 03 10 17 24	'35 Mar 01 08 15 22	'35 Apr 29 05 12 19 26	'35 May 03 10 17 24	'35 Jun 01 08 15 22	'35 Jul 29 05 12 19 26	'35 Aug 03 10 17 24	'35 Sep 01 08 15 22	'35 Oct 29 05 12 19 26	'35 Nov 03 10 17 24	'35 Dec 01 08 15 22	'36 Jan 29 05 12 19 26	'36 Feb 03 10 17 24	'36 Mar 01 08 15 22	'36 Apr 29 05 12 19 26	'36 May 03 10 17 24	'36 Jun 01 08 15 22	'36 Jul 29 05 12 19 26	'36 Aug 03 10 17 24	'36 Sep 01 08 15 22	'36 Oct 29 05 12 19 26	'36 Nov 03 10 17 24	'36 Dec 01 08 15 22	'37 Jan 29 05 12 19 26	'37 Feb 03 10 17 24	'37 Mar 01 08 15 22	'37 Apr 29 05 12 19 26	'37 May 03 10 17 24	'37 Jun 01 08 15 22	'37 Jul 29 05 12 19 26	'37 Aug 03 10 17 24	'37 Sep 01 08 15 22	'37 Oct 29 05 12 19 26	'37 Nov 03 10 17 24	'37 Dec 01 08 15 22	'38 Jan 29 05 12 19 26	'38 Feb 03 10 17 24	'38 Mar 01 08 15 22	'38 Apr 29 05 12 19 26	'38 May 03 10 17 24	'38 Jun 01 08 15 22	'38 Jul 29 05 12 19 26	'38 Aug 03 10 17 24	'38 Sep 01 08 15 22	'38 Oct 29 05 12 19 26	'38 Nov 03 10 17 24	'38 Dec 01 08 15 22	'39 Jan 29 05 12 19 26	'39 Feb 03 10 17 24	'39 Mar 01 08 15 22	'39 Apr 29 05 12 19 26	'39 May 03 10 17 24	'39 Jun 01 08 15 22	'39 Jul 29 05 12 19 26	'39 Aug 03 10 17 24	'39 Sep 01 08 15 22	'39 Oct 29 05 12 19 26	'39 Nov 03 10 17 24	'39 Dec 01 08 15 22	'40 Jan 29 05 12 19 26	'40 Feb 03 10 17 24	'40 Mar 01 08 15 22	'40 Apr 29 05 12 19 26	'40 May 03 10 17 24	'40 Jun 01 08 15 22	'40 Jul 29 05 12 19 26	'40 Aug 03 10 17 24	'40 Sep 01 08 15 22	'40 Oct 29 05 12 19 26	'40 Nov 03 10 17 24	'40 Dec 01 08 15 22	'41 Jan 29 05 12 19 26	'41 Feb 03 10 17 24	'41 Mar 01 08 15 22	'41 Apr 29 05 12 19 26	'41 May 03 10 17 24	'41 Jun 01 08 15 22	'41 Jul 29 05 12 19 26	'41 Aug 03 10 17 24	'41 Sep 01 08 15 22	'41 Oct 29 05 12 19 26	'41 Nov 03 10 17 24	'41 Dec 01 08 15 22	'42 Jan 29 05 12 19 26	'42 Feb 03 10 17 24	'42 Mar 01 08 15 22	'42 Apr 29 05 12 19 26	'42 May 03 10 17 24	'42 Jun 01 08 15 22	'42 Jul 29 05 12 19 26	'42 Aug 03 10 17 24	'42 Sep 01 08 15 22	'42 Oct 29 05 12 19 26	'42 Nov 03 10 17 24	'42 Dec 01 08 15 22	'43 Jan 29 05 12 19 26	'43 Feb 03 10 17 24	'43 Mar 01 08 15 22	'43 Apr 29 05 12 19 26	'43 May 03 10 17 24	'43 Jun 01 08 15 22	'43 Jul 29 05 12 19 26	'43 Aug 03 10 17 24	'43 Sep 01 08 15 22	'43 Oct 29 05 12 19 26	'43 Nov 03 10 17 24	'43 Dec 01 08 15 22	'44 Jan 29 05 12 19 26	'44 Feb 03 10 17 24	'44 Mar 01 08 15 22	'44 Apr 29 05 12 19 26	'44 May 03 10 17 24	'44 Jun 01 08 15 22	'44 Jul 29 05 12 19 26	'44 Aug 03 10 17 24	'44 Sep 01 08 15 22	'44 Oct 29 05 12 19 26	'44 Nov 03 10 17 24	'44 Dec 01 08 15 22	'45 Jan 29 05 12 19 26	'45 Feb 03 10 17 24	'45 Mar 01 08 15 22	'45 Apr 29 05 12 19 26	'45 May 03 10 17 24	'45 Jun 01 08 15 22	'45 Jul 29 05 12 19 26	'45 Aug 03 10 17 24	'45 Sep 01 08 15 22	'45 Oct 29 05 12 19 26	'45 Nov 03 10 17 24	'45 Dec 01 08 15 22	'46 Jan 29 05 12 19 26	'46 Feb 03 10 17 24	'46 Mar 01 08 15 22	'46 Apr 29 05 12 19 26	'46 May 03 10 17 24	'46 Jun 01 08 15 22	'46 Jul 29 05 12 19 26	'46 Aug 03 10 17 24	'46 Sep 01 08 15 22	'46 Oct 29 05 12 19 26	'46 Nov 03 10 17 24	'46 Dec 01 08 15 22	'47 Jan 29 05 12 19 26	'47 Feb 03 10 17 24	'47 Mar 01 08 15 22	'47 Apr 29 05 12 19 26	'47 May 03 10 17 24	'47 Jun 01 08 15 22	'47 Jul 29 05 12 19 26	'47 Aug 03 10 17 24	'47 Sep 01 08 15 22	'47 Oct 29 05 12 19 26	'47 Nov 03 10 17 24	'47 Dec 01 08 15 22	'48 Jan 29 05 12 19 26	'48 Feb 03 10 17 24	'48 Mar 01 08 15 22	'48 Apr 29 05 12 19 26	'48 May 03 10 17 24	'48 Jun 01 08 15 22	'48 Jul 29 05 12 19 26	'48 Aug 03 10 17 24	'48 Sep 01 08 15 22	'48 Oct 29 05 12 19 26	'48 Nov 03 10 17 24	'48 Dec 01 08 15 22	'49 Jan 29 05 12 19 26	'49 Feb 03 10 17 24	'49 Mar 01 08 15 22	'49 Apr 29 05 12 19 26	'49 May 03 10 17 24	'49 Jun 01 08 15 22	'49 Jul 29 05 12 19 26	'49 Aug 03 10 17 24	'49 Sep 01 08 15 22	'49 Oct 29 05 12 19 26	'49 Nov 03 10 17 24	'49 Dec 01 08 15 22	'50 Jan 29 05 12 19 26	'50 Feb 03 10 17 24	'50 Mar 01 08 15 22	'50 Apr 29 05 12 19 26	'50 May 03 10 17 24	'50 Jun 01 08 15 22	'50 Jul 29 05 12 19 26	'50 Aug 03 10 17 24	'50 Sep 01 08 15 22	'50 Oct 29 05 12 19 26	'50 Nov 03 10 17 24	'50 Dec 01 08 15 22	'51 Jan 29 05 12 19 26	'51 Feb 03 10 17 24	'51 Mar 01 08 15 22	'51 Apr 29 05 12 19 26	'51 May 03 10 17 24	'51 Jun 01 08 15 22	'51 Jul 29 05 12 19 26	'51 Aug 03 10 17 24	'51 Sep 01 08 15 22	'51 Oct 29 05 12 19 26	'51 Nov 03 10 17 24	'51 Dec 01 08 15 22	'52 Jan 29 05 12 19 26	'52 Feb 03 10 17 24	'52 Mar 01 08 15 22	'52 Apr 29 05 12 19 26	'52 May 03 10 17 24	'52 Jun 01 08 15 22	'52 Jul 29 05 12 19 26	'52 Aug 03 10 17 24	'52 Sep 01 08 15 22	'52 Oct 29 05 12 19 26	'52 Nov 03 10 17 24	'52 Dec 01 08 15 22	'53 Jan 29 05 12 19 26	'53 Feb 03 10 17 24	'53 Mar 01 08 15 22	'53 Apr 29 05 12 19 26	'53 May 03 10 17 24	'53 Jun 01 08 15 22	'53 Jul 29 05 12 19 26	'53 Aug 03 10 17 24	'53 Sep 01 08 15 22	'53 Oct 29 05 12 19 26	'53 Nov 03 10 17 24	'53 Dec 01 08 15 22	'54 Jan 29 05 12 19 26	'54 Feb 03 10 17 24	'54 Mar 01 08 15 22	'54 Apr 29 05 12 19 26	'54 May 03 10 17 24	'54 Jun 01 08 15 22	'54 Jul 29 05 12 19 26	'54 Aug 03 10 17 24	'54 Sep 01 08 15 22	'54 Oct 29 05 12 19 26	'54 Nov 03 10 17 24	'54 Dec 01 08 15 22	'55 Jan 29 05 12 19 26	'55 Feb 03 10 17 24	'55 Mar 01 08 15 22	'55 Apr 29 05 12 19 26	'55 May 03 10 17 24	'55 Jun 01 08 15 22	'55 Jul 29 05 12 19 26	'55 Aug 03 10 17 24	'55 Sep 01 08 15 22	'55 Oct 29 05 12 19 26	'55 Nov 03 10 17 24	'55 Dec 01 08 15 22	'56 Jan 29 05 12 19 26	'56 Feb 03 10 17 24	'56 Mar 01 08 15 22	'56 Apr 29 05 12 19 26	'56 May 03 10 17 24	'56 Jun 01 08 15 22	'56 Jul 29 05 12 19 26	'56 Aug 03 10 17 24	'56 Sep 01 08 15 22	'56 Oct 29 05 12 19 26	'56 Nov 03 10 17 24	'56 Dec 01 08 15 22	'57 Jan 29 05 12 19 26	'57 Feb 03 10 17 24	'57 Mar 01 08 15 22	'57 Apr 29 05 12 19 26	'57 May 03 10 17 24	'57 Jun 01 08 15 22	'57 Jul 29 05 12 19 26	'57 Aug 03 10 17 24	'57 Sep 01 08 15 22	'57 Oct 29 05 12 19 26	'57 Nov 03 10 17 24	'57 Dec 01 08 15 22	'58 Jan 29 05 12 19 26	'58 Feb 03 10 17 24	'58 Mar 01 08 15 22	'58 Apr 29 05 12 19 26	'58 May 03 10 17 24	'58 Jun 01 08 15 22	'58 Jul 29 05 12 19 26	'58 Aug 03 10 17 24	'58 Sep 01 08 15 22	'58 Oct 29 05 12 19 26	'58 Nov 03 10 17 24	'58 Dec 01 08 15 22	'59 Jan 29 05 12 19 26	'59 Feb 03 10 17 24	'59 Mar 01 08 15 22	'59 Apr 29 05 12 19 26	'59 May 03 10 17 24	'59 Jun 01 08 15 22	'59 Jul 29 05 12 19 26	'59 Aug 03 10 17 24	'59 Sep 01 08 15 22	'59 Oct 29 05 12 19 26	'59 Nov 03 10 17 24	'59 Dec 01 08 15 22	'60 Jan 29 05 12 19 26	'60 Feb 03 10 17 24	'60 Mar 01 08 15 22	'60 Apr 29 05 12 19 26	'60 May 03 10 17 24	'60 Jun 01 08 15 22	'60 Jul 29 05 12 19 26	'60 Aug 03 10 17 24	'60 Sep 01 08 15 22	'60 Oct 29 05 12 19 26	'60 Nov 03 10 17 24	'60 Dec 01 08 15 22	'61 Jan 29 05 12 19 26	'61 Feb 03 10 17 24	'61 Mar 01 08 15 22	'61 Apr 29 05 12 19 26	'61 May 03 10 17 24	'61 Jun 01 08 15 22	'61 Jul 29 05 12 19 26	'61 Aug 03 10 17 24	'61 Sep 01 08 15 22	'61 Oct 29 05 12 19 26	'61 Nov 03 10 17 24	'61 Dec 01 08 15 22	'62 Jan 29 05 12 19 26	'62 Feb 03 10 17 24	'62 Mar 01 08 15 22	'62 Apr 29 05 12 19 26	'62 May 03 10 17 24	'62 Jun 01 08 15 22	'62 Jul 29 05 12 19 26	'62 Aug 03 10 17 24	'62 Sep 01 08 15 22	'62 Oct 29 05 12 19 26	'62 Nov 03 10 17 24	'62 Dec 01 08 15 22	'63 Jan 29 05 12 19 26	'63 Feb 03 10 17 24	'63 Mar 01 08 15 22	'63 Apr 29 05 12 19 26

ID	Task Name	Duration	Start	Finish	Resource Names	Predecessors														
							'23 Jun 28 04 11 18 25	'23 Jul 02 09 16 23	'23 Aug 30 06 13 20 27	'23 Sep 03 10 17 24	'23 Oct 01 08 15 22	'23 Nov 29 05 12 19 26	'23 Dec 03 10 17 24	'24 Jan 31 07 14 21 28	'24 Feb 04 11 18 25					
210	Lobby Slabs	314 days	Wed 22-09-14	Tue 23-12-19																
349	Level 36	7 days	Wed 23-10-18	Thu 23-10-26																
350	FRP Lobby Slab L36	5 days	Wed 23-10-18	Tue 23-10-24	Hardwall	348														
351	Pour Lobby Slab L36	1 day	Wed 23-10-25	Wed 23-10-25	Hardwall	350														
352	FRP Lobby Walls L36-37	1 day	Thu 23-10-26	Thu 23-10-26	Hardwall	351														
353	Pour Lobby Walls L36-37	1 day	Thu 23-10-26	Thu 23-10-26	Hardwall	352SS														
354	Level 37	11 days	Fri 23-10-27	Fri 23-11-10																
355	FRP Lobby Slab L37	3 days	Fri 23-10-27	Tue 23-10-31	Hardwall	353														
356	Pour Lobby Slab L37	1 day	Wed 23-11-01	Wed 23-11-01	Hardwall	355														
357	FRP Lobby Walls L37-38	6 days	Thu 23-11-02	Thu 23-11-09	Hardwall	356														
358	Pour Lobby Walls L37-38	1 day	Fri 23-11-10	Fri 23-11-10	Hardwall	357														
359	Level 38	9 days	Mon 23-11-13	Thu 23-11-23																
360	FRP Lobby Slab L38	3 days	Mon 23-11-13	Wed 23-11-15	Hardwall	358														
361	Pour Lobby Slab L38	1 day	Thu 23-11-16	Thu 23-11-16	Hardwall	360														
362	FRP Lobby Walls L38-39	4 days	Fri 23-11-17	Wed 23-11-22	Hardwall	361														
363	Pour Lobby Walls L38-39	1 day	Thu 23-11-23	Thu 23-11-23	Hardwall	362														
364	Level 39	9 days	Fri 23-11-24	Wed 23-12-06																
365	FRP Lobby Slab L39	3 days	Fri 23-11-24	Tue 23-11-28	Hardwall	363														
366	Pour Lobby Slab L39	1 day	Wed 23-11-29	Wed 23-11-29	Hardwall	365														
367	FRP Lobby Walls L39-40	4 days	Thu 23-11-30	Tue 23-12-05	Hardwall	366														
368	Pour Lobby Walls L39-40	1 day	Wed 23-12-06	Wed 23-12-06	Hardwall	367														
369	Level 40	9 days	Thu 23-12-07	Tue 23-12-19																
370	FRP Lobby Slab L40	3 days	Thu 23-12-07	Mon 23-12-11	Hardwall	368														
371	Pour Lobby Slab L40	1 day	Tue 23-12-12	Tue 23-12-12	Hardwall	370														
372	FRP Lobby Walls L40-41	4 days	Wed 23-12-13	Mon 23-12-18	Hardwall	371														
373	Pour Lobby Walls L40-41	1 day	Tue 23-12-19	Tue 23-12-19	Hardwall	372														
374	Corner Slabs and Struts	207 days	Wed 22-09-14	Tue 23-07-18																
406	FRP Corner Slab L35	6 days	Fri 23-10-20	Fri 23-10-27	Hardwall	405														
407	FRP Corner Slab L36	6 days	Mon 23-10-30	Mon 23-11-06	Hardwall	406														
408	FRP Corner Slab L37	6 days	Tue 23-11-07	Tue 23-11-14	Hardwall	407														
409	Envelope	318 days	Fri 22-11-04	Thu 24-02-15																
410	Podium/West Bank	318 days	Fri 22-11-04	Thu 24-02-15																
411	South Podium Deficiencies (Originally 25 working days) LATE	243 days	Fri 22-11-04	Tue 23-10-31	Gamma															
412	V-Wall Deficiencies South (LATE)	223 days	Mon 22-12-05	Tue 23-10-31	Gamma															
413	V-Wall Deficiencies North (LATE)	218 days	Mon 22-12-12	Tue 23-10-31	Gamma															
414	V-Wall Lobby East (LATE)	21 days	Fri 23-09-08	Fri 23-10-06	Gamma	416														
415	Install North West Core Link (Originally 15 Days)	190 days	Mon 23-01-30	Tue 23-10-31	Gamma															
416	Install V-Wall NE Return (Delay by Item 378)	54 days	Tue 23-08-15	Tue 23-10-31	Gamma															
417	Install South West Core Link (Originally 10 days)	16 days	Tue 23-10-10	Tue 23-10-31	Gamma	414														
418	Install V-Wall SE Return (Delay by Item 378)	26 days	Mon 23-09-25	Tue 23-10-31	Gamma															
419	Installation of West V Wall	26 days	Mon 23-09-25	Tue 23-10-31	Gamma															
420	Install North Canopy Steel (Delay by Item 378)	10 days	Wed 23-11-01	Tue 23-11-14	Walters	417														
421	Install North Canopy Closures	5 days	Wed 23-11-15	Tue 23-11-21	Gamma	420														

Project: The One - Look Ahead Date: Fri 23-10-20	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

Page 2

ID	Task Name	Duration	Start	Finish	Resource Names	Predecessors
422	Install North Canopy Cladding	25 days	Wed 23-12-06	Thu 24-01-11	Riverside	421FS+10 d
423	Install South Canopy Steel (Delay by Item 378)	10 days	Wed 23-11-15	Tue 23-11-28	Walters	420
424	Install South Canopy Closures	5 days	Wed 23-11-29	Tue 23-12-05	Gamma	423
425	Install South Canopy Cladding	25 days	Fri 24-01-12	Thu 24-02-15	Riverside	424,422
426	Granite Paver Misc. metals material on site	1 day	Mon 23-09-11	Mon 23-09-11	Cult	
427	Granite Paver Misc. metals installation	35 days	Tue 23-09-12	Tue 23-10-31	Cult	426
429	DC-21 SCO-4 & SCO-5	5 days	Wed 23-11-01	Tue 23-11-07	Gamma	419
431	Tower	265 days	Mon 22-11-14	Fri 23-12-08		
439	Cladding L3-L6 (Originally 25 Days) Incomplete	175 days	Tue 23-02-21	Tue 23-10-31	Gamma	
440	West Link Wall Blueskin, Framing, and Insulation	10 days	Mon 23-10-16	Fri 23-10-27	Riverside	
441	Acoustic insulation for steel framing (L3-L6)	20 days	Mon 23-10-30	Fri 23-11-24	Riverside	440
442	Cladding & Soffits Ground - L3 (Delay by Item 367, 369 & 429)	62 days	Tue 23-05-23	Fri 23-08-18	Riverside	
443	L7 Curtain Wall & Cladding (Originally 10 Days) LATE	70 days	Wed 23-07-19	Fri 23-10-27	Gamma	
444	L8 Curtain Wall & Cladding (Originally 10 Days) LATE	56 days	Wed 23-08-09	Fri 23-10-27	Gamma	
445	L9 Curtain Wall & Cladding (Originally 6 Days) LATE	37 days	Wed 23-09-06	Fri 23-10-27	Gamma	
446	L10 Curtain Wall & Cladding (Originally 6 Days) LATE	27 days	Wed 23-09-20	Fri 23-10-27	Gamma	
447	L11 Curtain Wall & Cladding (Originally 6 Days) LATE	18 days	Tue 23-10-03	Fri 23-10-27	Gamma	
448	L12 Curtain Wall & Cladding	6 days	Mon 23-10-30	Mon 23-11-06	Gamma	447,394
449	L13 Curtain Wall & Cladding	6 days	Tue 23-11-07	Tue 23-11-14	Gamma	448,395
450	L14 Curtain Wall & Cladding	6 days	Wed 23-11-15	Wed 23-11-22	Gamma	449,396
451	L15 Curtain Wall & Cladding	6 days	Thu 23-11-23	Thu 23-11-30	Gamma	450,397
452	L16 Curtain Wall & Cladding	6 days	Fri 23-12-01	Fri 23-12-08	Gamma	451,398
469	Yonge Street Building	364 days	Fri 22-08-12	Tue 24-01-30		
478	New Yonge Street Façade Brick and Backup Assemblies	40 days	Mon 23-10-30	Fri 23-12-22	Clifford	
480	YSF Window Trim Installation	1 day	Wed 23-12-27	Wed 23-12-27	Gamma	478
481	Correct Deficiencies YSF Punched Windows	10 days	Mon 23-08-14	Fri 23-08-25	Gamma	487SS
482	Remove Scaffolding at North	5 days	Mon 23-10-30	Fri 23-11-03	Clifford	
483	Excavate & Remove Piles	10 days	Mon 23-11-06	Fri 23-11-17		482
484	Hot Rubber Waterproofing	5 days	Mon 23-11-20	Fri 23-11-24	Bothwell	483
485	Pour Concrete Topper	5 days	Mon 23-11-27	Fri 23-12-01	Hardwall	484
486	Heritage & Yonge Street Storefront & Doors	25 days	Mon 23-12-04	Tue 24-01-09	Gamma	485
487	Install Heritage Windows (Late-Originally 5 days)	50 days	Mon 23-08-14	Tue 23-10-24	Gamma	
488	Yonge Street Cladding	15 days	Wed 24-01-10	Tue 24-01-30	Riverside	486
494	West Bank Wing Wall	208 days	Fri 23-03-31	Fri 24-01-26		
499	CMU Wall Installation (Phase-2)	40 days	Mon 23-11-06	Tue 24-01-02	Blockwall	
500	Sheet Metal Installation	5 days	Wed 24-01-03	Tue 24-01-09	Modern	499
501	Air Shaft Liner	5 days	Wed 24-01-03	Tue 24-01-09	Bothwell	499
502	Misc. Metals Air shaft/support	3 days	Wed 24-01-03	Fri 24-01-05	Cult	499
503	West Wing Wall Cladding	15 days	Mon 24-01-08	Fri 24-01-26	Riverside	502
504	Install Gutter & Roof	5 days	Mon 24-01-08	Fri 24-01-12	Bothwell/Modern	502
541	Mechanical Levels 17 & 18	197 days	Wed 23-04-26	Mon 24-02-05		
542	Mechanical Level 17	197 days	Wed 23-04-26	Mon 24-02-05		
552	HSS Framing	93 days	Tue 23-06-13	Wed 23-10-25	Walters	549

Project: The One - Look Ahead
Date: Fri 23-10-20

Task

Split

Milestone

Summary

Inactive Task

Inactive Summary

Inactive Milestone

Inactive Summary

Manual Task

Manual Summary Rollup

Manual Summary

Duration-only

Manual Summary

Start-only

External Tasks

External Milestone

Finish-only

External Milestone

Deadline

Manual Progress

Progress

Manual Progress

Down Arrow

Blue Line

Teal Line

Page 3


ID	Task Name	Duration	Start	Finish	Resource Names	Predecessors																																																
554	North Elevation HSS Rework	3 days	Wed 23-10-18	Fri 23-10-20	Walters																																																	
555	Drywall/Acoustic wall	57 days	Tue 23-08-08	Fri 23-10-27	United Drywall																																																	
556	M&E Rough In	91 days	Tue 23-06-20	Mon 23-10-30	Modern/Ozz																																																	
557	Blockwall (Phase-2)	10 days	Tue 23-10-31	Mon 23-11-13	Blockwall	556																																																
558	Acoustic Ceiling	5 days	Tue 23-10-31	Mon 23-11-06	United Drywall	556																																																
560	Removal of Interior Scaffold (North)	2 days	Thu 23-11-09	Fri 23-11-10		558FS+2 day																																																
561	L17-18 Louvre Framing and Backpan Installation	117 days	Mon 23-08-21	Mon 24-02-05		559																																																
564	West Elevation (Delayed Fabrication Issue)	8 days	Wed 23-10-25	Fri 23-11-03	Bass																																																	
565	North Elevation	12 days	Mon 23-11-13	Tue 23-11-28	Bass	560,554																																																
566	SW Corner	14 days	Tue 23-11-07	Fri 23-11-24	Bass	552																																																
567	NE Corner	29 days	Mon 23-11-27	Mon 24-01-08	Bass																																																	
568	NW Corner	15 days	Thu 23-12-28	Wed 24-01-17	Bass																																																	
569	SE Corner	13 days	Thu 24-01-11	Mon 24-01-29	Bass																																																	
570	South Elevation	20 days	Tue 24-01-09	Mon 24-02-05	Bass																																																	
571	Mechanical Equipment Hook ups	30 days	Tue 23-11-07	Mon 23-12-18	Modern	558																																																
572	Paint	2 days	Tue 23-12-19	Wed 23-12-20	Luis	571																																																
573	Testing (M&E)	5 days	Tue 23-12-19	Wed 23-12-27	Modern	571																																																
574	Commissioning (Mechanical + Controls)	21 days	Thu 23-12-28	Thu 24-01-25	Modern	573																																																
575	Mechanical Level 18	183 days	Wed 23-05-10	Tue 24-01-30																																																		
582	Blockwall	86 days	Tue 23-06-20	Mon 23-10-23	Blockwall	580																																																
583	Drywall/Acoustic wall	55 days	Tue 23-08-08	Wed 23-10-25	United Drywall																																																	
584	M&E Rough In	91 days	Fri 23-06-16	Thu 23-10-26	Modern/Ozz	581																																																
585	Acoustic Ceiling	10 days	Fri 23-10-27	Thu 23-11-09	United Drywall	584																																																
586	Testing (M&E)	5 days	Fri 23-11-10	Thu 23-11-16	Modern	585																																																
587	Mechanical Equipment Hook ups	30 days	Fri 23-11-17	Mon 24-01-01	Modern	586																																																
588	Paint	2 days	Tue 24-01-02	Wed 24-01-03	Luis	587																																																
589	Commissioning (Mechanical + Controls)	21 days	Tue 24-01-02	Tue 24-01-30	Modern	587																																																
590	Skybuild	118 days	Thu 23-06-15	Fri 23-12-01																																																		
595	Landscaping	71 days	Wed 23-08-30	Fri 23-12-08																																																		
604	Misc. Items	332 days	Fri 22-08-12	Wed 23-12-13																																																		
Project: The One - Look Ahead Date: Fri 23-10-20		Task		Project Summary		Manual Task		Start-only		Deadline																																												
		Split		Inactive Task		Duration-only		Finish-only		Progress																																												
		Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress																																												
		Summary		Inactive Summary		Manual Summary		External Milestone																																														
Page 4																																																						



MIZRAHI

DESIGN / BUILD

APPENDIX H

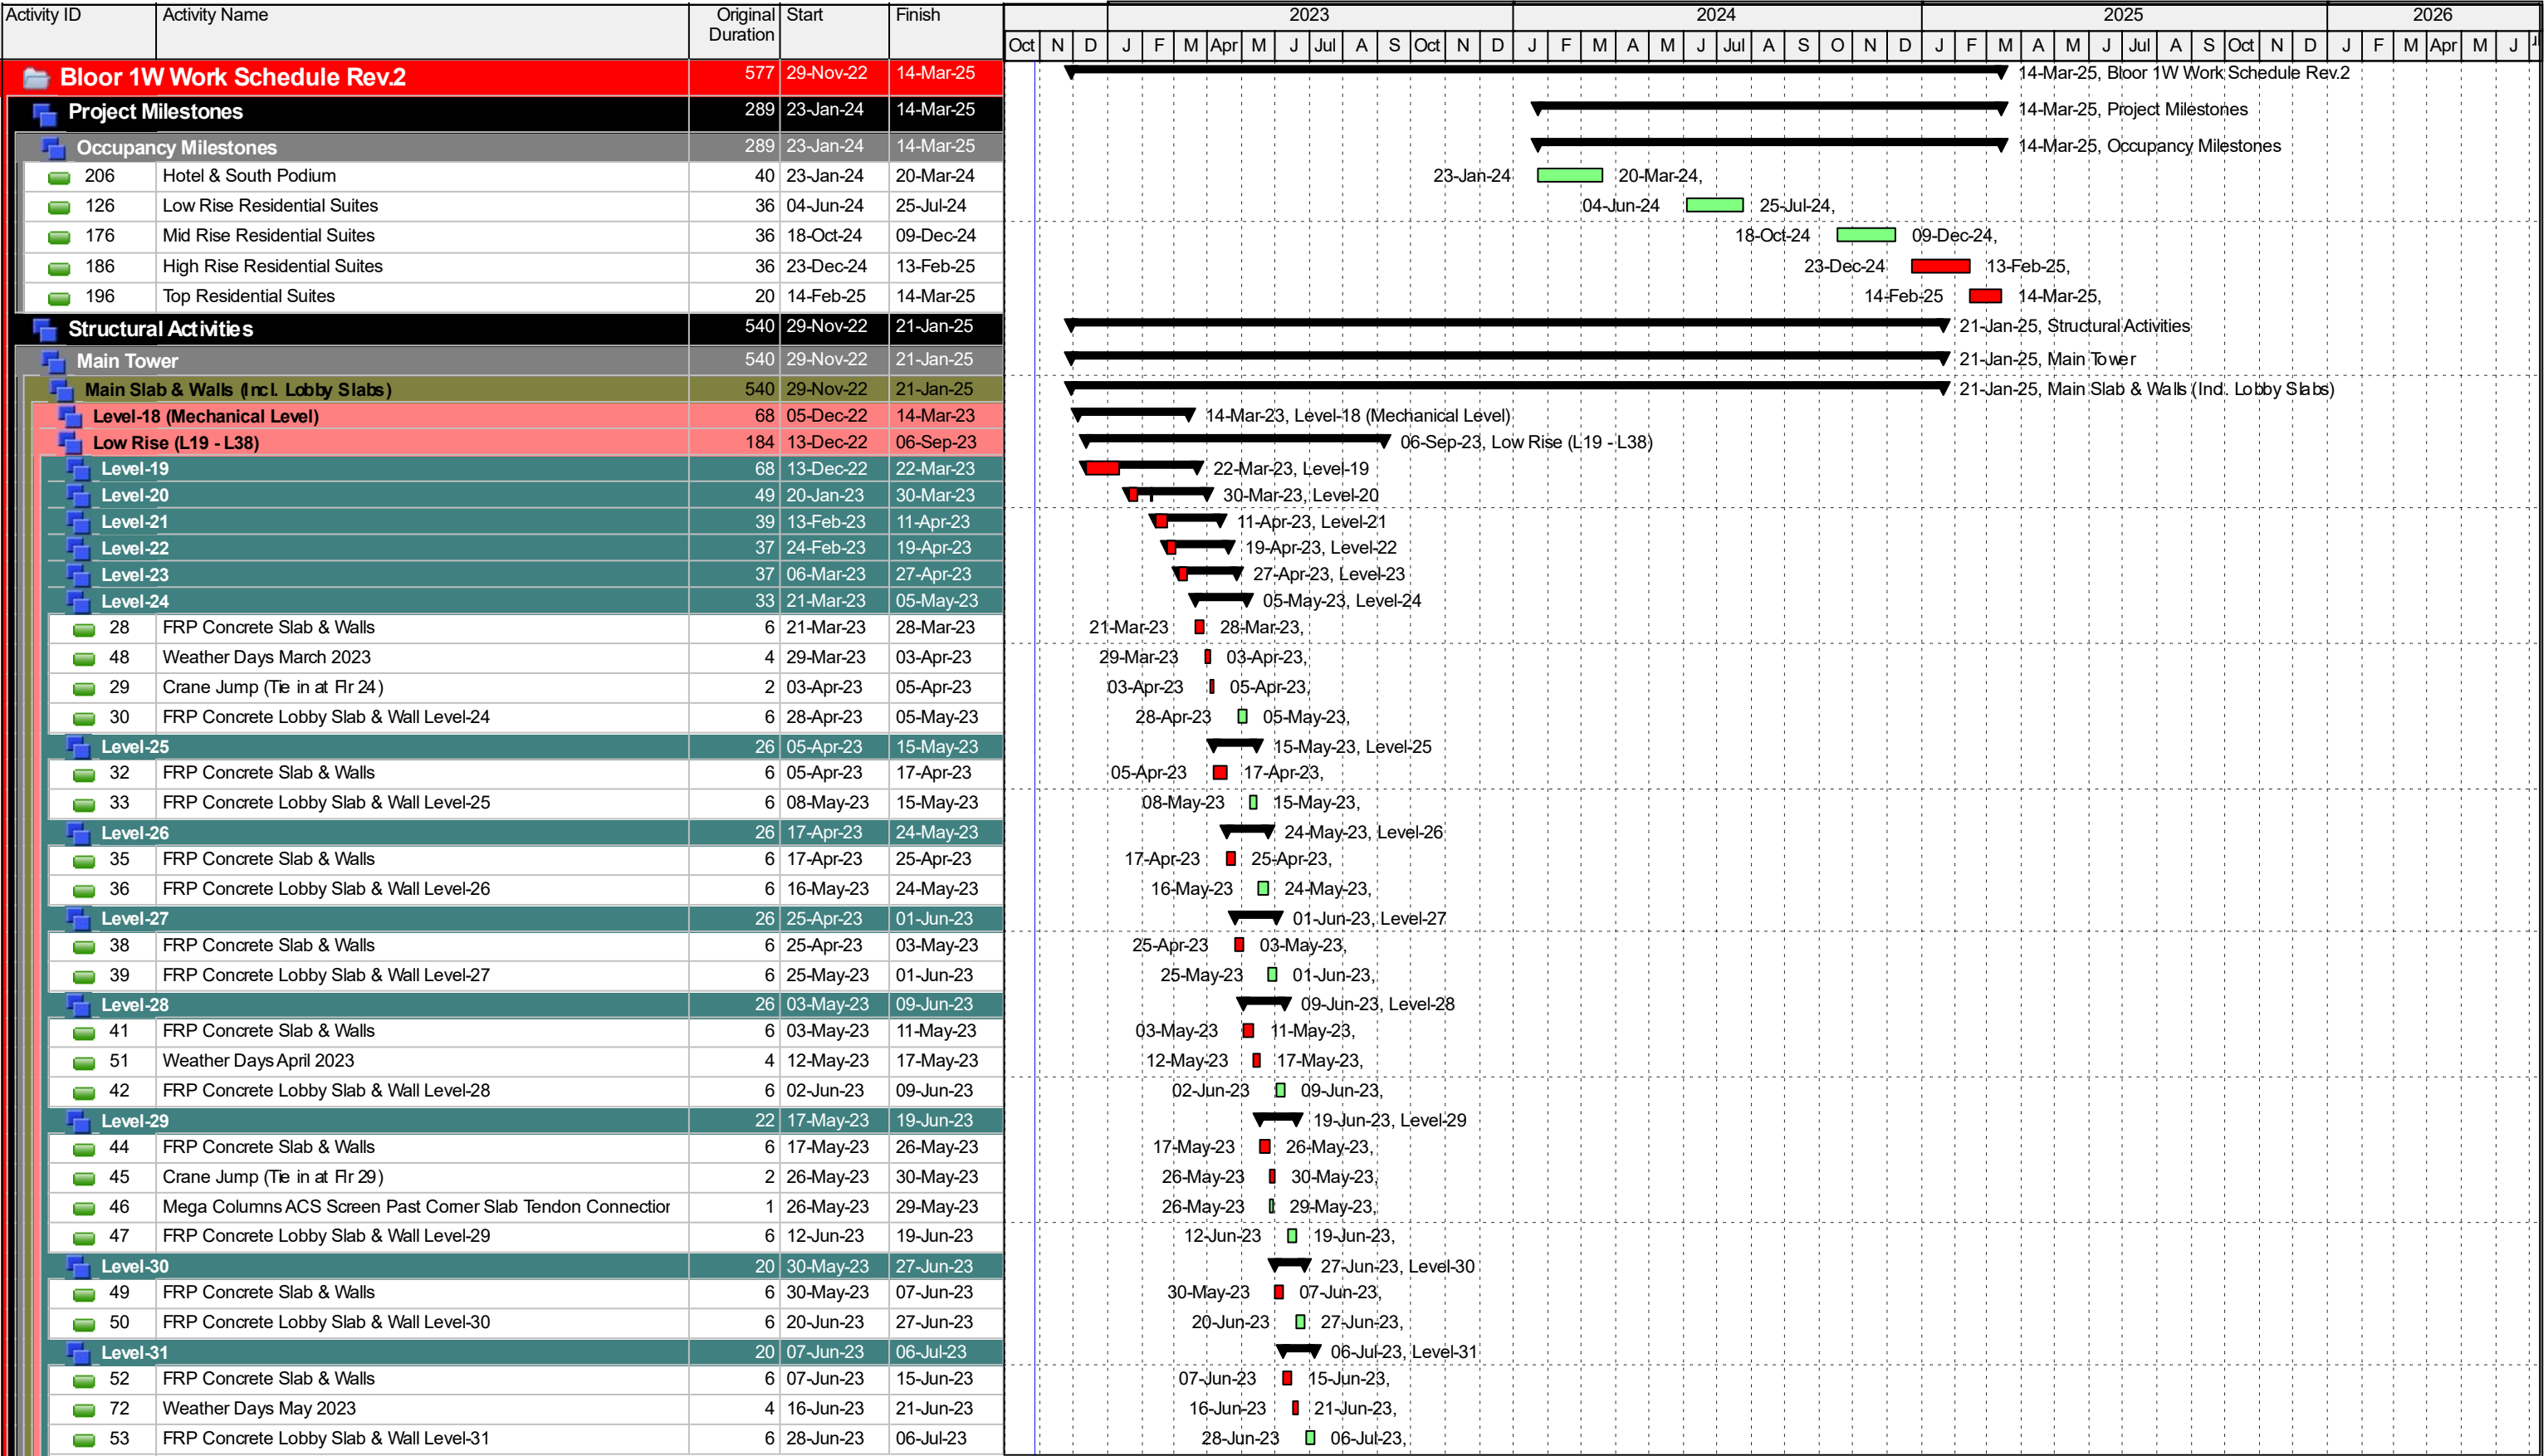

Date

Revision

Ch...

ONE BLOOR STREET WEST

Work Schedule

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Activity ID		Activity Name	Original Duration	Start	Finish	2023												2024												2025												2026																																	
						Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	J																								
		 Level-32	16	21-Jun-23	14-Jul-23	14-Jul-23, Level-32																																																																					
		 55 FRP Concrete Slab & Walls	6	21-Jun-23	29-Jun-23	21-Jun-23, 29-Jun-23,																																																																					
		 56 FRP Concrete Lobby Slab & Wall Level-32	6	07-Jul-23	14-Jul-23	07-Jul-23, 14-Jul-23,																																																																					
		 Level-33	16	29-Jun-23	24-Jul-23	24-Jul-23, Level-33																																																																					
		 58 FRP Concrete Slab & Walls	6	29-Jun-23	10-Jul-23	29-Jun-23, 10-Jul-23,																																																																					
		 59 FRP Concrete Lobby Slab & Wall Level-33	6	17-Jul-23	24-Jul-23	17-Jul-23, 24-Jul-23,																																																																					
		 Level-34	16	10-Jul-23	01-Aug-23	01-Aug-23, Level-34																																																																					
		 61 FRP Concrete Slab & Walls	6	10-Jul-23	18-Jul-23	10-Jul-23, 18-Jul-23,																																																																					
		 71 Weather Days June 2023	4	19-Jul-23	24-Jul-23	19-Jul-23, 24-Jul-23,																																																																					
		 62 FRP Concrete Lobby Slab & Wall Level-34	6	25-Jul-23	01-Aug-23	25-Jul-23, 01-Aug-23,																																																																					
		 Level-35	12	24-Jul-23	10-Aug-23	10-Aug-23, Level-35																																																																					
		 64 FRP Concrete Slab & Walls	6	24-Jul-23	01-Aug-23	24-Jul-23, 01-Aug-23,																																																																					
		 65 Crane Jump (Tie In at Flr35)	2	01-Aug-23	03-Aug-23	01-Aug-23, 03-Aug-23,																																																																					
		 66 Mega ColumnsACS Screen Past Comer Slab Tendon Connector	1	01-Aug-23	02-Aug-23	01-Aug-23, 02-Aug-23,																																																																					
		 67 FRP Concrete Lobby Slab & Wall Level-35	6	02-Aug-23	10-Aug-23	02-Aug-23, 10-Aug-23,																																																																					
		 Level-36	12	01-Aug-23	18-Aug-23	18-Aug-23, Level-36																																																																					
		 69 FRP Concrete Slab & Walls	6	01-Aug-23	10-Aug-23	01-Aug-23, 10-Aug-23,																																																																					
		 70 FRP Concrete Lobby Slab & Wall Level-36	6	11-Aug-23	18-Aug-23	11-Aug-23, 18-Aug-23,																																																																					
		 Level-37 & 38 (Mechanical Levels)	18	10-Aug-23	06-Sep-23	06-Sep-23, Level-37 & 38 (Mechanical Levels)																																																																					
		 Level-37	12	10-Aug-23	28-Aug-23	28-Aug-23, Level-37																																																																					
		 73 FRP Concrete Slab & Walls	6	10-Aug-23	18-Aug-23	10-Aug-23, 18-Aug-23,																																																																					
		 123 Weather Days July 2023	4	21-Aug-23	24-Aug-23	21-Aug-23, 24-Aug-23,																																																																					
		 74 FRP Concrete Lobby Slab & Wall Level-37	6	21-Aug-23	28-Aug-23	21-Aug-23, 28-Aug-23,																																																																					
		 Level-38	8	24-Aug-23	06-Sep-23	06-Sep-23, Level-38																																																																					
		 76 FRP Concrete Slab & Walls	6	24-Aug-23	01-Sep-23	24-Aug-23, 01-Sep-23,																																																																					
		 78 FRP Concrete Lobby Slab & Wall Level-38	6	29-Aug-23	06-Sep-23	29-Aug-23, 06-Sep-23,																																																																					
		 77 Crane Jump (Tie In at Flr38)	2	01-Sep-23	06-Sep-23	01-Sep-23, 06-Sep-23,																																																																					
		 Mid Rise (L39- L58)	121	06-Sep-23	29-Feb-24	29-Feb-24, Mid: Rise (L39- L58)																																																																					
		 Level-39	6	06-Sep-23	14-Sep-23	14-Sep-23, Level-39																																																																					
		 80 FRP Concrete Slab & Walls	4	06-Sep-23	12-Sep-23	06-Sep-23, 12-Sep-23,																																																																					
		 81 FRP Concrete Lobby Slab & Wall Level-39	6	07-Sep-23	14-Sep-23	07-Sep-23, 14-Sep-23,																																																																					
		 Level-40	8	12-Sep-23	22-Sep-23	22-Sep-23, Level-40																																																																					
		 83 FRP Concrete Slab & Walls	4	12-Sep-23	18-Sep-23	12-Sep-23, 18-Sep-23,																																																																					
		 84 FRP Concrete Lobby Slab & Wall Level-40	6	15-Sep-23	22-Sep-23	15-Sep-23, 22-Sep-23,																																																																					
		 133 Weather DaysAugust 2023	4	19-Sep-23	22-Sep-23	19-Sep-23, 22-Sep-23,																																																																					
		 Level-41	6	22-Sep-23	02-Oct-23	02-Oct-23, Level-41																																																																					
		 86 FRP Concrete Slab & Walls	4	22-Sep-23	28-Sep-23	22-Sep-23, 28-Sep-23,																																																																					
		 87 FRP Concrete Lobby Slab & Wall Level-41	6	25-Sep-23	02-Oct-23	25-Sep-23, 02-Oct-23,																																																																					
		 Level-42	8	28-Sep-23	11-Oct-23	11-Oct-23, Level-42																																																																					
		 89 FRP Concrete Slab & Walls	4	28-Sep-23	04-Oct-23	28-Sep-23, 04-Oct-23,																																																																					
		 90 FRP Concrete Lobby Slab & Wall Level-42	6	03-Oct-23	11-Oct-23	03-Oct-23, 11-Oct-23,																																																																					
		 Level-43	10	04-Oct-23	19-Oct-23	19-Oct-23, Level-43																																																																					
		 92 FRP Concrete Slab & Walls	4	04-Oct-23	11-Oct-23	04-Oct-23, 11-Oct-23,																																																																					
		 93 Mega ColumnsACS Screen Past Comer Slab Tendon Connector	1	11-Oct-23	12-Oct-23	11-Oct-23, 12-Oct-23,																																																																					
		 94 FRP Concrete Lobby Slab & Wall Level-43	6	12-Oct-23	19-Oct-23	12-Oct-23, 19-Oct-23,																																																																					
		 Level-44	12	11-Oct-23	27-Oct-23	27-Oct-23, Level-44																																																																					
		 96 FRP Concrete Slab & Walls	4	11-Oct-23	17-Oct-23	11-Oct-23, 17-Oct-23,																																																																					
		 97 FRP Concrete Lobby Slab & Wall Level-44	6	20-Oct-23	27-Oct-23	20-Oct-23, 27-Oct-23,																																																																					
		 Level-45	14	17-Oct-23	06-Nov-23	06-Nov-23, Level-45																																																																					
Date	Revision		Ch...	ONE BLOOR STREET WEST Work Schedule																																																Remaining Level of Effort Actual Level of Effort Actual Work												Remaining Work Critical Remaining Work Milestone											

Activity ID	Activity Name	Original Duration	Start	Finish	2023							2024							2025							2026																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										
					Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			
Level-45	99	FRP Concrete Slab & Walls	4	17-Oct-23	23-Oct-23												17-Oct-23		23-Oct-23,																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	</

Date

Revision

Ch...

ONE BLOOR STREET WEST

Work Schedule

Remaining Level of Effort

Actual Level of Effort

Actual Work


Remaining Work

Critical Remaining Work

Milestone

Activity ID		Activity Name	Original Duration	Start	Finish	2023														2024														2025														2026													
						Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	J										
		Level-58	28	19-Jan-24	29-Feb-24	19-Jan-24 25-Jan-24 26-Jan-24 31-Jan-24 22-Feb-24 29-Feb-24 29-Feb-24, Level-58																																																							
		146 FRP Concrete Slab & Walls	4	19-Jan-24	25-Jan-24	19-Jan-24 25-Jan-24																																																							
		266 Weather Days December 2023	4	26-Jan-24	31-Jan-24	26-Jan-24 31-Jan-24																																																							
		147 FRP Concrete Lobby Slab & Wall Level-58	6	22-Feb-24	29-Feb-24	22-Feb-24 29-Feb-24																																																							
		High Rise (L59- L78)	142	31-Jan-24	22-Aug-24	31-Jan-24 22-Aug-24, High Rise (L59- L78)																																																							
		Level-59	26	31-Jan-24	08-Mar-24	31-Jan-24 08-Mar-24, Level-59																																																							
		149 FRP Concrete Slab & Walls	4	31-Jan-24	06-Feb-24	31-Jan-24 06-Feb-24																																																							
		150 Crane Jump (Tie In at Flr 59)	2	06-Feb-24	08-Feb-24	06-Feb-24 08-Feb-24																																																							
		151 FRP Concrete Lobby Slab & Wall Level-59	6	01-Mar-24	08-Mar-24	01-Mar-24 08-Mar-24																																																							
		Level-60	28	06-Feb-24	18-Mar-24	06-Feb-24 18-Mar-24, Level-60																																																							
		153 FRP Concrete Slab & Walls	4	06-Feb-24	12-Feb-24	06-Feb-24 12-Feb-24																																																							
		154 FRP Concrete Lobby Slab & Wall Level-60	6	11-Mar-24	18-Mar-24	11-Mar-24 18-Mar-24																																																							
		Level-61	30	12-Feb-24	26-Mar-24	12-Feb-24 26-Mar-24, Level-61																																																							
		156 FRP Concrete Slab & Walls	4	12-Feb-24	16-Feb-24	12-Feb-24 16-Feb-24																																																							
		157 FRP Concrete Lobby Slab & Wall Level-61	6	19-Mar-24	26-Mar-24	19-Mar-24 26-Mar-24																																																							
		Level-62	33	16-Feb-24	05-Apr-24	16-Feb-24 05-Apr-24, Level-62																																																							
		160 FRP Concrete Slab & Walls	4	16-Feb-24	23-Feb-24	16-Feb-24 23-Feb-24																																																							
		170 Weather Days January 2024	4	26-Feb-24	29-Feb-24	26-Feb-24 29-Feb-24																																																							
		161 FRP Concrete Lobby Slab & Wall Level-62	6	27-Mar-24	05-Apr-24	27-Mar-24 05-Apr-24																																																							
		Level-63	30	29-Feb-24	15-Apr-24	29-Feb-24 15-Apr-24, Level-63																																																							
		163 FRP Concrete Slab & Walls	4	29-Feb-24	06-Mar-24	29-Feb-24 06-Mar-24																																																							
		164 Crane Jump (Tie In at Flr 63)	2	06-Mar-24	08-Mar-24	06-Mar-24 08-Mar-24																																																							
		165 Mega Columns ACS Screen Past Corner Slab Tendon Connector	1	06-Mar-24	07-Mar-24	06-Mar-24 07-Mar-24																																																							
		166 FRP Concrete Lobby Slab & Wall Level-63	6	08-Apr-24	15-Apr-24	08-Apr-24 15-Apr-24																																																							
		Level-64	30	08-Mar-24	23-Apr-24	08-Mar-24 23-Apr-24, Level-64																																																							
		168 FRP Concrete Slab & Walls	4	08-Mar-24	14-Mar-24	08-Mar-24 14-Mar-24																																																							
		169 FRP Concrete Lobby Slab & Wall Level-64	6	16-Apr-24	23-Apr-24	16-Apr-24 23-Apr-24																																																							
		Level-65	32	14-Mar-24	01-May-24	14-Mar-24 01-May-24, Level-65																																																							
		171 FRP Concrete Slab & Walls	4	14-Mar-24	20-Mar-24	14-Mar-24 20-Mar-24																																																							
		172 FRP Concrete Lobby Slab & Wall Level-65	6	24-Apr-24	01-May-24	24-Apr-24 01-May-24																																																							
		Level-66	34	20-Mar-24	09-May-24	20-Mar-24 09-May-24, Level-66																																																							
		174 FRP Concrete Slab & Walls	4	20-Mar-24	26-Mar-24	20-Mar-24 26-Mar-24																																																							
		175 FRP Concrete Lobby Slab & Wall Level-66	6	02-May-24	09-May-24	02-May-24 09-May-24																																																							
		Level-67	37	26-Mar-24	17-May-24	26-Mar-24 17-May-24, Level-67																																																							
		177 FRP Concrete Slab & Walls	4	26-Mar-24	03-Apr-24	26-Mar-24 03-Apr-24																																																							
		217 Weather Days February 2024	4	04-Apr-24	09-Apr-24	04-Apr-24 09-Apr-24																																																							
		178 FRP Concrete Lobby Slab & Wall Level-67	6	10-May-24	17-May-24	10-May-24 17-May-24																																																							
		Level-68	34	09-Apr-24	28-May-24	09-Apr-24 28-May-24, Level-68																																																							
		180 FRP Concrete Slab & Walls	4	09-Apr-24	15-Apr-24	09-Apr-24 15-Apr-24																																																							
		181 FRP Concrete Lobby Slab & Wall Level-68	6	21-May-24	28-May-24	21-May-24 28-May-24																																																							
		Level-69	36	15-Apr-24	05-Jun-24	15-Apr-24 05-Jun-24, Level-69																																																							
		183 FRP Concrete Slab & Walls	4	15-Apr-24	19-Apr-24	15-Apr-24 19-Apr-24																																																							
		184 Mega Columns ACS Screen Past Corner Slab Tendon Connector	1	19-Apr-24	22-Apr-24	19-Apr-24 22-Apr-24																																																							
		185 FRP Concrete Lobby Slab & Wall Level-69	6	29-May-24	05-Jun-24	29-May-24 05-Jun-24																																																							
		Level-70	38	19-Apr-24	13-Jun-24	19-Apr-24 13-Jun-24, Level-70																																																							
		187 FRP Concrete Slab & Walls	4	19-Apr-24	25-Apr-24	19-Apr-24 25-Apr-24																																																							
		188 Crane Jump (Tie In at Flr 70)	2	25-Apr-24	29-Apr-24	25-Apr-24 29-Apr-24																																																							
		189 FRP Concrete Lobby Slab & Wall Level-70	6	06-Jun-24	13-Jun-24	06-Jun-24 13-Jun-24																																																							
		Level-71	38	29-Apr-24	21-Jun-24	29-Apr-24 21-Jun-24, Level-71																																																							
Date	Revision		Ch...	ONE BLOOR STREET WEST																																																									
				Work Schedule																																																									

[illegible]

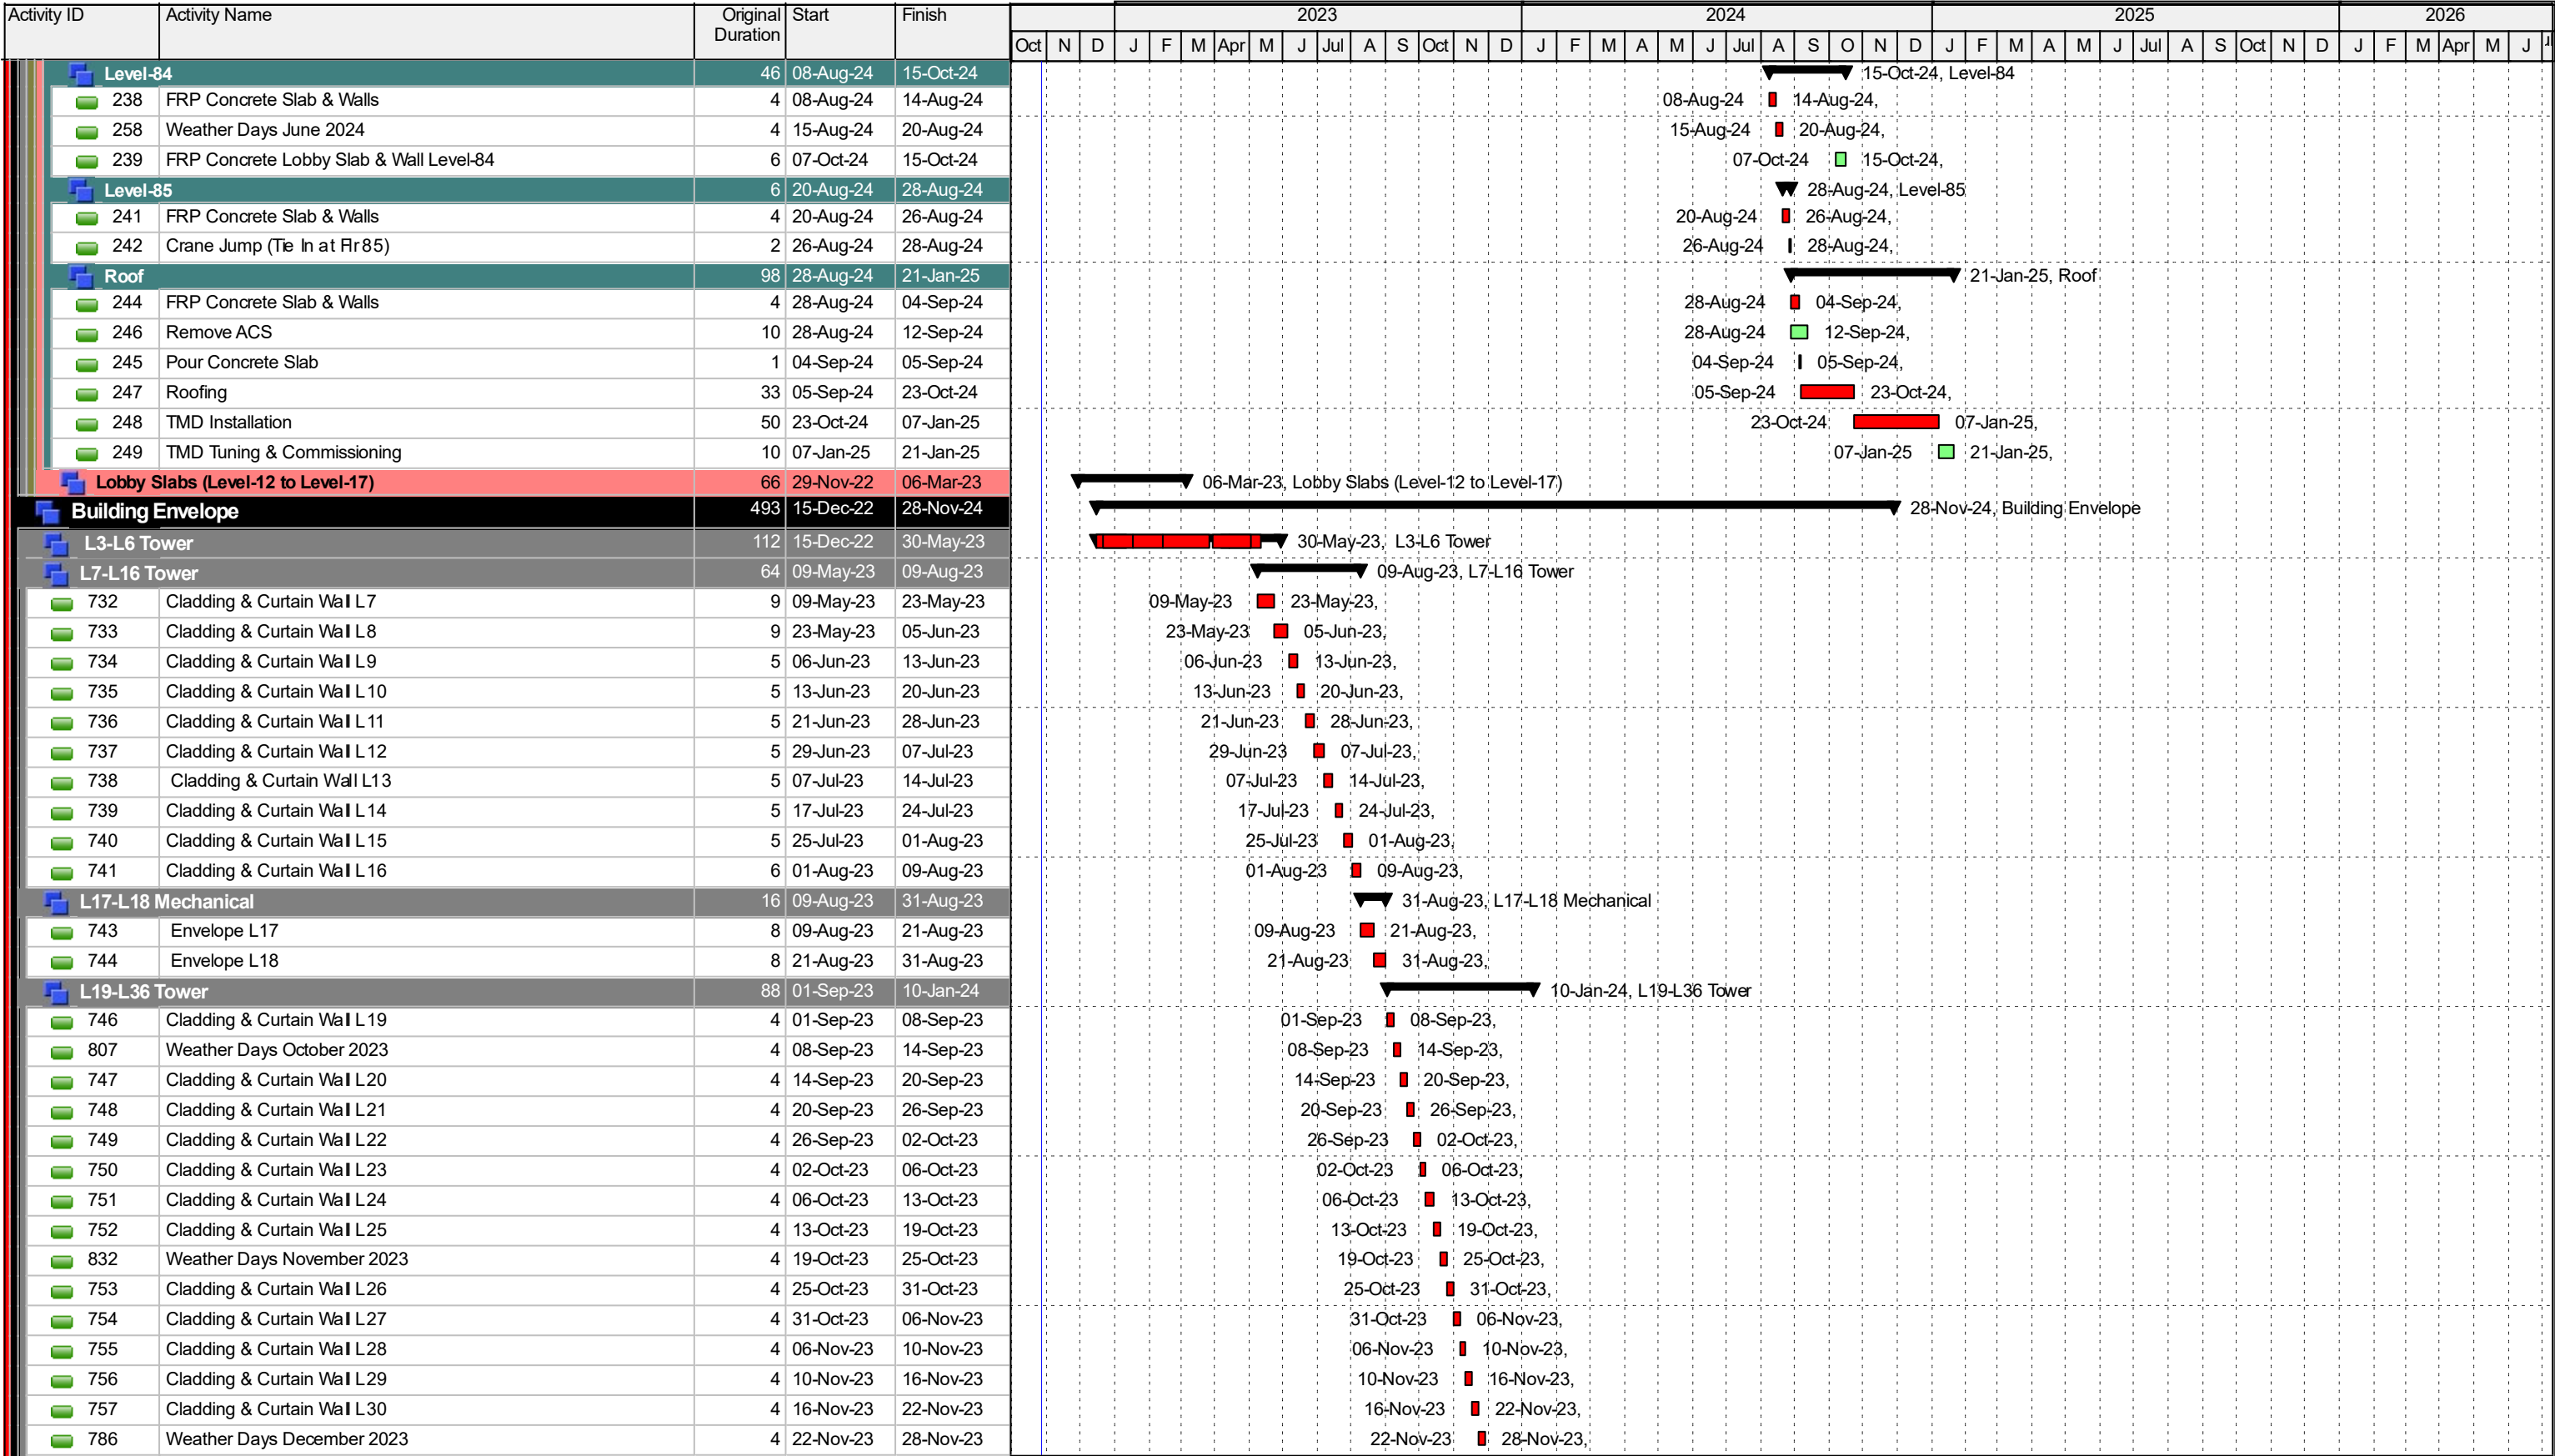

Date

Revision

Ch...

ONE BLOOR STREET WEST

Work Schedule

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Activity ID	Activity Name	Original Duration	Start	Finish	2023							2024							2025							2026																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																
					Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N

Activity ID	Activity Name	Original Duration	Start	Finish				2023												2024												2025												2026																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
					Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jun																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
799	Cladding & Curtain Wall L68	4	26-Jul-24	31-Jul-24																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			

Date

Revision

Ch...

ONE BLOOR STREET WEST

Work Schedule

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Activity ID	Activity Name	Original Duration	Start	Finish	2023							2024							2025							2026																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
					Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	J																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													
992	Finish paint	5	07-Sep-23	14-Sep-23										07-Sep-23		14-Sep-23,																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															</

Date

Revision

Ch...

ONE BLOOR STREET WEST

Work Schedule

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Activity ID	Activity Name	Original Duration	Start	Finish	2023							2024							2025							2026																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			
					Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												
1039	Turnover	1	20-Oct-23	23-Oct-23											20-Oct-23		23-Oct-23,																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												

Date

Revision

Ch...

ONE BLOOR STREET WEST
Work Schedule

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Activity ID	Activity Name	Original Duration	Start	Finish	2023														2024														2025														2026																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
					Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M

Date

Revision

Ch...

ONE BLOOR STREET WEST

Work Schedule

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Activity ID	Activity Name	Original Duration	Start	Finish								2023							2024							2025							2026																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										
					Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										
MECHANICAL	1180	Tape & Jointing	5	28-Sep-23	05-Oct-23												28-Sep-23	05-Oct-23																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									</

Date

Revision

Ch...

ONE BLOOR STREET WEST
Work Schedule

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Activity ID	Activity Name	Original Duration	Start	Finish								2023							2024							2025							2026																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
					Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
1213-1222	1213	Install kitchen & vanities (Measure for counter tops) + Install lights	5	02-Dec-23	08-Dec-23												02-Dec-23		08-Dec-23,																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				</

Date

Revision

Ch...

ONE BLOOR STREET WEST
Work Schedule

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

[illegible]

Activity ID	Activity Name	Original Duration	Start	Finish								2023							2024							2025							2026																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
					Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
Level-26	1354	Install counter tops / backsplashes (measure mirrors)	5	19-Jan-24	25-Jan-24														19-Jan-24			25-Jan-24,																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																

Date

Revision

Ch...

ONE BLOOR STREET WEST

Work Schedule

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Activity ID	Activity Name	Original Duration	Start	Finish								2023							2024							2025							2026																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
					Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
Level-28	1401 Plumbing / Mechanical fixtures	5	08-Feb-24	14-Feb-24														08-Feb-24		14-Feb-24,																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		

Date

Revision

Ch...

ONE BLOOR STREET WEST

Work Schedule

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Activity ID	Activity Name	Original Duration	Start	Finish	2023														2024														2025														2026																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													
					Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
	1495	5	11-Mar-24	16-Mar-24																11-Mar-24		16-Mar-24,																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
	1496	5	16-Mar-24	22-Mar-24																16-Mar-24		22-Mar-24,																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
	1497	5	22-Mar-24	28-Mar-24																22-Mar-24		28-Mar-24,																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
	1498	1	28-Mar-24	30-Mar-24																28-Mar-24		30-Mar-24,																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
	Level-32	96	08-Dec-23	04-Apr-24																04-Apr-24, Level-32																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								

Date

Revision

Ch...

ONE BLOOR STREET WEST

Work Schedule

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

[illegible]

[illegible]

[illegible]

[illegible]

[illegible]

[illegible]

[illegible]

[illegible]

Activity ID	Activity Name	Original Duration	Start	Finish				2023												2024												2025												2026																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																
					Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	J																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										
Level-54	1951	Install interior door & frames & trims. Install top head trim	5	03-Jun-24	08-Jun-24																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							</

Date

Revision

Ch...

ONE BLOOR STREET WEST

Work Schedule

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

[illegible]

Activity ID	Activity Name	Original Duration	Start	Finish				2023												2024												2025												2026																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															
					Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										
High Rise Floors (L59- L78)	3015	Frame & Board Acoustical Drywall Ceiling	15	26-Jul-24	13-Aug-24																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						

Date

Revision

Ch...

ONE BLOOR STREET WEST

Work Schedule

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

[illegible]

Activity ID	Activity Name	Original Duration	Start	Finish				2023												2024												2025												2026																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
					Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																
Level-63	2125	Appliances / Dry wall check out	3	05-Sep-24	09-Sep-24																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												

Date

Revision

Ch...

ONE BLOOR STREET WEST

Work Schedule

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

[illegible]

Activity ID	Activity Name	Original Duration	Start	Finish				2023												2024												2025												2026																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										
					Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
	2219	Mill work finishes, HVAC (sprinkler finishes), MCC handyman	5	07-Oct-24	12-Oct-24																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	</

Date

Revision

Ch...

ONE BLOOR STREET WEST

Work Schedule

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

[illegible]

[illegible]

[illegible]

Date	Revision	Ch...

ONE BLOOR STREET WEST

Work Schedule

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

CONFIDENTIAL APPENDIX “33”
REPORT BY KDC DATED DECEMBER 31, 2023

CONFIDENTIAL APPENDIX OMITTED

CONFIDENTIAL APPENDIX “34”
MEMO TO FILE - MI CM ISSUES DATED JANUARY 2, 2024

CONFIDENTIAL APPENDIX OMITTED
